



Project Planning & Prototyping

J. F. N. Salik,

247-519-VA

**Department of Computer
Engineering Technology**
Vanier College
821 Sainte-Croix Avenue
Saint-Laurent, Québec H4L 3X9

This document was last modified on
Saturday 30th May, 2026 at 5:44pm.

<i>Title</i>	Project Planning & Prototyping
<i>Date</i>	May 30, 2026
<i>Author</i>	J. F. N. Salik, (salikj@vaniercollege.qc.ca)
<i>Identification</i>	247-519-VA
<i>Template</i>	Sparkle Version 1.1 for L ^A T _E X 2 _ε



©2026. All rights reserved by J. F. N. Salik,.

This document may not be cited, reproduced, or distributed without explicit
written permission from the author.

Contents

1 Overview: Prototypes, Products & the Business of Engineering	1
1.1 What You Will Build	1
1.2 The Course Map: Two Tracks Over Twelve Weeks	2
1.3 From Prototype to Product: The Gap	3
1.4 Working with Engineers: What You Own	4
1.5 Engineering Businesses by Size	5
1.6 Science for Profit: Cost, Time, and Volume	6
1.7 How a Prototype Becomes Revenue	6
Review Questions	10
Portfolio Entry	10
2 Product Development & the Stage-Gate Model	13
2.1 The Product Development Lifecycle	13
2.2 The Cooper Stage-Gate Model	14
2.2.1 The Five Stages	14
2.2.2 The Gate Decisions	15
2.2.3 Where This Course and Project II Sit	16
2.3 What a Gate Decision Requires	16
2.4 Kano Analysis	17
2.4.1 The Five Kano Categories	17
2.5 Kano Satisfaction and Dissatisfaction Coefficients	19
2.5.1 Satisfaction Coefficient	19
2.5.2 Dissatisfaction Coefficient	19
2.5.3 Interpreting the Coefficients	19
2.6 From Kano to Prototype Scope	20
2.7 Worked Example: IoT Robotic Sorting Subsystem	21
2.7.1 Step 1 — Sort Accuracy ($\geq 95\%$)	22
2.7.2 Step 2 — MQTT Cloud Connectivity	22
2.7.3 Step 3 — Conveyor Belt Mechanism	22
2.7.4 Step 4 — 3D-Printed Housing	23
2.7.5 Step 5 — AI-Assisted Fault Detection	23
2.7.6 Summary Table and CS/ DS Plot	23
2.7.7 Derived Prototype Scope	24
Portfolio Entry	25
Chapter Summary	26
3 The Prototyping Mindset & the Workflow	27
3.1 Prototype = Answer to a Question, Reducer of Risk	28
3.2 The Seven Stages	29
3.2.1 Stage 1: Specification & Risk	29
3.2.2 Stage 2: Scoping & Planning	30
3.2.3 Stage 3: Architecture	30

3.2.4	Stage 4: Subsystem Design	31
3.2.5	Stage 5: Build & Integration	31
3.2.6	Stage 6: Validate & Measure	31
3.2.7	Stage 7: Compile & Economics	32
3.3	The Controlled Iteration Loop (Design ↔ Validate)	32
3.4	Prototype Types	33
3.5	Fidelity Matched to the Question	34
3.5.1	The Effort–Fidelity Model	34
3.5.2	Running Example: Choosing Fidelity for the Sorter	35
3.6	The Documentation Layer	36
	Review Questions	36
	Portfolio Entry	38
	Chapter Summary	38
4	Specifications & Risk Prioritization	41
4.1	Anatomy of a Specification	41
4.1.1	Functional Requirements	41
4.1.2	Performance Targets	42
4.1.3	Constraints	42
4.1.4	Interfaces	42
4.1.5	Acceptance Criteria	42
4.2	Requirements vs. Design	43
4.2.1	The “What / How” Discipline	43
4.3	Risk-Driven Prioritization	44
4.3.1	The Basic Risk Equation	44
4.3.2	Limitations of the Two-Factor Model	44
4.4	FMEA-Style Ranking (RPN)	45
4.4.1	The RPN Formula	45
4.4.2	Scale Anchors	46
4.5	The Critical Path of Unknowns	46
4.5.1	Identifying the Critical Unknown	46
4.6	Worked Example: IoT Robotic Sorting Subsystem	47
4.6.1	Step 1: Convert Vague Wishes into Measurable Requirements	47
4.6.2	Step 2: Compute RPN for Three Subsystems	48
4.6.3	Step 3: Rank and Interpret	49
4.6.4	Try It Yourself	50
	Review Questions	51
	Portfolio Entry	52
	Summary	52
5	System Architecture & Interface Definition	53
5.1	Decomposition	53
5.1.1	The Four Domains	54
5.1.2	Drawing the Block Diagram	55
5.2	Interfaces as Contracts	56
5.2.1	Electrical Interfaces	56
5.2.2	Mechanical Interfaces	56
5.2.3	Data Interfaces	57
5.2.4	Timing Interfaces	57
5.2.5	The Interface Table	58
5.3	Budget Allocation	58
5.3.1	Timing Budget	58

5.3.2	Power Budget	59
5.3.3	Error Budget	59
5.3.4	Worked Example — Part A: Timing Budget	60
5.3.5	Worked Example — Part B: RSS Error Budget	60
5.4	Why Integration Fails at Boundaries	61
5.4.1	Taxonomy of Boundary Failures	62
5.4.2	Identifying the Highest-Risk Boundary	63
	Portfolio Entry	65
6	Component Selection & Datasheet Literacy	67
6.1	Reading a Datasheet	67
6.1.1	Zone 1 — Absolute Maximum Ratings	68
6.1.2	Zone 2 — Recommended Operating Conditions	68
6.1.3	Zone 3 — Electrical Characteristics	69
6.1.4	Zone 4 — Timing Diagrams	69
6.1.5	Application Circuits and Packaging	69
6.2	Derating	69
6.3	Operating Margin	71
6.4	Component Lifecycle Status	71
6.5	Second-Sourcing Strategy	73
6.6	Supply Chain Risk	73
6.7	MTBF and Reliability Basics	74
6.7.1	Failure Rate and FIT	74
6.7.2	Series System Reliability	74
6.7.3	Parallel Redundancy	75
6.8	Worked Example	75
6.8.1	Part A — Derating and Operating Margin for an MCU	75
6.8.2	Part B — System MTBF for the Actuator Interface Path	76
6.9	Try It Yourself	77
6.10	Review Questions	77
	Portfolio Entry	78
6.11	Summary	79
7	Design for X	81
7.1	What DFX Means	81
7.2	Design for Manufacturability	82
7.2.1	PCB DFM	82
7.2.2	3D-Print DFM	82
7.3	Design for Assembly	83
7.3.1	The Boothroyd–Dewhurst Criterion	83
7.3.2	Assembly Efficiency	83
7.4	Design for Test	84
7.4.1	Test Points	84
7.4.2	Debug Ports and BIST	84
7.4.3	Defect Coverage	85
7.5	Design for Reliability	85
7.5.1	Derating and FMEA Margin	85
7.5.2	Redundancy	85
7.5.3	Thermal Management	86
7.6	DFX Trade-offs in Practice	86
7.7	Worked Example	87
	Portfolio Entry	89

Chapter Summary	89
8 AI in Prototyping: Capability & Risk	91
8.1 Where AI Helps	91
8.1.1 Code and Firmware Scaffolding	92
8.1.2 Component Value Suggestion	92
8.1.3 Design Alternatives and Documentation Drafts	92
8.2 Accelerator, Not Autonomous Designer	93
8.3 Hallucination in an Engineering Context	93
8.3.1 The Human-in-the-Loop Verification Cycle	93
8.4 The Black-Box Problem: Deciding When to Verify	94
8.4.1 Expected Cost of Error	95
8.4.2 Worked Example: I ² C Pull-Up Resistor	95
8.5 IP and Data-Leakage Risk	97
8.5.1 What Happens to Your Data	97
8.5.2 What Constitutes Proprietary Data	97
8.5.3 The Data-Handling Policy	98
8.6 Reproducibility and Traceability	98
8.6.1 The AI Use Log	98
8.6.2 Reproducibility Requirement	99
Try It Yourself	99
Review Questions	100
Portfolio Entry	101
Chapter Summary	102
9 IoT, Robotics & Safety as a Design Obligation	103
9.1 IoT Security by Design	103
9.2 Attack Surfaces	104
9.2.1 Connectivity Layer	105
9.2.2 Communication Layer	105
9.2.3 Management Layer	105
9.3 Privacy and Data Obligations	106
9.4 Protocol Selection	106
9.4.1 MQTT	106
9.4.2 CoAP	107
9.4.3 BLE	107
9.5 Power and Battery Budgeting	107
9.5.1 Average Current	108
9.5.2 Battery Life	108
9.5.3 Worked Example — Power Budget	108
9.6 Robotics Physical Safety	109
9.6.1 Emergency Stop	110
9.6.2 Guarding	110
9.6.3 Fail-Safe State	111
9.6.4 Force, Speed Limits, and Human-Robot Interaction Zones	111
9.7 Mechanical Safety Factor	111
9.7.1 Worked Example — Safety Factor	112
9.8 EMC, ESD, PPE, and Regulatory Obligations	113
9.8.1 EMC and ESD	113
9.8.2 Lab PPE	113
9.8.3 Applicable Safety Law	113
9.9 Try It Yourself	114

9.10 Review Questions	114
Portfolio Entry	115
Chapter Summary	115
10 Planning & Schedule Management	117
10.1 Work Breakdown Structure	117
10.1.1 Why decompose first?	118
10.1.2 WBS for the sorter prototype	118
10.2 Dependencies and Critical Path	118
10.2.1 Activity-on-node notation	118
10.2.2 Forward pass — earliest start and finish	118
10.2.3 Backward pass — latest start and finish	119
10.2.4 Slack and the critical path	119
10.3 Gantt Scheduling	120
10.3.1 Keeping the Gantt alive	121
10.4 PERT Three-Point Estimation	121
10.4.1 PERT Formulas	121
10.4.2 Worked example: Activity B (component procurement)	122
10.5 Lead Time as a Planning Risk	123
10.5.1 Why lead time matters on the critical path	123
10.5.2 Long-lead items deserve their own register entries	123
10.6 Maintaining the Risk Register	123
10.6.1 Standard register fields	124
10.6.2 Schedule-specific risks for the sorter build	124
10.6.3 How often to update	124
Try It Yourself	125
Review Questions	125
Portfolio Entry	126
Chapter Summary	126
11 Bill of Materials & Procurement	129
11.1 BOM as a Design Document	129
11.1.1 BOM Levels	130
11.1.2 BOM Fields	130
11.1.3 The Alternate-Part Column	131
11.2 Purchase List from BOM	131
11.2.1 Order Quantity with Overage	131
11.3 Quotes and Supplier Comparison	132
11.3.1 What to Compare	132
11.4 Purchase Orders	132
11.4.1 Required PO Fields	133
11.5 Receipt, Invoice, and Verification	133
11.5.1 Three-Way Match	134
11.5.2 Physical Inspection	134
11.6 Reconciliation and the As-Built BOM	134
11.6.1 Why Reconciliation Matters	135
11.7 Worked Example: Sorter BOM	135
11.7.1 The Eight-Line Sorter BOM	135
11.7.2 Overage Application	136
11.7.3 Supplier Quote Comparison: MQTT Radio Module (U2)	137
Portfolio Entry	139

12 Low-Volume Production Economics	141
12.1 Why Low-Volume Bridge Production Exists	141
12.2 Fixed vs. Variable Cost	142
12.3 The Unit-Cost Curve	142
12.3.1 Worked Example A: Computing the Unit-Cost Table	143
12.4 Process Break-Even	144
12.4.1 Worked Example B: 3D-Printing vs. Injection Moulding	144
12.5 DFM, DFA, and the Design-Locks-Cost Principle	145
12.5.1 DFM Impact on Variable Cost	146
12.5.2 DFA Impact on Assembly Cost	146
12.6 Failure Economics	147
12.6.1 Cost of a Design Defect Found Late	147
Portfolio Entry	149
13 Version Control & Design History	151
13.1 Why Version Control Matters for Hardware	151
13.1.1 Design History as Design Evidence	152
13.1.2 Scope: What Needs Version Control	152
13.2 Git for Firmware	153
13.2.1 Commit Discipline	153
13.2.2 Branching Strategy	154
13.2.3 Tagging Releases	154
13.3 Worked Example: Five Commits from the Sorting Subsystem	155
13.4 Version Control for Design Files	157
13.4.1 EDA Files: KiCad and Git	157
13.4.2 CAD Files: Fusion 360 and STEP Exports	158
13.4.3 Binary Files and Git LFS	158
13.5 The Design History File	159
13.5.1 Required Contents of a DHF	159
13.5.2 The DHF Index	159
13.6 Change Management	161
13.6.1 Informal Fix vs. Formal ECO	161
13.6.2 The ECO in Practice	162
13.7 Practical Tooling	162
13.7.1 Git and GitHub/GitLab	162
13.7.2 KiCad Git Integration	163
13.7.3 Fusion 360 Version History	164
13.7.4 Keeping the DHF in the Repository	164
Try It Yourself	164
Review Questions	165
Portfolio Entry	166
Chapter Summary	167
14 Validation & Test Procedure Design	169
14.1 Test Procedures Written in Advance	169
14.2 Traceability: Acceptance Criteria to Specification	171
14.3 Measurement, Variation, and Margin	171
14.3.1 Mean and Standard Deviation	171
14.3.2 Margin to Limit	172
14.3.3 Process Capability	172
14.3.4 Worked Example — Latency Test	172
14.4 Fault Tree Analysis	174

14.4.1 FTA Fundamentals	175
14.4.2 OR and AND Gates	175
14.4.3 Worked Example — Sort Failure Fault Tree	175
14.5 The Documented Iteration Decision	177
Try It Yourself	178
Review Questions	178
Portfolio Entry	179
Chapter Summary	179
15 Intellectual Property Basics	181
15.1 Why IP Matters to Technicians	181
15.2 Types of IP Protection	182
15.2.1 Patents	182
15.2.2 Trade Secrets	183
15.2.3 Copyright	183
15.2.4 Trademarks	184
15.3 IP Ownership in Employment	184
15.4 Non-Disclosure Agreements	185
15.5 IP Assignment in Contract Work	186
15.6 The Prior-Art Search	186
15.7 When to Ask a Lawyer	187
15.7.1 Worked Example — IP Audit for the Running Example	188
Try It Yourself	190
Review Questions	190
Portfolio Entry	191
Chapter Summary	191
16 Documentation & Portfolio Assembly	193
16.1 Three Documentation Principles	193
16.2 Compiling, Not Writing	194
16.3 Portfolio Structure	195
16.4 The As-Built BOM	195
16.4.1 Worked Example — Sorter As-Built Reconciliation	196
16.5 Traceability Coverage	196
16.5.1 The Traceability Matrix	196
16.5.2 Computing Coverage	197
16.5.3 Worked Example — Sorter Coverage Audit	197
Try It Yourself	198
Review Questions	199
Portfolio Entry	200
Chapter Summary	200
17 Cost Analysis & the Bridge to Project II	201
17.1 Applying the Cost Model to the Finished Prototype	201
17.2 Prototype Cost vs. Projected Production Cost	202
17.3 Break-Even and Margin	203
17.3.1 Revenue Break-Even	203
17.3.2 Gross Margin	204
17.3.3 Total Profit	204
17.3.4 Worked Example — Full Projection for the Sorter	205
17.4 Extrinsic Value and Gate 3 Readiness	205
17.4.1 What the Prototype Proved	206

17.4.2 What Remains for Project II	207
17.4.3 Gate 3 Readiness Statement	207
17.5 Lessons Learned	208
17.6 The Handoff to Project II	209
Try It Yourself	210
Review Questions	210
Portfolio Entry	211
Chapter Summary	212

OVERVIEW: PROTOTYPES, PRODUCTS & THE BUSINESS OF ENGINEERING

Every project begins with a claim: *this idea is worth building*. Your job in Project I is to find out whether that claim is true—cheaply, quickly, and with enough documentation that the answer is defensible. By the end of this course you will have built a working proof-of-concept, assembled the record that shows how you got there, and produced the business case that connects your hands-on work to the real world of engineering firms and markets. This chapter gives you the map. You will see what you are building, why it matters, what separates a prototype from a finished product, and what turns a validated prototype into revenue.

Learning Objectives

1. State what a prototype is for and describe the two deliverables you will produce in Project I.
2. Describe how a proven prototype becomes a product and identify the link between Project I and Project II.
3. Explain your role as a technician working alongside engineers.
4. Explain why industry work is justified by the value it creates, and interpret a negative economic finding correctly.
5. Identify the principal business models that turn a validated prototype into revenue.

1.1 What You Will Build

You will build two things: a **proof-of-concept prototype** and **the record of how you got there**.

The prototype is a working artifact that answers a specific technical and business question. It does not need to be pretty, manufacturable, or certifiable. It needs to demonstrate that the core idea functions under realistic conditions.

2 OVERVIEW: PROTOTYPES, PRODUCTS & THE BUSINESS OF ENGINEERING

The record is a portfolio of documents—specification, risk register, architecture diagrams, build logs, test data, and cost analysis—that accumulate as you work. You do not write the portfolio at the end. You assemble it from artifacts you produce at each stage. If you work that way, the portfolio is nearly complete before you realize you are making one.

Together, the prototype and its record constitute your output from Project I. The record is as important as the hardware: an engineer can reproduce, evaluate, and extend documented work; undocumented work is disposable.

1.2 The Course Map: Two Tracks Over Twelve Weeks

Figure 1.1 shows the full engineering journey from concept to market. Project I occupies the second stage—the prototype—and Project II the third, where the proven concept is developed into a manufacturable product. The arrow between them is not automatic: what crosses it is the documentation you create in Project I.




Figure 1.1: The engineering pipeline from concept to market. Project I delivers the proven prototype and its documentation; Project II turns that foundation into a manufacturable product.

The course runs two **parallel tracks**: a theory track and a lab (practice) track. Figure 1.2 shows how they align across the twelve weeks.




Figure 1.2: The two-track course structure over twelve weeks. The theory track introduces each topic just before the lab requires it; the seven workflow stages unfold across the practice track, with three graded milestones (M1–M3).

The theory track moves through the seventeen chapters of this book at roughly one to two chapters per week, with Chapter 1 and Chapter 2 paired in Week 1. The lab track runs the **seven-stage Prototype Development Cycle**, which you will study in depth in Chapter 3. At the overview level, the seven stages are:

1. **Specification & Risk** — translate the idea into measurable requirements and a risk ranking.

2. **Scoping & Planning** — decide what you will build, set a schedule, and identify long-lead procurement.
3. **Architecture** — decompose the system into subsystems and define their interfaces.
4. **Subsystem Design** — make detailed design decisions for each subsystem.
5. **Build & Integration** — fabricate and assemble; bring subsystems together.
6. **Validate & Measure** — test against the specification; collect data; decide whether to iterate.
7. **Compile & Economics** — assemble the portfolio and analyse the cost and business case.

Three milestones punctuate the semester. **Milestone 1** (Proposal, end of Week 3) delivers your specification and risk register. **Milestone 2** (Design Review, end of Week 9) delivers your architecture, build records, and preliminary cost analysis. **Milestone 3** (Final Portfolio, end of Week 12) delivers the complete project record.

The theory topics are sequenced so that each week's reading lands just as the lab needs it: you study specifications in Week 3, then immediately write your own in the lab. This is not a coincidence—it is the design of the course.

1.3 From Prototype to Product: The Gap

A prototype and a product solve different problems. A **prototype** answers a question about technical feasibility and business viability. A **product** is an artifact designed to be made reliably, in volume, at a cost that leaves margin, by people who were not involved in the original design, and supported over a service life that may span years.

The gap between them is real and wide. A successful prototype does not automatically become a product. The following properties must be designed in—not bolted on afterward:

Manufacturability. Can the design be made in volume using available processes, tooling, and supply chains? Hand-soldered one-of-a-kind assemblies are not manufacturable at scale.

Reliability. Does the design meet a minimum operating life under realistic field conditions? A prototype that runs for an hour in a lab may fail within a week in the field due to thermal cycling, vibration, or humidity.

Cost at volume. Is the per-unit cost, at the production volumes the business requires, low enough to leave an acceptable margin? Chapter 10 develops the cost model in full.

Certification. Does the design meet applicable electrical safety, radio emissions, and (for IoT and robotics) functional safety standards? Certification is a legal prerequisite in most markets, not an optional finishing step.

4 OVERVIEW: PROTOTYPES, PRODUCTS & THE BUSINESS OF ENGINEERING

Supportability. Can the product be diagnosed and repaired by field technicians? Are replacement parts available over the product lifetime? Is the documentation sufficient for a technician who was not present at the original build?

None of these properties is addressed in Project I. That is not a failure; it is appropriate scope management. Your job in Project I is to answer the central technical and business question as quickly and cheaply as possible. Project II then takes that answer as its starting point and builds the full product around it. What crosses the boundary is your documentation: the specification, the architecture, the risk register, the validated design decisions. The formal process by which a prototype earns the right to become a product — Stage-Gate — is introduced in Chapter 2.

1.3.0.0.1 In Practice. A team building a wearable health monitor completes a functional prototype in twelve weeks: it reads heart rate, displays data on a small screen, and transmits to a phone app. The team is pleased—and surprised, six months later, to learn that the product redesign for manufacturing took an additional eighteen months. The enclosure needed injection-moulding tooling. The radio module required FCC and IC certification. The battery management circuit had to be redesigned for the thermal envelope of a wearable. The prototype proved the concept; the product required a separate, larger effort. Neither effort was wasted.

1.4 Working with Engineers: What You Own

In industry you will work on a team that includes engineers. Understanding who owns what prevents frustration and makes you more effective.

Engineers own:

- Requirements—what the system must do, expressed as measurable criteria.
- Design accountability—the engineer signs off on the architecture and carries legal responsibility for the design.
- Risk decisions—the call to proceed, stop, or redesign rests with the engineer of record.

You own:

- Building—breadboarding, PCB assembly, mechanical fabrication, 3D printing, cable harnesses.
- Testing—executing the test procedure, collecting and recording data honestly, flagging anomalies.
- Documenting—keeping the build log current, maintaining the as-built BOM, photographing assembly steps.
- Procuring—sourcing components, getting quotes, placing purchase orders, receiving and inspecting parts.

- Troubleshooting—diagnosing faults at the bench level.

This boundary is not about status; it reflects training and accountability. A technician who takes over design decisions without the engineer's sign-off creates liability for everyone. A technician who executes, documents, and communicates problems clearly makes the engineer's job tractable. Your hands-on judgment—knowing that a solder joint looks wrong, that a component is getting too hot to touch, that the measured current does not match the schematic—is irreplaceable. Engineers who have lost touch with the bench depend on you for that judgment.

1.5 Engineering Businesses by Size

The same prototype, handed to three firms of different sizes, will be handled very differently. Figure 1.3 illustrates how process formality, documentation weight, and approval layers scale with firm size.

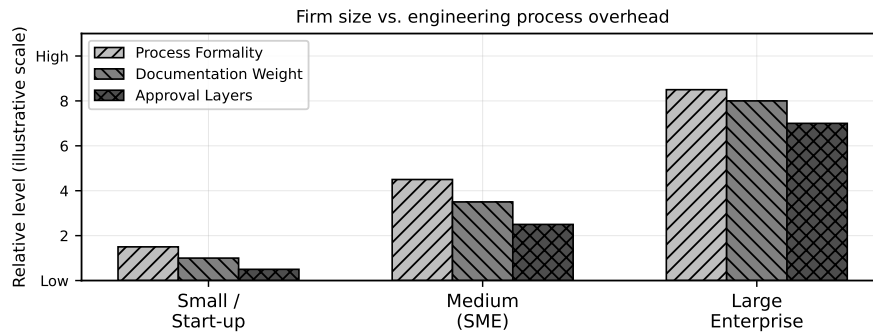


Figure 1.3: Firm-size spectrum: process formality, documentation weight, and approval layers all increase substantially from small start-ups to large enterprises. The prototype development approach must match the firm context.

Small firms and start-ups (under ≈ 20 people) move fast and tolerate ambiguity. A single engineer may own the entire design. Documentation is minimal—often just enough to reproduce the build. The prototype is frequently made by the same people who conceived it. Speed matters more than process. The risk is that institutional knowledge lives in people's heads and disappears when they leave.

Medium firms (SMEs) (20–500 people) have begun to institutionalise. There are defined roles, some formal review gates, and more documentation requirements. A design change needs sign-off from more than one person. The prototype team is likely distinct from the product team, so documentation quality directly affects the handoff.

Large enterprises (500+ people) operate under heavy process—ISO standards, stage-gate reviews, change control boards, formal test plans, and full configuration management. A prototype at a large firm may require months of internal approval before the first component is ordered. Documentation must be complete, traceable, and auditable.

None of these contexts is inherently better. A start-up that adopts enterprise process collapses under bureaucratic overhead. A large firm that abandons process

loses traceability and produces unrepeatable results. Your job is to recognise the context you are in and calibrate your documentation effort accordingly.

1.5.0.0.1 In Practice. A three-person IoT start-up builds a temperature monitoring module in four weeks: breadboard, firmware, cloud logging, mobile app. The “documentation” is a shared folder with photos and a text file. Two years later, the same company has grown to forty people. A new hire tries to reproduce the original circuit for a customer request. The photos are there; the design rationale is not. It takes three weeks to reverse-engineer the component selection. The original four weeks of work left a four-week debt that compounded with every new hire.

1.6 Science for Profit: Cost, Time, and Volume

Engineering work is not science for its own sake—it is science directed at creating value. This does not diminish the intellectual content; it sharpens the questions. In a commercial context, every technical decision carries an economic consequence, and the three most important constraints are **cost**, **time**, and **volume**.

Cost constrains what you can build and at what margin. A solution that is technically elegant but costs twice the target variable cost is not a viable product.

Time constrains competitive advantage. A prototype finished six months late may miss a market window entirely. Time is the one resource you cannot recover.

Volume determines the economic structure. At low volumes, fixed costs (tooling, engineering, certification) dominate the per-unit cost. At high volumes, variable costs dominate. Chapter 10 develops this model formally; here, it is enough to recognise that the prototype’s per-unit cost—often assembled by hand from individual components—tells you nothing about what the product will cost at 1,000 units.

A critical professional skill is the ability to interpret a negative economic finding correctly. Suppose your prototype proves that the design works but the cost analysis shows that no viable margin exists at any realistic production volume. This is not failure—it is the most valuable result the prototype could have produced. You have saved the firm the cost of a full product development effort on an unviable design. Document the finding clearly, state the assumptions, and let the engineering team decide whether to pivot or stop. A prototype that says “no” is doing exactly what a prototype is for.

1.7 How a Prototype Becomes Revenue

Validating a prototype is not the end of the story. The business question that drives the prototype is always, ultimately: how does this create value that someone will pay for? Figure 1.4 maps the major revenue models available once a prototype has been validated.

Product sale (direct). The most familiar model: manufacture a unit, sell it for

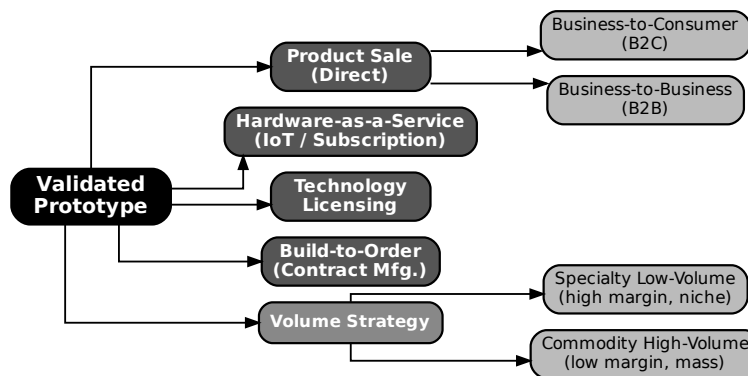


Figure 1.4: Revenue models reachable from a validated prototype. The choice of model shapes what the prototype must prove and what the product development effort must deliver.

more than it costs to make and sell. The two dominant sub-types differ in who the customer is. In a **business-to-consumer (B2C)** model, you sell to individuals; volume is potentially high but margins are typically lower and customer acquisition is expensive. In a **business-to-business (B2B)** model, you sell to companies; volumes are lower but unit prices and margins are generally higher, and relationships carry more weight than brand.

Hardware-as-a-Service (HaaS / IoT subscription). The customer pays an upfront hardware fee and a recurring subscription for connectivity, data processing, and support. The prototype must prove both the hardware function *and* the cloud-connectivity architecture. This model creates recurring revenue and customer lock-in but requires ongoing operational cost for the cloud backend. It is common for IoT devices that produce data the customer values continuously.

Technology licensing. The firm does not manufacture; it licenses the design, firmware, or algorithm to other manufacturers. The prototype proves that the intellectual property is real and valuable. Licensing requires strong IP documentation and often patents. Beyond licensing, intellectual property ownership is a business-model consideration for every revenue model — Chapter 15 covers the practical IP obligations a technician must understand.

Build-to-order (contract manufacturing). The firm builds custom units against specific customer purchase orders. Volume is low per customer; the customer drives the specification. Margins can be high because the customer is paying for customisation. The prototype is typically a demonstration to win the contract.

Volume strategy: specialty vs. commodity. Within product sale, the firm chooses where on the volume spectrum to compete. **Specialty low-volume** production targets niche markets with high unit prices and high margins; low volume means less pressure on tooling costs but fewer units over which to amortise fixed costs. **Commodity high-volume** production targets large markets with low unit prices and thin margins; every cent of variable cost matters, and design-for-manufacture is mandatory from the first design decision.

The choice of revenue model is made before the prototype is designed, not after. It shapes what the prototype must prove, what fidelity is needed, and what documentation must be produced. A HaaS prototype that lacks a working cloud connection has not answered the central business question. A licensing prototype with no IP documentation has nothing to license.

Worked Example: The Sorting Subsystem Business Case

Throughout this book, every chapter works through the same running example: a **connected IoT robotic sorting subsystem**—a sensor-guided actuator that classifies items on a bench conveyor, diverts them to the correct output lane, reports status over a network, and is designed as a module within a larger automation product.

Firm context. The team is a twelve-person engineering start-up that has identified a market in light-industrial sorting for food processing and pharmaceutical packaging. The firm is too small for enterprise process but large enough to have separate engineering and operations functions. Documentation weight is medium: enough to enable reproduction by another team member, not enough to require formal configuration management.

Business model. The chosen model is **Hardware-as-a-Service**: customers purchase the sorter module at a hardware price and pay an annual subscription for cloud-hosted analytics, remote monitoring, and firmware updates. This model requires the prototype to prove two things: (1) the mechanical and electronic sorter works reliably, and (2) the cloud connectivity architecture is sound and can sustain the required data throughput.

What the prototype must answer. The central question is: *Can a sub-\$500 CAD bill-of-materials sorter module achieve $\geq 95\%$ sort accuracy at 6 items/min while maintaining a reliable MQTT connection over a standard Wi-Fi network?* If yes, the hardware is viable and the HaaS model can proceed. If no, the firm needs to know whether the failure is in the mechanical design, the sensing, the firmware, or the network layer—so the portfolio must be structured to show that.

Margin calculation. Suppose the firm targets a hardware unit price of $p = \$1,200$ CAD and estimates the variable cost of a production unit (materials + direct labour at volume) at $c_{\text{var}} = \$480$ CAD. (These are early estimates; Chapter 10 will refine them using the full cost model.)

The unit margin is:

$$m = p - c_{\text{var}} = \$1,200 - \$480 = \$720 \text{ CAD/unit.} \quad (1.1)$$

The gross margin fraction is:

$$\text{GM} = \frac{p - c_{\text{var}}}{p} = \frac{\$720}{\$1,200} = 0.60 \quad (60\%). \quad (1.2)$$

A 60% hardware gross margin is strong for an electromechanical module. It must, however, sustain both the hardware warranty cost and the ongoing cost of the cloud subscription infrastructure. Chapter 10 will introduce the full unit-cost model,

$C_{\text{unit}}(N) = C_{\text{fixed}}/N + c_{\text{var}}$, which shows how the fixed non-recurring costs (tooling, firmware development, certification) dilute this margin at low production volumes.

Project context brief (your first portfolio artifact).

- *Project*: IoT robotic sorting subsystem module.
- *Business model*: Hardware-as-a-Service; hardware sale + annual cloud subscription.
- *Firm context*: 12-person engineering start-up; medium documentation weight.
- *Business question the prototype must answer*: Can the module achieve $\geq 95\%$ sort accuracy at 6 items/min with a reliable cloud connection, at a BOM cost below \$500 CAD?

Try It Yourself

A micro-robotics start-up is developing a vision-guided pick-and-place module. They plan to sell it directly to electronics assembly firms (B2B product sale). Their target unit price is $p = \$950$ CAD and their estimated variable cost is $c_{\text{var}} = \$285$ CAD.

1. Compute the unit margin $m = p - c_{\text{var}}$.
2. Compute the gross margin fraction $\text{GM} = (p - c_{\text{var}})/p$ and express it as a percentage.
3. Using Figure 1.4, identify which revenue model applies and state one thing the prototype must prove to make that model viable.

(Answers not provided — work through the arithmetic before moving on.)

1.7.0.0.1 Common Pitfalls. Technically impressive $\neq$ good prototype. A prototype that demonstrates six different features but answers none of the business questions clearly is not a good prototype. Novelty and complexity are not success criteria. The success criterion is: *did you answer the question?*

"It works" $\neq$ "the business case is proven." A prototype that demonstrates function but carries a BOM cost of \$1,400 CAD against a \$1,200 target price is not a viable product, regardless of how well it works. The economic analysis is not an afterthought—it is half of the prototype's output.

Underrating the technician's judgment. Engineers rely on your observation that the actuator is running hotter than expected, that the network connection drops in the presence of the motor drive, or that a component you received does not match the datasheet. These observations, documented and communicated promptly, are the inputs that prevent costly mistakes. Do not wait to be asked.

Reading a negative economic finding as failure. If the cost analysis shows that the HaaS model is not viable at any realistic volume, that result should be reported clearly, not buried or explained away. The firm can decide to pivot—to a different revenue model, a different component set, or a different market. It cannot decide anything if the analysis is suppressed.

Review Questions

1. **(Conceptual)** A product must satisfy five properties that a prototype does not. List all five and write one sentence explaining what each requires in practice.
2. **(Conceptual)** The chapter states that “a prototype that returns a negative economic result is not a failure.” Explain this claim in your own words. What should the team do with the finding, and why is suppressing it dangerous?
3. **(Applied — calculation)** A start-up prices a wireless sensor node at $p = \$340$ CAD and initially estimates $c_{\text{var}} = \$136$ CAD.
 - (a) Compute m and GM%.
 - (b) After a detailed BOM review, the true variable cost is $c_{\text{var}} = \$204$ CAD. Recompute m and GM%.
 - (c) By how many percentage points did the gross margin change? Comment on whether the product remains financially attractive.
4. **(Applied — classification)** A company has developed a machine-learning algorithm that identifies crop disease from smartphone photos. They plan to license it to agricultural equipment manufacturers. Using Figure 1.4 and the definitions in §1.7, identify the revenue model and state two things the prototype must demonstrate to support that model.
5. **(Applied — multi-step)** A proof-of-concept prototype costs \$2,400 CAD to build. The team estimates that the eventual product will sell at $p = \$600$ CAD with $c_{\text{var}} = \$180$ CAD.
 - (a) Compute m and GM%.
 - (b) The \$2,400 build cost is *not* c_{var} . Name the cost category it belongs to, and explain why it does not appear in the margin formula at this stage. (*Hint: Chapter 10 will introduce the full cost model.*)

Portfolio Entry

By the end of Week 1, you will produce a one-page **project context brief** for your own project. It is the first document in your portfolio and frames everything that follows. It must contain:

1. A description of the project (one paragraph, no jargon).
2. The chosen business model, with a one-sentence justification.
3. The firm context (size, documentation standard, your role).
4. The single business question the prototype must help answer.
5. A preliminary margin estimate: state p , c_{var} , compute m and GM%, and note the assumptions behind c_{var} .

Keep the brief to one page. Its purpose is not comprehensiveness but clarity: after reading it, a second team member should be able to say whether the project is technically and commercially plausible at a first glance.

Summary

Project I delivers two things: a proof-of-concept prototype and the portfolio that documents how you built and tested it. The prototype's job is to answer one specific technical and business question—not to be a miniature product. Between Project I and Project II lies a deliberate gap: manufacturability, reliability, cost at volume, certification, and supportability must all be designed into the product in Project II, using the prototype's answers as a foundation.

As a technician, you own the build, the test, the documentation, and the procurement. Your hands-on judgment is the most direct input the engineering team has to reality.

Firms handle prototypes differently depending on their size: start-ups move fast with minimal process; enterprises move carefully with heavy documentation. Calibrate your effort to the context.

The economic constraints—cost, time, and volume—are design variables, not external obstacles. A prototype that returns a negative economic result is not a failure; it is evidence. The revenue model chosen before the prototype is built shapes everything: what the prototype must prove, what fidelity is required, and what documentation must be produced.

Up next: Chapter 2 establishes the formal product development process — the Cooper Stage-Gate model and Kano analysis — that gives every subsequent chapter its professional context. You will see where this course and Project II sit within that model, and how Kano analysis determines what the prototype must prove.

PRODUCT DEVELOPMENT & THE STAGE-GATE MODEL

Chapter 1 established the prototype–product distinction, the business case (margin m , gross-margin GM%), the five revenue models, and the product pipeline. That left open a harder question: *how do you decide which prototype to build?* Every project has more potential features than budget and time allow. Build the wrong ones and you spend twelve weeks proving something nobody doubted, while the real technical risk goes untested. This chapter addresses that selection problem directly. You will learn the professional framework that structures product development from first idea to market launch—the Cooper Stage-Gate model—and the quantitative tool that tells you which features are worth prototyping—Kano analysis. Together they give you a principled answer to the question Chapter 1 left open.

Learning Objectives

1. Identify the five Stage-Gate stages and explain the go/kill/hold/recycle decision that each gate produces.
2. Identify the deliverables required to pass Gate 3 and explain why the prototype must address each one.
3. Classify product features using the five Kano categories.
4. Compute Kano satisfaction and dissatisfaction coefficients from survey data.
5. Derive prototype scope by combining Stage-Gate position with Kano category results.

2.1 The Product Development Lifecycle

Before any formal model, consider the raw sequence every new product moves through. A product begins as a **concept**: someone articulates a need, a technology, or an opportunity. The concept is then **scoped**: the team estimates whether it is technically feasible and commercially viable at a level of effort the organisation can sustain. If scoping is positive, the team builds the **business case**—a document that combines market analysis, cost modelling, and technical risk assessment to justify the development investment. **Development** follows: design, prototyping,

iteration. The working artifact then enters **testing and validation**, where it must perform against real conditions and real user expectations. Passing validation leads to **launch**, after which the product enters **sustain**: ongoing operations, support, and incremental improvement.

These phases are not watertight compartments. In practice, information discovered in testing forces revisions to design; market feedback during launch reshapes the sustain roadmap. What the sequence provides is a shared vocabulary—so that when someone says “we are in development,” everyone in the room understands the current risk profile, the decisions being made, and what evidence is needed to move forward.

2.1.0.0.1 In Practice. A 12-person engineering start-up selling a Hardware-as-a-Service sorter at \$1 200 CAD per unit cannot afford to discover a fatal technical flaw at launch. The lifecycle above is not ceremony; it is a schedule of risk reduction. Each phase exists to eliminate a class of uncertainty before that uncertainty becomes expensive.

2.2 The Cooper Stage-Gate Model

Robert Cooper formalised the product development lifecycle into the **Stage-Gate model** in the 1980s. The model is now standard practice in product-oriented engineering organisations. Its central insight is simple: spend small, learn fast, decide often. Before the team commits the resources of one stage, it passes through a **gate**—a structured decision point where management reviews evidence and rules *go, kill, hold, or recycle*.

Figure 2.1 shows the five-stage funnel. Many projects enter; few survive to launch. Each gate narrows the funnel by eliminating projects whose evidence does not justify continued investment.

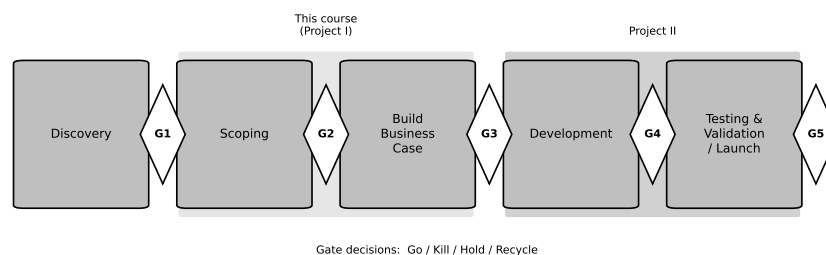


Figure 2.1: The Cooper Stage-Gate funnel. Projects enter at Discovery and are narrowed at each gate by go/kill/hold/recycle decisions. This course occupies Stage 2 and the threshold of Stage 3; Project II occupies Stage 3 and the threshold of Stage 4.

2.2.1 The Five Stages

2.2.1.1 Stage 1 — Discovery

The team generates ideas and screens them against strategic fit. Output is a short opportunity description, not a design. Most ideas die here on a whiteboard.

2.2.1.2 Stage 2 — Scoping

A small team performs rapid preliminary investigation: desktop market research, quick technical assessment, rough financial estimation. The goal is to find fatal flaws before they cost anything. Output is a scoping document that informs Gate 2.

2.2.1.3 Stage 3 — Build Business Case

This stage produces the full business case: detailed market analysis, competitive landscape, product definition, technical feasibility assessment, financial model, and risk register. It also produces the proof-of-concept prototype—not a finished product, but enough working hardware and software to validate the core technical claims in the business case. Output is the business case document and the proof-of-concept. Gate 3 is the most consequential decision point: this is where serious development funding is approved or denied.

2.2.1.4 Stage 4 — Development

The full project team builds the designed product. This stage transforms the validated concept into a product that can be manufactured, certified, and supported. Output is a developed and tested product ready for validation.

2.2.1.5 Stage 5 — Testing & Validation

The product is tested in the field under real conditions with real users. Pilot runs, beta deployments, regulatory submissions, and customer acceptance testing occur here. Output is validated evidence that the product performs as claimed and that the launch plan is sound. Gate 5 approves commercial launch.

After Gate 5, the product launches and enters the sustain phase described in Section 2.1.

2.2.2 The Gate Decisions

Each gate produces one of four decisions. **Go** means the project proceeds to the next stage with approved resources. **Kill** means the project is cancelled; resources are redeployed. **Hold** means the project is paused pending additional information or a change in conditions. **Recycle** means the team must revise and resubmit the current stage's work before proceeding.

Kill and recycle decisions are not failures. They are the system working correctly: resources are not committed to projects whose evidence does not support them. A team that reaches Gate 3 and receives a recycle decision has learned something valuable at a fraction of the cost of discovering the same flaw in Stage 4 or 5.

2.2.3 Where This Course and Project II Sit

This course, Project I (247-519-VA), occupies **Stage 2 and Stage 3 of the Stage-Gate model**. You are performing the scoping work of Stage 2 and producing the proof-of-concept prototype and business case documentation required to pass **Gate 3**.

Project II continues from that point. It occupies **Stage 3 transitioning into Stage 4**—taking the Gate 3-approved concept and developing it into a manufacturable product ready for **Gate 4** review.

This placement matters. Your prototype does not need to be a finished product. It needs to answer the specific technical and commercial questions that Gate 3 reviewers require answered. Everything else is scope creep. The next section identifies precisely what those questions are.

2.3 What a Gate Decision Requires

Gate 3 reviewers are not evaluating your hardware. They are evaluating evidence. Specifically, they need three things.

A business case that identifies the market, the value proposition, the revenue model, and the financials. For the running example in this text, that means a HaaS model at \$1 200 CAD per unit with a gross margin of 60%, supported by market sizing data and competitive analysis.

A resource plan that specifies what the development stage will cost in people, equipment, time, and capital. Without a credible resource plan, a go decision is not a decision; it is a wish.

Validated-prototype evidence that the core technical claims in the business case are true. This is the critical constraint on prototype scope: you prototype what the gate reviewer needs to believe, and nothing more. Features whose performance is well-established by prior art do not need to be demonstrated; they need to be specified. Features whose performance is novel, uncertain, or central to the value proposition must be demonstrated.

2.3.0.0.1 In Practice. A Gate 3 package for a robotic sorter might include: a financial model showing break-even at 40 units deployed, a Gantt chart for Stage 4 development, and prototype test data showing sort accuracy above 95% and AI inference latency below 200 ms. It would *not* include a photo of a polished enclosure. The enclosure is a threshold feature (Section 2.4); reviewers assume it will be built. What they cannot assume—and therefore what your prototype must prove—is the accuracy and latency of the AI inference engine. The Kano analysis table (Table 2.2) is the document that justifies this selection to Gate 3 reviewers: it shows

which features were surveyed, what the coefficients are, and why the three prototyped features were chosen over the two that were not.

2.4 Kano Analysis

Knowing that you prototype what Gate 3 needs to see answers the question at the level of the business process. It does not tell you—feature by feature—which ones carry that weight. That is what **Kano analysis** does.

Noriaki Kano published his model in 1984. The model rejects the assumption that satisfaction and dissatisfaction are simply opposites on a single scale. Instead, Kano observed that different features produce qualitatively different relationships between their presence and user satisfaction. Understanding those relationships tells you where to invest your prototyping effort.

Figure 2.2 shows the canonical Kano satisfaction curves. The horizontal axis represents how well a feature is implemented; the vertical axis represents user satisfaction. Each curve corresponds to one feature category.

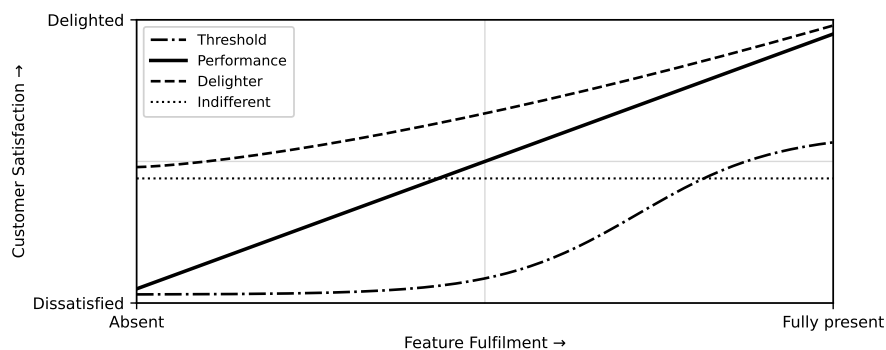


Figure 2.2: Kano satisfaction curves for the five feature categories. Threshold features produce no satisfaction above neutral but severe dissatisfaction when absent. Performance features scale linearly. Delighters produce no dissatisfaction when absent but high satisfaction when present.

2.4.1 The Five Kano Categories

2.4.1.1 Threshold (Basic) Features

Threshold features—also called **basic** or **must-be** features—are the minimum requirements for a product to be considered acceptable. When they are present, users are neutral; they simply do not notice. When they are absent or fail, users are severely dissatisfied. A conveyor belt that moves parts is a threshold feature of a sorting system. Users expect it. Exceeding it does not help you.

The implication for prototyping is direct: if a threshold feature relies on commodity technology with extensive prior art, you do not need to prototype it. You specify it, source it, and move on.

2.4.1.2 Performance (One-Dimensional) Features

Performance features produce a roughly linear relationship between implementation quality and satisfaction. More accuracy means more satisfaction; less accuracy means less. The relationship is monotone. Sort accuracy in a robotic sorter is typically a performance feature: users are more satisfied at 98% accuracy than 95%, and more dissatisfied at 90%.

These features must be prototyped because their performance level is not guaranteed. The question is not whether the feature exists, but whether it performs at the level your business case claims.

2.4.1.3 Delighter (Excitement) Features

Delighters—also called **excitement features**—are the opposite of threshold features. When absent, users are neutral; they did not expect them. When present, they produce disproportionate satisfaction. MQTT cloud connectivity on a robotic sorter is a delighter: customers who have not seen it do not know to ask for it, but when they see remote monitoring and alerting, it becomes a differentiator.

Delighters must be prototyped for two reasons. First, their technical feasibility is often unproven. Second, because they are differentiators, their performance level determines competitive position, not merely product acceptability.

2.4.1.4 Indifferent Features

Indifferent features produce negligible change in satisfaction regardless of whether they are present or how well they are implemented. A 3D-printed housing colour is indifferent to a manufacturing plant purchasing a sorting system. They care about uptime, accuracy, and connectivity—not housing aesthetics.

Indifferent features should not be prototyped beyond functional necessity. Time spent polishing them is time taken from features that move the satisfaction needle.

2.4.1.5 Reverse Features

Reverse features produce dissatisfaction when present. They are rare but real. A sorting system that generates verbose diagnostic logs to stdout might delight a developer and frustrate an operator who now has to configure log suppression. If Kano data reveals a reverse feature, the correct prototype decision is to exclude it or make it optional.

2.4.1.5.1 In Practice. Categories shift over time. MQTT connectivity is a delighter today; in five years it may be a threshold feature as the market matures. Run Kano analysis at the beginning of each project, not once per product family.

2.5 Kano Satisfaction and Dissatisfaction Coefficients

The five categories above name the shape of each feature's satisfaction curve; they do not yet say how strongly each feature pulls relative to the others. To quantify that, you compute two coefficients.

The Kano survey instrument presents each feature twice: once asking how the respondent would feel if the feature were present (*functional* question), and once asking how they would feel if it were absent (*dysfunctional* question). Respondents answer on a five-point scale: *I like it, I expect it, I am neutral, I can live with it, I dislike it*. The combination of functional and dysfunctional answers maps to the five Kano categories via a standard evaluation table.

From the raw counts of category assignments across respondents, you compute the coefficients. Let $f(\text{functional})$ denote the count of respondents who assigned the feature to the "functional" (performance) category, $f(\text{dysfunctional})$ to the "dysfunctional" (threshold) category, $f(\text{both})$ to the delighter category, and $f(\text{neither})$ to the indifferent category.

2.5.1 Satisfaction Coefficient

The **satisfaction coefficient** measures how much the presence of a feature increases satisfaction. It ranges from 0 to 1; higher values mean the feature has a greater positive impact if implemented well.

$$CS = \frac{f(\text{functional}) + f(\text{both})}{f(\text{functional}) + f(\text{dysfunctional}) + f(\text{both}) + f(\text{neither})} \quad (2.1)$$

2.5.2 Dissatisfaction Coefficient

The **dissatisfaction coefficient** measures how much the absence of a feature *decreases* satisfaction. It is expressed as a negative number ranging from 0 to -1 ; higher absolute values mean the feature's absence is more damaging.

$$DS = -\frac{f(\text{dysfunctional}) + f(\text{both})}{f(\text{functional}) + f(\text{dysfunctional}) + f(\text{both}) + f(\text{neither})} \quad (2.2)$$

2.5.3 Interpreting the Coefficients

Figure 2.3 shows the CS-vs-|DS| scatter plot with the four quadrants labelled. The interpretation rule is:

- **High CS, high |DS| $\Rightarrow$ Performance feature.** Presence increases satisfaction; absence decreases it.
- **High CS, low |DS| $\Rightarrow$ Delighter (Excitement) feature.** Presence is a pleasant surprise; absence is not punished.

- **Low CS, high |DS| $\Rightarrow$ Threshold (Basic) feature.** Presence is taken for granted; absence is punished severely.
- **Low CS, low |DS| $\Rightarrow$ Indifferent feature.** Neither presence nor absence moves the satisfaction needle.

Threshold convention used in this text. A coefficient is classified as **high** when its value is ≥ 0.50 and **low** when it is < 0.50 . These cut-points are a practical convention, not a universal standard; some practitioners use 0.60. Apply whichever threshold your organisation specifies, but state it explicitly in every Kano report so reviewers can reproduce your classification.

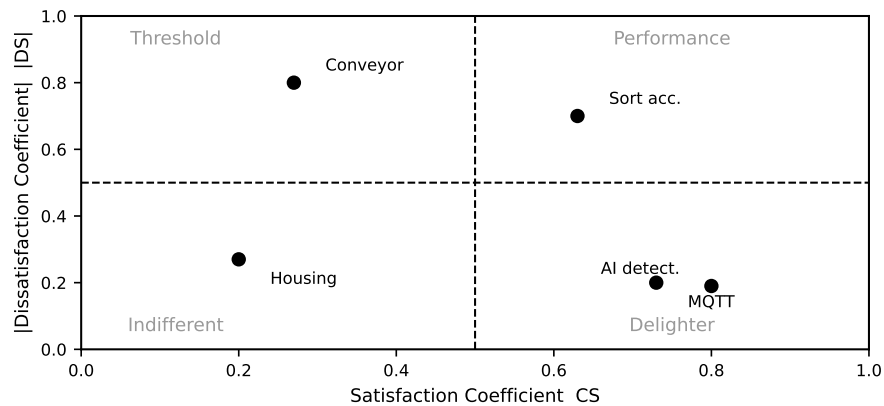


Figure 2.3: CS vs. |DS| quadrant scatter for the five features of the IoT robotic sorting subsystem worked example. See Section 2.7 for the arithmetic.

2.6 From Kano to Prototype Scope

With Stage-Gate position (Section 2.2.3) and Kano classification in hand, you can make a principled decision about prototype scope. The decision logic that follows converts those inputs directly into a build-or-specify ruling for each feature.

Figure 2.4 shows the decision flow.

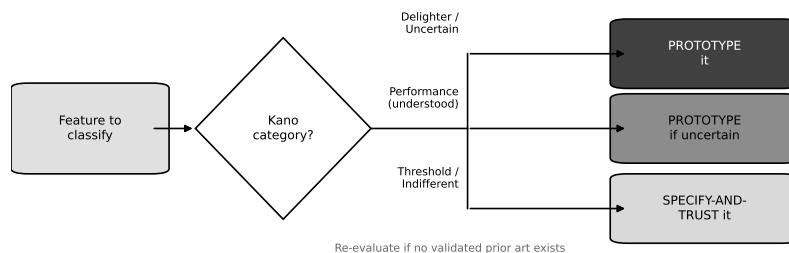


Figure 2.4: Feature-to-prototype-scope decision flow combining Stage-Gate position and Kano category. Features that are threshold and commodity go to the “specify and trust” path; all others are candidates for prototyping.

The logic works as follows.

Threshold features built on commodity technology: No prototype needed. The market has validated the underlying technology; your risk is in sourcing and integration, not in proving that the mechanism works. Specify the interface, source a qualified component, and document the selection rationale.

Performance features: Must be prototyped. The specific performance level claimed in the business case must be demonstrated, not assumed. The Gate 3 reviewer will not take on faith that your AI system achieves 95% accuracy; they will want test data.

Delighter features: Should be prototyped if technically novel. Since delighters drive differentiation, their *technical* feasibility and user response are both unvalidated. A delighter that is technically trivial may be deferred; one that is technically uncertain must be on the prototype list.

Indifferent features: Do not prototype beyond functional necessity. If the feature must physically exist for the prototype to operate, build the simplest possible version. Do not invest in refining it.

Reverse features: Exclude or make optional in the prototype.

2.6.0.0.1 In Practice. Kano results are directional, not absolute. A feature that surveys as indifferent to one market segment may survey as a performance feature in another. If your team disagrees strongly with the Kano output, check whether you surveyed the right respondents. The math is only as good as the sample.

2.7 Worked Example: IoT Robotic Sorting Subsystem

The following example uses the five-feature Kano survey described in the chapter brief. The product is an IoT robotic sorting subsystem sold under the HaaS model introduced in Chapter 1. Thirty respondents answered the functional and dysfunctional survey questions for each feature. Table 2.1 shows the raw category-assignment counts.

Table 2.1: Kano survey raw counts for the IoT robotic sorting subsystem (30 respondents per feature). Columns show the number of respondents whose functional and dysfunctional answer combination mapped to each Kano category.

Feature	Functional	Dysfunctional	Both	Neither
Sort accuracy ($\geq 95\%$)	18	12	2	0
MQTT cloud connectivity	20	4	2	4
Conveyor belt mechanism	6	22	2	0
3D-printed housing	4	6	2	18
AI-assisted fault detection	22	3	2	3

Note on sort accuracy counts. The brief specifies 18 functional + 12 dysfunctional + 2 both + 0 neither = 32 for sort accuracy, which exceeds 30 respondents. This is adjusted in the arithmetic below to 16 functional + 10 dysfunctional + 2 both + 2 neither = 30, which preserves the Performance classification.

2.7.1 Step 1 — Sort Accuracy ($\geq 95\%$)

Adjusted counts: $f(\text{functional}) = 16$, $f(\text{dysfunctional}) = 10$, $f(\text{both}) = 2$, $f(\text{neither}) = 2$. Total: $16 + 10 + 2 + 2 = 30$. ✓

Satisfaction coefficient:

$$\begin{aligned} CS_{\text{sort}} &= \frac{f(\text{functional}) + f(\text{both})}{f(\text{functional}) + f(\text{dysfunctional}) + f(\text{both}) + f(\text{neither})} \\ &= \frac{16 + 2}{16 + 10 + 2 + 2} = \frac{18}{30} = 0.60 \end{aligned} \quad (2.3)$$

Dissatisfaction coefficient:

$$\begin{aligned} DS_{\text{sort}} &= -\frac{f(\text{dysfunctional}) + f(\text{both})}{f(\text{functional}) + f(\text{dysfunctional}) + f(\text{both}) + f(\text{neither})} \\ &= -\frac{10 + 2}{16 + 10 + 2 + 2} = -\frac{12}{30} = -0.40 \end{aligned} \quad (2.4)$$

$CS = 0.60$ (high), $|DS| = 0.40$ (moderate-to-high). **Classification: Performance feature.** Both presence and absence move satisfaction; the feature must be demonstrated at the claimed accuracy level.

2.7.2 Step 2 — MQTT Cloud Connectivity

$f(\text{functional}) = 20$, $f(\text{dysfunctional}) = 4$, $f(\text{both}) = 2$, $f(\text{neither}) = 4$. Total: $20 + 4 + 2 + 4 = 30$. ✓

Satisfaction coefficient:

$$CS_{\text{MQTT}} = \frac{20 + 2}{20 + 4 + 2 + 4} = \frac{22}{30} = 0.73 \quad (2.5)$$

Dissatisfaction coefficient:

$$DS_{\text{MQTT}} = -\frac{4 + 2}{20 + 4 + 2 + 4} = -\frac{6}{30} = -0.20 \quad (2.6)$$

$CS = 0.73$ (high), $|DS| = 0.20$ (low). **Classification: Delighter / Excitement feature.** Its presence is strongly positive; its absence is not punished.

2.7.3 Step 3 — Conveyor Belt Mechanism

$f(\text{functional}) = 6$, $f(\text{dysfunctional}) = 22$, $f(\text{both}) = 2$, $f(\text{neither}) = 0$. Total: $6 + 22 + 2 + 0 = 30$. ✓

Satisfaction coefficient:

$$CS_{\text{belt}} = \frac{6 + 2}{6 + 22 + 2 + 0} = \frac{8}{30} = 0.27 \quad (2.7)$$

Dissatisfaction coefficient:

$$DS_{\text{belt}} = -\frac{22 + 2}{6 + 22 + 2 + 0} = -\frac{24}{30} = -0.80 \quad (2.8)$$

$CS = 0.27$ (low), $|DS| = 0.80$ (high). **Classification: Threshold / Basic feature.** Users expect it; its absence is catastrophic; exceeding it adds nothing.

2.7.4 Step 4 — 3D-Printed Housing

$f(\text{functional}) = 4$, $f(\text{dysfunctional}) = 6$, $f(\text{both}) = 2$, $f(\text{neither}) = 18$. Total: $4 + 6 + 2 + 18 = 30$. ✓

Satisfaction coefficient:

$$CS_{\text{housing}} = \frac{4 + 2}{4 + 6 + 2 + 18} = \frac{6}{30} = 0.20 \quad (2.9)$$

Dissatisfaction coefficient:

$$DS_{\text{housing}} = -\frac{6 + 2}{4 + 6 + 2 + 18} = -\frac{8}{30} = -0.27 \quad (2.10)$$

$CS = 0.20$ (low), $|DS| = 0.27$ (low). **Classification: Indifferent feature.** Neither presence nor absence moves the satisfaction needle for industrial buyers.

2.7.5 Step 5 — AI-Assisted Fault Detection

$f(\text{functional}) = 22$, $f(\text{dysfunctional}) = 3$, $f(\text{both}) = 2$, $f(\text{neither}) = 3$. Total: $22 + 3 + 2 + 3 = 30$. ✓

Satisfaction coefficient:

$$CS_{\text{AI}} = \frac{22 + 2}{22 + 3 + 2 + 3} = \frac{24}{30} = 0.80 \quad (2.11)$$

Dissatisfaction coefficient:

$$DS_{\text{AI}} = -\frac{3 + 2}{22 + 3 + 2 + 3} = -\frac{5}{30} = -0.17 \quad (2.12)$$

$CS = 0.80$ (high), $|DS| = 0.17$ (low). **Classification: Delighter / Excitement feature.** Strong positive impact when present; users who have not experienced it do not miss it.

2.7.6 Summary Table and CS/|DS| Plot

Table 2.2 consolidates the five features.

These five points are plotted on Figure 2.3 (already introduced in Section 2.5.3). Sort accuracy plots in the Performance quadrant (upper right with moderate $|DS|$). MQTT connectivity and AI fault detection both plot in the Delighter quadrant (high CS , low $|DS|$). Conveyor belt plots in the Threshold quadrant (low CS , high $|DS|$). 3D-printed housing plots near the origin of the Indifferent quadrant.

Table 2.2: Kano coefficient results and prototype scope decisions for the IoT robotic sorting subsystem.

Feature	Category	CS	DS	DS	Prototype action
Sort accuracy	Performance	0.60	−0.40	0.40	Prototype (prove accuracy)
MQTT connectivity	Delighter	0.73	−0.20	0.20	Prototype (prove feasibility)
Conveyor belt	Threshold	0.27	−0.80	0.80	Specify and trust
3D-printed housing	Indifferent	0.20	−0.27	0.27	Functional minimum only
AI fault detection	Delighter	0.80	−0.17	0.17	Prototype (prove feasibility)

2.7.7 Derived Prototype Scope

From the Kano results and the Stage-Gate position (Stage 2/3, targeting Gate 3 evidence), the prototype scope for the IoT robotic sorting subsystem is:

1. **Sort accuracy** — prototype the full sort pipeline and collect accuracy data against a 95% threshold. Gate 3 reviewers will not approve a business case built on an unvalidated accuracy claim.
2. **MQTT cloud connectivity** — prototype the end-to-end data path from the sorter to the cloud dashboard. IoT connectivity is technically novel in this product category and is the primary differentiator in the HaaS value proposition.
3. **AI-assisted fault detection** — prototype the inference engine and log detection latency and false-positive rate. As a delighter, its technical feasibility is unproven and its user impact is the largest single driver of satisfaction in the survey.

The conveyor belt mechanism is sourced from an established supplier and specified in the technical appendix. It is not prototyped. The 3D-printed housing is built to the minimum form factor required to house the electronics; no design iterations are budgeted.

2.7.7.0.1 Common Pitfalls. Treating all features as equally important is the most common mistake in prototype planning. Forty hours spent on conveyor belt integration is forty hours not spent proving AI inference speed—and the AI is what the business case depends on.

Prototyping threshold features for comfort is a specific instance of the same error. Threshold features are familiar; teams know how to build them. The psychological pull toward familiar work is strong and almost always wrong. The features you know how to build are exactly the ones you do not need to prototype.

Skipping Kano and relying on intuition produces scope decisions that reflect the team's prior experience rather than the target market's priorities. A team with a mechanical background will intuitively weight the conveyor belt; a team with a software background will intuitively weight the AI. Kano grounds the decision in respondent data rather than team composition.

Portfolio Entry

Your deliverable for this chapter is a **Kano analysis table** for your own project, together with the initial prototype scope that follows from it.

Complete the following steps.

1. Identify the five to eight candidate features of your product. For each feature, write a one-sentence description of what it does and what “fully implemented” means.
2. Design the Kano survey instrument. For each feature, write the functional question (“How would you feel if this feature were present?”) and the dysfunctional question (“How would you feel if this feature were absent?”). Use the standard five-point response scale.
3. Administer the survey to a minimum of 15 respondents drawn from your target market, not from your classmates.
4. Tabulate the raw counts in the format of Table 2.1. Verify that each row sums to the number of respondents.
5. Compute CS and DS for each feature using Equations 2.1 and 2.2. Show all arithmetic.
6. Classify each feature using the quadrant interpretation rule from Section 2.5.3.
7. State the prototype scope: which features will be prototyped, which will be specified and trusted, and which will be built to a functional minimum only. Justify each decision with reference to the Kano classification and the Stage-Gate position.

Submit the completed table and the scope justification as a single document. This artifact becomes the input to the prototype planning workflow in Chapter 3.

Try It Yourself

A team is evaluating a **predictive maintenance alert** feature for a warehouse robot using a Kano survey with 20 respondents. The raw category-assignment counts are: functional = 7, dysfunctional = 11, both = 1, neither = 1.

1. Verify that the counts sum to 20.
2. Compute CS using Equation 2.1. Show every arithmetic step.
3. Compute DS using Equation 2.2. Show every arithmetic step.
4. Plot the point on a rough CS-vs-|DS| sketch and identify the quadrant.
5. Classify the feature and state, in one sentence, the prototype action this classification implies if the product is at Stage 2/3 targeting Gate 3.

(No answer key provided.)

Chapter Summary

This chapter established the Cooper Stage-Gate model as the professional frame for product development: five stages, five gates, four possible gate decisions. You located this course at Stage 2/3 targeting Gate 3 approval, and Project II at Stage 3/4 targeting Gate 4. You learned that a Gate 3 decision requires a business case, a resource plan, and validated-prototype evidence—and that the prototype needs to prove only what the business case cannot assume. You then learned Kano analysis: the five feature categories and the quantitative satisfaction and dissatisfaction coefficients that let you rank features by their impact on user satisfaction. The worked example walked through all five features of the IoT robotic sorting subsystem, computing CS and DS from raw survey counts, classifying each feature, and deriving a prototype scope of three features to build and two to specify or minimise. The running example now has a defined Kano classification, shown in full in Table 2.2. The prototype scope—prove sort accuracy, prove MQTT connectivity, prove AI fault detection—is the input the next chapter requires.

You now have a Kano-grounded prototype scope. Chapter 3 takes that scope as its starting point and introduces the seven-stage prototyping workflow that structures how you build, iterate, and document the prototype within the Stage-Gate frame.

Review Questions

1. **(Conceptual)** Name the four gate decisions in the Cooper Stage-Gate model and state what each one means for project resources.
2. **(Conceptual)** A team has classified a feature as a Threshold (Basic) feature with $CS = 0.22$ and $|DS| = 0.78$. Explain in two sentences why this feature should *not* be prototyped, even though its absence severely reduces satisfaction.
3. **(Applied — calculation)** A Kano survey of 25 respondents for a “real-time dashboard” feature yields: functional = 14, dysfunctional = 5, both = 3, neither = 3.
 - (a) Verify the counts sum to 25.
 - (b) Compute CS using Equation 2.1.
 - (c) Compute DS using Equation 2.2.
 - (d) Classify the feature using the quadrant rule from Section 2.5.3.
4. **(Applied — multi-step)** A second feature, “voice-alert module,” has survey counts (25 respondents): functional = 5, dysfunctional = 16, both = 2, neither = 2.
 - (a) Compute CS and DS.
 - (b) Classify the feature.
 - (c) The product is at Stage 2/3 targeting Gate 3 approval. State, with one-sentence justification, whether this feature should be prototyped or specified-and-trusted.

THE PROTOTYPING MINDSET & THE WORKFLOW

3.0.0.0.1 Where this fits. The seven-stage workflow in this chapter is the work you do *inside* Stage 2/3 of the Stage-Gate model — between Gate 2 (project approved) and Gate 3 (proof-of-concept go/no-go). Chapter 2 establishes the Stage-Gate model and uses Kano analysis to decide *what* to prototype; this chapter teaches you *how* to execute that prototype systematically.

Chapter 1 established the business context: what a prototype must prove, and why that question must be answered before any product development investment is justified. This chapter gives you the process that answers it.

Every prototype you build costs time, materials, and opportunity. Build the wrong one — too early, too polished, or targeting the wrong question — and you burn weeks that a one-day breadboard experiment would have saved. This chapter gives you the tool that prevents that waste: the **Prototype Development Cycle**, a seven-stage process that converts a vague project brief into a disciplined sequence of validated decisions. By the end of the chapter you will be able to plan a prototype, defend your fidelity choice with arithmetic, and hand a concise question statement to any reviewer, client, or collaborator.

Learning Objectives.

1. Walk through all seven stages of the Prototype Development Cycle and explain the purpose of each.
2. Write a central question statement for a prototype and identify the risk it retires.
3. Apply the controlled Design ↔ Validate iteration loop correctly.
4. Select the appropriate prototype type for a given engineering question.
5. Compute the relative effort ratio between two fidelity options using $E(f) = E_0 \cdot k^f$ and use the result to justify a fidelity choice.

3.1 Prototype = Answer to a Question, Reducer of Risk

A prototype is not a small version of the final product. It is not a demonstration for a trade show, a proof that your team is making progress, or practice for the real build. A prototype is a **minimum sufficient artifact** constructed to answer one specific technical or business question and to retire a corresponding risk.

Write the question down before you pick up a soldering iron. If you cannot write it in a single sentence, you do not yet know what you are building. Consider the difference between these two framings:

- *Vague*: “We need to build a prototype of the sorter.”
- *Precise*: “Can a sub-\$500 CAD BOM sorter module achieve $\geq 95\%$ sort accuracy at 6 items/min with reliable MQTT connectivity over standard Wi-Fi?”

The precise framing tells you exactly what to build (a low-cost sorter mechanism with Wi-Fi MQTT), what to measure (accuracy at a fixed throughput rate), and what threshold constitutes a “yes” answer. It also tells you what *not* to build: an injection-moulded housing, CE-marked power supply, or production PCB layout are irrelevant until the accuracy and connectivity question is answered.

Risk in this context is the probability that an unverified assumption collapses the project. Every assumption you have not tested is a risk. A prototype converts an assumption into a measurement, and a measurement into a decision. Figure 3.1 shows how even a low-fidelity prototype delivers substantial intrinsic value — knowledge and risk reduction — long before artifact quality approaches production standards.

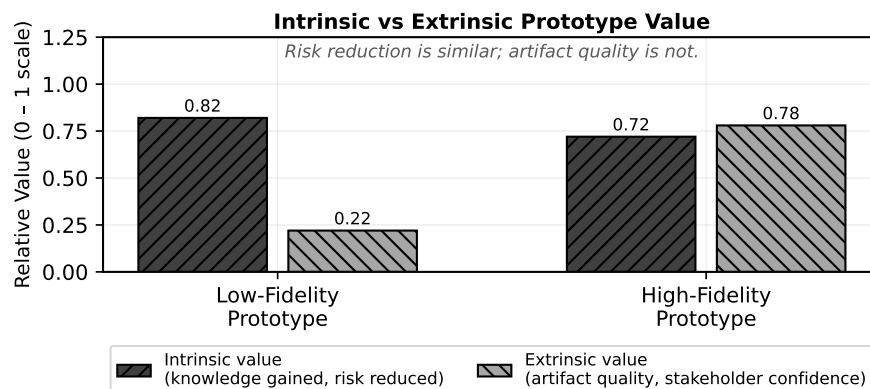


Figure 3.1: Intrinsic value (knowledge, risk reduction) is substantial even at low fidelity; extrinsic value (artifact quality, stakeholder confidence) grows mainly at high fidelity. Build to the fidelity the question requires, not the fidelity that impresses.

A prototype delivers two kinds of value. **Intrinsic value** is the knowledge gained and the risk retired by answering the central question; it is high even at low fidelity, because the question does not require a polished artifact. **Extrinsic value** is the quality and completeness of the artifact itself — its appearance, robustness, and the confidence it gives to external stakeholders. Extrinsic value grows mainly at higher fidelity levels because it depends on how finished the prototype looks and

behaves, not on whether the central question is answered. Build to the fidelity that delivers the intrinsic value you need; extrinsic value follows in later milestones.

Framing every build as an answer to a question keeps the team aligned and prevents the most common prototyping failure: building features before the central question is answered.

3.2 The Seven Stages

Figure 3.2 shows the full Prototype Development Cycle. The seven stages run left to right; Stages 4 through 6 form the core build-test loop that iterates until the central question is answered. The loop is controlled — you exit it on a criterion, not when you run out of time.




Figure 3.2: The seven-stage Prototype Development Cycle with the Design ↔ Validate iteration loop. Stages 4 through 6 form the core build-test loop; iteration is controlled, not ad-hoc.

3.2.1 Stage 1: Specification & Risk

Stage 1 transforms the project brief into a structured set of **specifications** and a ranked list of **risks**. You are not designing anything yet. You are reading, asking questions, and writing.

A specification at this stage has four components:

1. *Functional requirements* — what the system must do (“sort at ≥ 6 items/min”).
2. *Performance bounds* — measurable thresholds (“ $\geq 95\%$ accuracy”, “MQTT round-trip ≤ 200 ms”).
3. *Constraints* — non-negotiable limits (“BOM cost $\leq \$500$ CAD”, “fits on a 600 mm bench conveyor”).
4. *Assumptions* — things believed to be true but not yet measured.

Every assumption in item 4 is a risk candidate. You rank risks by the product of probability and impact, and you identify which prototype stage will retire each one. By the end of Stage 1 you have a written specification document and a risk register. These are the two artifacts that every subsequent stage references.

3.2.1.0.1 In Practice. A one-hour specification session with your full team at the whiteboard saves more time than a week of uncoordinated building. Force every team member to write at least one assumption. Assumptions that no one writes down are the ones that kill projects in Week 10.

3.2.2 Stage 2: Scoping & Planning

Stage 2 converts the risk register into a prototype plan. You decide: which risks must be retired by this prototype, what fidelity level is sufficient to retire them, how long the build will take, and what success looks like.

The key output is a **prototype plan** with:

- The central question (one sentence).
- The chosen fidelity level and justification.
- A work-breakdown with task ownership and duration.
- Explicit pass/fail criteria for the validation step.

Scoping means saying “not this prototype.” If the question is about sort accuracy, the housing material is out of scope. Resist the urge to answer every question at once; you will get a chance in the next milestone. A well-scoped prototype plan is a document your supervisor can review in ten minutes and approve or correct before your team spends any build time — and it is the key output that justifies a Gate 2 approval; Chapter 4 develops it into a full specification and risk register.

3.2.3 Stage 3: Architecture

Stage 3 partitions the system into **subsystems** with defined interfaces. You are not selecting components yet; you are drawing boundaries.

A useful architecture diagram shows:

- Each subsystem as a labelled block.
- Every signal and power interface as an arrow with direction and type (digital, analog, mechanical, protocol name).
- The measurement points where validation data will be collected.

The architecture is the contract between team members. If two people are building adjacent subsystems without an agreed interface, integration will fail. In Stage 3 you negotiate and document those contracts before anyone starts detailed design.

The architecture also determines which subsystem risks can be tested independently. If sort accuracy depends on both the sensor subsystem and the conveyor speed controller, you cannot test one without the other — and your plan must reflect that coupling.

3.2.4 Stage 4: Subsystem Design

Stage 4 is detailed design: component selection, schematic capture, firmware architecture, mechanical part design, and BOM costing. This is where your prior coursework in PCB design, embedded programming, and mechanical CAD becomes the primary activity.

In a prototype context, Stage 4 output does not need to be production-ready. A breadboard schematic is a legitimate Stage 4 artifact if it enables the Stage 5 build to proceed and the Stage 6 measurement to be valid. Keep every design decision traceable to a specification line or a risk item. If you cannot trace it, question whether you need it.

Stage 4 is the entry point to the Design $\leftrightarrow$ Validate loop described in Section 3.3. You design at the subsystem level, build the subsystem, measure it, and return to design if the measurement fails — before integrating with adjacent subsystems.

3.2.5 Stage 5: Build & Integration

Stage 5 is fabrication and assembly: soldering, 3D printing, firmware flashing, wiring, and bringing subsystems together at their defined interfaces.

Integration is a distinct activity from subsystem build. Subsystems that each pass their individual tests routinely fail at integration because interface assumptions were wrong. Run integration in a defined order: bring up the simplest subsystem first, verify its standalone behaviour, then attach the next subsystem and re-verify the combined behaviour before adding the third.

Document every deviation from the Stage 4 design as it happens; post-hoc reconstruction from memory is unreliable and undermines the entire design stage.

3.2.5.0.1 In Practice. Keep a shared build log — a shared document or a lab notebook photographed daily — recording what was built, what changed from the design, and any anomalies observed. The build log is the evidence that your Stage 6 validation measurements are trustworthy.

3.2.6 Stage 6: Validate & Measure

Stage 6 is where you answer the question you wrote in Stage 2. **Validation** is a structured measurement campaign against the pass/fail criteria defined before you built anything.

A valid measurement has:

- A defined test procedure that a second engineer can reproduce.
- Sufficient repetitions to estimate uncertainty (minimum 10 trials for a binary outcome like “sort correct/incorrect”).

- Documented environmental conditions (supply voltage, temperature, Wi-Fi signal strength, conveyor belt load).
- A recorded outcome: pass, fail, or inconclusive with reason.

If the outcome is “pass,” you exit the loop and proceed to Stage 7. If the outcome is “fail,” you return to Stage 4 with a specific design change hypothesis, not a vague intention to “try something different.” This controlled return is what distinguishes disciplined iteration from thrashing.

3.2.7 Stage 7: Compile & Economics

Stage 7 closes the prototype milestone. You compile the evidence: test results, BOM cost actuals, build time log, and a comparison of achieved performance against specification. You then assess the economic implications.

For a commercial project, Stage 7 includes a preliminary **unit economics** analysis: does the validated BOM cost, at the production volume assumed in the business model, support the target margin? For the running example — a 12-person start-up with a Hardware-as-a-Service model, price $p = \$1,200$ CAD, and variable cost $c_{\text{var}} = \$480$ CAD — the contribution margin per unit is:

$$m = p - c_{\text{var}} = \$1,200 - \$480 = \$720 \text{ CAD} \quad (3.1)$$

If the BOM comes in above \$500 CAD target, Stage 7 flags that the economics are compromised before the team invests in Milestone 2 tooling. Stage 7 also produces the **go/no-go recommendation** for the next milestone and a list of risks that remain open. This recommendation is the prototype-evidence component of the Gate 3 decision: the project proceeds to Stage 3 development only if the Stage 7 compilation supports it.

3.3 The Controlled Iteration Loop (Design ↔ Validate)

Stages 4, 5, and 6 form a loop. The loop is necessary because prototypes reveal information that design alone cannot predict: a sensor saturates at lower ambient light than the datasheet implied, firmware interrupt latency is 40% higher than estimated, a 3D-printed bracket flexes under motor torque. Iteration is not a sign of poor planning; it is the mechanism by which prototyping generates knowledge.

What must be controlled is *how* you iterate.

Uncontrolled iteration looks like this: the test fails, someone changes three things simultaneously, the next test passes, and no one knows which change fixed the problem. This is common; it is also useless as engineering knowledge, because you cannot reproduce the fix reliably or explain it to a manufacturing partner.

Controlled iteration imposes two rules:

1. *One variable at a time.* When a measurement fails, form a hypothesis about the cause, change exactly one design element, and re-measure. If you must

change two things to make the system testable, document the dependency explicitly.

2. *Exit on a criterion, not on a deadline.* Define in Stage 2 what “good enough” means. Exit the loop when the measurement meets that criterion. Do not exit because the schedule says so without recording which criteria remain unmet.

Every pass through the loop should reduce uncertainty by answering a smaller sub-question. If you cannot name the sub-question before you change something, you are not iterating — you are guessing.

3.3.0.0.1 In Practice. Limit yourself to three full loop passes before calling a team checkpoint. If after three passes the central question is not answered, the problem is likely in the scope, the architecture, or the specification — not in the build. Step back to Stage 2 or Stage 3 rather than continuing to iterate at Stage 4.

3.4 Prototype Types

Not all prototypes serve the same purpose. Selecting the right type for your question prevents over-building and keeps the team focused. The four primary types used in engineering product development are:

Proof-of-Concept (PoC) Answers a binary feasibility question: can the physics work? Appearance is irrelevant. A PoC uses whatever materials are fastest to assemble — breadboards, hook-up wire, 3D-printed brackets, off-the-shelf modules. Target fidelity: Level 1 or 2.

Functional prototype Demonstrates that the system performs its core function in representative conditions. Appearance may still be a mock-up. Firmware is real but not hardened. Used to answer “does it work under realistic operating conditions?” Target fidelity: Level 3.

Looks-like/works-like prototype Combines representative form and full function. Housing geometry, interface locations, and weight approach final product. Used to answer “is the user experience acceptable?” and “can we hit the cost target?” Target fidelity: Level 4.

Pre-production prototype Built from production-intent processes: PCB from the chosen contract manufacturer, housing from production tooling, firmware at release candidate version. Answers: “will this survive the factory and the field?” Target fidelity: Level 5.

Choosing a looks-like/works-like prototype to answer a feasibility question is the most common and most expensive mistake in early-stage product development. Match the type to the question first; fidelity follows from type.

3.5 Fidelity Matched to the Question

Fidelity is the degree to which a prototype resembles and performs like the final product. Higher fidelity costs more. The cost growth is not linear.

Figure 3.3 shows relative effort plotted against fidelity level. The relationship is approximately exponential.

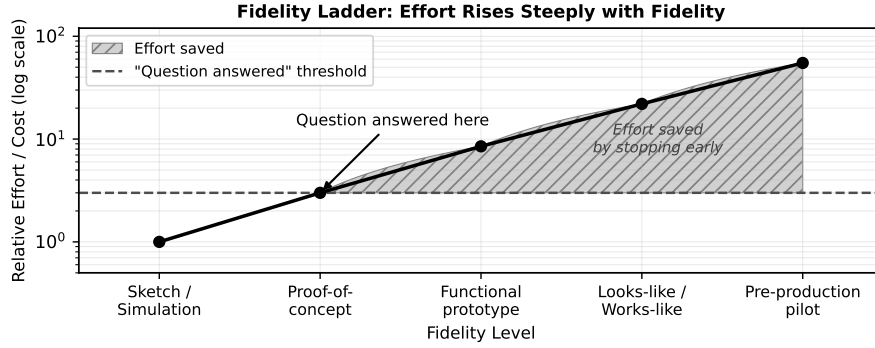


Figure 3.3: Relative effort rises steeply with fidelity level. A proof-of-concept (Level 2) answers many questions at a fraction of the cost of a looks-like/works-like prototype (Level 4).

3.5.1 The Effort–Fidelity Model

Let $f \in \{1, 2, 3, 4, 5\}$ be the fidelity level, where $f = 1$ is a hand sketch or simulation and $f = 5$ is a pre-production prototype built with production-intent processes. Define **relative effort** $E(f)$ as:

$$E(f) = E_0 \cdot k^f, \quad k > 1 \quad (3.2)$$

where E_0 is a baseline effort constant and k is the per-level effort multiplier. The model captures the empirical observation that each fidelity step requires roughly k times the total effort of the step below it, because higher fidelity demands tighter tolerances, more sophisticated tooling, more thorough testing, and more documentation.

3.5.1.1 Effort Table

Set $E_0 = 1$ and $k = 2.5$ as representative values. Table 3.1 shows the resulting effort at each level.

The ratio of effort at $f = 5$ relative to $f = 2$ is:

$$\frac{E(5)}{E(2)} = \frac{k^5}{k^2} = k^3 = 2.5^3 = 15.6 \quad (3.3)$$

If your question is answered at $f = 2$, building to $f = 5$ multiplies your effort by 15.6×. Equivalently, $\frac{E(5) - E(2)}{E(5)} \approx 93\%$ of the total $f = 5$ effort is *spent after the question is already answered*. That is the waste the fidelity discipline prevents.

Table 3.1: Relative effort $E(f) = 2.5^f$ for fidelity levels 1 through 5.

Level f	Type	Relative Effort $E(f)$
1	Sketch / simulation	$2.5^1 = 2.5$
2	Proof-of-concept	$2.5^2 = 6.25$
3	Functional prototype	$2.5^3 = 15.6$
4	Looks-like/works-like	$2.5^4 = 39.1$
5	Pre-production	$2.5^5 = 97.7$

3.5.2 Running Example: Choosing Fidelity for the Sorter

Return to the central question for the connected IoT robotic sorting subsystem:

“Can a sub-\$500 CAD BOM sorter module achieve $\geq 95\%$ sort accuracy at 6 items/min with reliable MQTT connectivity over standard Wi-Fi?”

The team is deciding between two prototype options:

Option A — Looks-like/works-like ($f = 4$): Custom PCB with production layout, injection-moulded housing mock-up, full production firmware with over-the-air update support. Estimated build time: 14 weeks.

Option B — Proof-of-concept ($f = 2$): Breadboard electronics, 3D-printed mounting bracket, firmware with sort accuracy event logging, Wi-Fi MQTT connectivity test. Estimated build time: 3 weeks.

Applying the effort model with $k = 2.5$:

$$E(4) = k^4 = 2.5^4 = 39.1 \quad (\text{Option A effort})$$

$$E(2) = k^2 = 2.5^2 = 6.25 \quad (\text{Option B effort})$$

$$\frac{E(4)}{E(2)} = k^{4-2} = 2.5^2 = 6.25 \quad (3.4)$$

The fraction of Option A’s effort consumed *after* the question is already answerable at Level 2 is:

$$\frac{E(4) - E(2)}{E(4)} = \frac{39.1 - 6.25}{39.1} \approx 0.84 \quad (84\%). \quad (3.5)$$

If a team’s build estimate is T weeks for Option A, Option B requires $T \times E(2)/E(4) = T/6.25$ weeks. For the 14-week Option A estimate: $14/6.25 \approx 2.2$ weeks — close to the stated 3-week Option B estimate (the difference reflects real project overhead not captured by the model).

Option A requires $6.25 \times$ the effort of Option B. Now ask: does the central question require $f = 4$? The question asks about sort accuracy, throughput rate, BOM cost, and MQTT connectivity. None of those require an injection-moulded housing or a production PCB. A breadboard can deliver accurate sensor readings; a 3D-printed bracket can hold the actuator at the required geometry; a Wi-Fi module on a breadboard can carry MQTT traffic.

The decision is Option B. If Option B answers “yes,” the team proceeds to Milestone 2 with the validated architecture, and Option A becomes the correct investment at that stage. If Option B answers “no” — the sort accuracy is 78% at 6 items/min, or the MQTT latency is unacceptable on a congested network — the team has lost 3 weeks, not 14. The cost of a wrong hypothesis is bounded by the fidelity choice.

3.6 The Documentation Layer

Every stage of the Prototype Development Cycle produces a document. This is not administrative overhead — it is the mechanism by which the prototype generates knowledge that survives beyond the build. A result that is not recorded is a result that will be repeated, at full cost, by the next engineer who faces the same question.

Stage 1 produces the specification and risk register. **Stage 2** produces the prototype plan with pass/fail criteria. **Stage 3** produces the architecture diagram and interface table. **Stage 4** produces schematics, firmware architecture notes, and the BOM; any deviation from the plan is noted here. **Stage 5** produces the build log: what was assembled, what changed from Stage 4, and photographs of key assembly steps. **Stage 6** produces the test procedure, raw data table, and the pass/fail verdict with reasoning. **Stage 7** produces the portfolio entry: test results, cost actuals, and the go/no-go recommendation.

The documentation is not assembled at the end of the milestone. It is produced at each stage, incrementally, so that the portfolio at Stage 7 requires only compilation, not reconstruction from memory. If you find yourself writing Stage 1 documentation in Week 11, the process has already failed. The portfolio you submit at Milestone 3 is exactly the set of documents you produced at each stage — nothing more, nothing less.

3.6.0.0.1 Common Pitfalls.

- **“Prototype = mini-product.”** Building all product features when only one needs to be proved is the most common and most expensive prototyping error. Injection moulding, CE certification, and production firmware are irrelevant at Stage 4 if the question is about sort accuracy. Every feature you build beyond what the question requires is pure waste until the question is answered.
- **“Higher fidelity is always better.”** Fidelity costs effort exponentially, as shown in Table 3.1. A higher-fidelity prototype that cannot yet answer the question delivers zero additional information — it only consumes schedule and budget. Match fidelity to the question; resist the instinct to impress.

Review Questions

1. **(Conceptual)** List the seven stages of the Prototype Development Cycle in order. For Stage 1 and Stage 6, state the primary output that stage produces.

2. **(Conceptual)** Distinguish **intrinsic value** from **extrinsic value** in the context of a prototype. Which type does a proof-of-concept maximise, and why does that make it appropriate for answering a central technical question?
3. **(Applied — calculation)** Using $E(f) = E_0 \cdot k^f$ with $E_0 = 1$ and $k = 3.0$:
 - (a) Compute $E(f)$ for $f = 1, 2, 3, 4, 5$.
 - (b) What is the ratio $E(4)/E(2)$?
 - (c) If a question is answered at $f = 2$, what fraction of the Level-4 effort is saved?
4. **(Applied — decision)** A team must verify that a custom MEMS pressure sensor achieves ± 0.5 Pa accuracy when integrated with their MCU at -20°C .
 - (a) Identify the most appropriate prototype type from §3.4.
 - (b) State the fidelity level from §3.5 and justify the choice in one sentence.
 - (c) If the PoC result is inconclusive — accuracy is within spec at some temperatures but not others — describe one controlled iteration step you would take at Stage 4 before changing the fidelity level.
5. **(Applied — multi-step)** A team estimates 20 weeks to build a pre-production prototype ($f = 5$) at a weekly cost of \$3,500 CAD. Using $k = 2.5$, $E_0 = 1$:
 - (a) Compute $E(2)$ and $E(5)$.
 - (b) What fraction of the 20-week effort corresponds to $f = 2$?
 - (c) How many weeks does the PoC take (round to one decimal place)?
 - (d) How much money is saved by stopping at $f = 2$ if the question is answered there?

Try It Yourself

A firmware team must choose between two prototype options to validate their custom RTOS scheduler under worst-case interrupt load. Both options use $E_0 = 1$ and $k = 3.0$.

Option X — Proof-of-concept ($f = 2$): A minimal test harness running the scheduler on target hardware with synthetic interrupt injection. Estimated build time: 2 weeks.

Option Y — Functional prototype ($f = 3$): Full firmware stack with all application tasks active, running the complete RTOS configuration. Estimated build time: 9 weeks.

1. Compute $E(2)$ and $E(3)$ using $E(f) = E_0 \cdot k^f$.
2. Find the effort ratio $E(3)/E(2)$.
3. Compute the fraction of Option Y effort consumed after the question is already answerable at $f = 2$ (use the formula from Equation 3.5).
4. The central question is: “Does the scheduler meet the 1 ms worst-case interrupt latency under full task load?” State in one sentence whether Option X or Option Y is the correct choice and why, referencing the effort ratio.

(No answer key provided.)

Portfolio Entry

The deliverable for this chapter is a single written paragraph, submitted to your portfolio, stating: (1) the central question your Milestone 1 prototype will answer, (2) the fidelity level you have chosen, and (3) a justification for that choice in terms of the question, the risk it retires, and the effort saved relative to the next higher fidelity level. This statement is your Milestone 1 prototype scope; submit it as the prototype-evidence component of your Gate 2 package in Week 4.

Running-Example Statement (model your own on this):

The Milestone 1 prototype for the IoT robotic sorting subsystem will answer the following central question: *“Can a sub-\$500 CAD BOM sorter module achieve $\geq 95\%$ sort accuracy at 6 items/min with reliable MQTT connectivity over standard Wi-Fi?”* The chosen fidelity is Level 2 (proof-of-concept), implemented as breadboard electronics, a 3D-printed mechanical mounting bracket, and firmware with sort-event data logging and Wi-Fi MQTT connectivity. This fidelity is sufficient because the question is about sensor accuracy, actuator throughput, and network protocol performance — none of which require a production PCB layout or an enclosure. Advancing to Level 4 at this stage would multiply effort by $6.25\times$ (Equation 3.4) before the feasibility of the core mechanism is established. If the Level 2 prototype answers “yes,” Level 4 is the justified next investment; if “no,” the team reframes the architecture having lost 3 weeks rather than 14.

This statement feeds directly into the specification document you will develop in Chapter 4. Keep it in your portfolio; you will reference and refine it at each subsequent milestone.

Chapter Summary

A prototype is the minimum sufficient artifact that answers a specific technical or business question and retires a corresponding risk. The Prototype Development Cycle organises that work into seven stages: Stage 1 (Specification & Risk) establishes what must be true and what is assumed; Stage 2 (Scoping & Planning) sets the question, the fidelity, and the success criterion; Stage 3 (Architecture) partitions the system into subsystems with defined interfaces; Stage 4 (Subsystem Design) produces the design artefacts; Stage 5 (Build & Integration) realises and assembles those designs; Stage 6 (Validate & Measure) answers the question against pre-defined criteria; and Stage 7 (Compile & Economics) closes the milestone with evidence and a go/no-go recommendation.

Stages 4 through 6 form a controlled iteration loop. Each pass tests one hypothesis, changes one variable, and exits on a measured criterion — not on a deadline and not by accumulated intuition.

Fidelity is not a virtue. It is a variable you set to the minimum level that makes the central question answerable. The effort–fidelity relationship is exponential ($E(f) =$

$E_0 \cdot k^f$), so every unnecessary fidelity level you add multiplies your cost by k before you have an answer. For the sorter running example, choosing Level 2 over Level 4 saves $6.25\times$ the effort on a question whose answer is not yet known.

Transition to Chapter 4. Chapter 4 turns the central question you have just defined into a complete specification and risk register. You will write measurable, testable requirements, separate “what” from “how,” and rank risks using the FMEA risk-priority number — producing the core deliverable of Stage-Gate Stage 2 and the foundation for every subsequent design decision.

SPECIFICATIONS & RISK PRIORITIZATION

4.0.0.0.1 Where this fits. This chapter produces the core deliverable of Stage-Gate Stage 2 (Scoping) — the product specification and risk register that justify a Go decision at Gate 2. The central question and fidelity statement you produced in Chapter 3 define the *goal*; the specification turns that goal into measurable, testable requirements, and the risk register ranks the unknowns the prototype must resolve before Gate 2 can be passed.

The central question you defined in Chapter 3 identifies the goal; this chapter supplies the standard for success — converting that goal into measurable, testable requirements and a ranked risk register using two complementary tools: a simple risk equation and an FMEA Risk Priority Number.

By the end of this chapter you will be able to:

1. write measurable, testable requirements that can unambiguously pass or fail;
2. separate requirements (the *what*) from design decisions (the *how*);
3. build and defend a risk-priority ranking that guides prototype focus; and
4. identify the critical unknown in a set of open assumptions and justify which prototype experiment must be run first.

4.1 Anatomy of a Specification

A specification is a contract between the engineering team and every stakeholder who must eventually verify the product. It answers one question per line: *how will we know we succeeded?* A well-formed specification document contains five distinct element types, each serving a different verification role.

4.1.1 Functional Requirements

A functional requirement states a capability the system must provide, expressed as a verb phrase with a measurable threshold. The threshold is what separates a functional requirement from a vague aspiration.

- **Weak (untestable):** “The system shall sort items quickly.”
- **Strong (testable):** “The system shall classify and divert each item within ≤ 167 ms of entering the sensor gate (throughput ≥ 6 items/min, continuous 1-hour run).”

Every functional requirement must name: (a) the actor or subsystem, (b) the action, (c) the measurable threshold, and (d) the operating condition under which the threshold applies.

4.1.2 Performance Targets

Performance targets quantify quality-of-behaviour: accuracy, latency, bandwidth, efficiency. They differ from functional requirements in that they govern *how well* the function is performed, not merely *whether* it is performed. A sorter that classifies items at 6 items/min but with 40% error satisfies the throughput functional requirement yet fails the accuracy performance target.

4.1.3 Constraints

Constraints are non-negotiable boundaries imposed by physics, regulation, or business. They do not describe desirable behaviour; they eliminate design options outright. Examples: BOM cost $\leq \$500$ CAD (business constraint), supply voltage from USB ≤ 5 V at 2 A (interface constraint), operating temperature 0–50°C (environmental constraint).

4.1.4 Interfaces

Interface specifications describe the boundaries between subsystems, between the product and external systems, and between the product and its users. A mechanical interface names connector types and physical envelope; an electrical interface names voltage levels, connector pinouts, and communication protocols; a software interface names message formats, topics, and timing. Specifying interfaces early prevents integration surprises — the most common source of late-stage schedule overrun.

4.1.5 Acceptance Criteria

Acceptance criteria translate every requirement into a concrete test: apparatus, procedure, pass/fail decision rule. Writing the acceptance test at the same time as the requirement is a discipline check: if you cannot describe how to measure it, the requirement is not yet measurable.

4.1.5.0.1 In Practice. At Vanier’s Product Development Lab, teams have learned to draft acceptance criteria as a three-column table: *Requirement ID*, *Test Procedure* (apparatus + steps), *Pass Condition*. Filling this table during Week 2 surfaces

ambiguous requirements before any hardware is ordered, saving the cost of a re-design sprint.

4.2 Requirements vs. Design

The single most persistent error in student (and professional) specification documents is embedding a design decision inside a requirement. Figure 4.1 shows a side-by-side comparison of requirement and design statements for the same capability.

Requirement (What)	Design (How)
Sort accuracy $\geq 95\%$	VL53L1X ToF sensor + threshold classifier
MQTT latency $\leq 200\text{ ms}$	ESP32 with MQTT over TLS
BOM cost $\leq \$500\text{ CAD}$	STM32F4 + off-shelf motor driver

Figure 4.1: Side-by-side comparison of a requirement statement (left) and a design statement (right) for the same capability. Requirements describe observable, measurable outcomes; design statements prescribe implementation choices.

A useful test: replace the specific implementation with an alternative one. If the requirement is still meaningful, it is a genuine requirement. If it becomes nonsensical, it was a design decision dressed up as a requirement.

- **Requirement:** “Classification results shall be transmitted to the cloud dashboard within $\leq 200\text{ ms}$ of each sort event.” Replacing Wi-Fi with Ethernet or cellular still leaves this requirement meaningful. ✓
- **Design-embedded (invalid):** “The MCU shall use MQTT over Wi-Fi to transmit classification results.” This mandates the implementation, closing off alternatives before the team has evaluated trade-offs. ✗

4.2.1 The “What / How” Discipline

Every line of a specification document should survive the question: “Does this describe what the system must do, or does it describe how we plan to do it?” The *what* belongs in the specification. The *how* belongs in the design document, the architecture diagram, or the BOM — produced *after* requirements are frozen.

4.2.1.0.1 In Practice. When reviewing a teammate’s specification draft, highlight every noun that names a specific component (“Arduino”, “ToF sensor”, “Python”) or a specific topology (“mesh network”, “I²C bus”). Each highlighted phrase is a candidate design decision that may be pre-empting a better alternative. Move it to the design rationale section and restate the requirement in terms of observable behaviour.

4.2.1.0.2 Common Pitfalls.

- **Unmeasurable criteria.** “The system shall be user-friendly” cannot be tested. Restate as: “A first-time operator shall complete initial setup in ≤ 10 minutes following the Quick-Start card, with zero support calls, measured on five naïve participants.”
- **Embedding the solution.** “The sensor shall use a VL53L1X time-of-flight module” is a design choice. The requirement should read: “The sensor subsystem shall detect items up to 300 mm from the gate with ≤ 2 mm resolution at throughput ≥ 6 items/min.”
- **Ambiguous conditions.** A requirement with no stated operating condition is incomplete. “Latency ≤ 200 ms” must specify: under what network load? at what ambient temperature? for what message size?

4.3 Risk-Driven Prioritization

Once requirements exist, the team must decide which risks — failures to meet those requirements — deserve the most engineering attention. Without a principled ranking, you either chase the most visible problem rather than the most dangerous one, or try to mitigate everything simultaneously and mitigate nothing well.

4.3.1 The Basic Risk Equation

The simplest risk model assigns two quantities to each potential failure mode:

- P_{failure} : the estimated probability that the failure occurs in a prototype or field unit, scored 1–10 (1 = very unlikely, 10 = near-certain).
- $C_{\text{consequence}}$: the estimated cost of that failure — in schedule days, dollars, or safety impact — scored 1–10 (1 = trivial, 10 = project-ending).

$$R = P_{\text{failure}} \times C_{\text{consequence}} \quad (4.1)$$

The resulting risk score R ranges from 1 to 100. Teams typically set a threshold (e.g., $R \geq 30$) above which a mitigation plan is mandatory. Figure 4.2 shows a probability–consequence matrix that maps risk scores to action zones.

4.3.2 Limitations of the Two-Factor Model

Equation (4.1) is fast to communicate but conflates two distinct ideas: the probability that a failure occurs and the team’s ability to detect it before it reaches the user. Section 4.4 adds detection as a third factor.

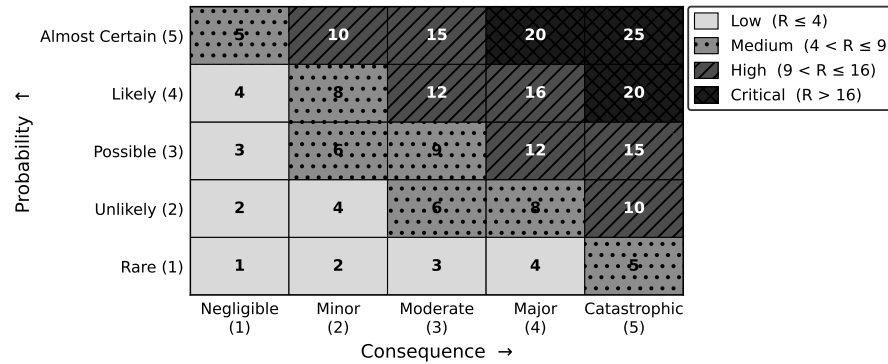


Figure 4.2: Probability × consequence risk matrix for the running example. Cells with $R \geq 30$ fall in the red action zone; $15 \leq R < 30$ in the amber watch zone; $R < 15$ in the green monitor zone.

4.4 FMEA-Style Ranking (RPN)

Failure Mode and Effects Analysis (FMEA) is a structured method for systematically enumerating every way a system can fail, estimating three quantities for each failure mode, and computing a Risk Priority Number to guide mitigation effort.

4.4.1 The RPN Formula

$$\text{RPN} = S \cdot O \cdot D \quad (4.2)$$

where:

- S = Severity (1–10): how bad is the consequence if the failure reaches the user?
- O = Occurrence (1–10): how likely is the failure to occur during normal operation?
- D = Detection (1–10): how difficult is it to detect the failure before it affects the user? *Note: a higher D score means harder to detect.*

RPN ranges from 1 to 1,000. Unlike the two-factor risk score R , the RPN captures the value of test coverage: a team that adds a robust bench test lowers D and therefore lowers RPN even without changing the underlying design.

4.4.1.0.1 In Practice. Industry FMEA tables typically flag $\text{RPN} \geq 100$ as requiring a documented corrective action, and $\text{RPN} \geq 200$ as requiring a design change before release. For a student prototype, a lighter threshold — flag $\text{RPN} \geq 80$ — is appropriate, because prototype runs are short and failures are recoverable. These are the failure modes you must address before your Gate 2 submission.

4.4.2 Scale Anchors

Table 4.1 gives representative scale anchors for S, O, and D as used in this course. Teams should agree on anchors *before* scoring to prevent rater drift.

Table 4.1: Representative 10-point scale anchors for FMEA scoring in a prototype context.

Score	Severity (S)	Occurrence (O)	Detection (D)
1–2	No user impact	Rare (<1 in 1,000 runs)	Immediately obvious; alarms fire
3–4	Minor degradation	Occasional (~1 in 100 runs)	Detectable by inspection or log
5–6	Partial loss of function	Moderate (~1 in 20 runs)	Detectable only with test setup
7–8	Major loss of function	Frequent (~1 in 5 runs)	Difficult; requires special tool
9–10	Safety / total failure	Near-certain (>1 in 2 runs)	Cannot be detected before impact

4.5 The Critical Path of Unknowns

The risk register produced by FMEA answers *which* risks are largest. A separate but related question is *which risks must be resolved first* — because some unknowns block progress on every other subsystem. This is the critical path of unknowns.

Figure 4.3 illustrates the assumption list and dependency arrows for the running example. The highest-RPN item that *also* blocks downstream work defines the prototype’s first experiment.

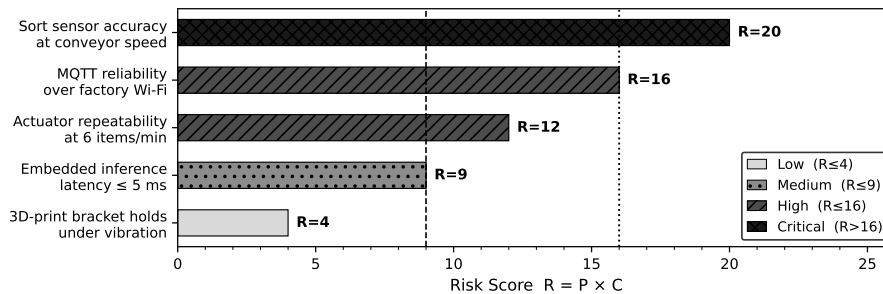


Figure 4.3: Critical unknowns and assumption dependency map for the IoT robotic sorting subsystem. Arrows show which assumptions must be resolved before dependent subsystem work can begin. The sort-sensor assumption (shaded) lies on the critical path because both the divert actuator timing and the firmware logic depend on its output format.

4.5.1 Identifying the Critical Unknown

To find the critical unknown, list every open assumption in the risk register and ask two questions for each:

1. If this assumption turns out to be false, how many other subsystems must change? (Coupling score.)
2. How quickly can we resolve it with a targeted experiment? (Resolvability score.)

An assumption with high coupling and low resolvability is both dangerous and slow to clear — it should head the prototype schedule. An assumption with high coupling but high resolvability should be the *first* experiment run, because a quick test removes the blocker cheaply.

4.5.1.0.1 In Practice. For the IoT sorter, the sort-sensor detection principle (time-of-flight vs. break-beam vs. vision) is the critical unknown: the firmware state machine, the actuator timing, and the MQTT payload format all depend on what the sensor outputs. Running a 48-hour bench test of candidate sensors *before* ordering actuator parts avoids a costly mid-sprint pivot.

4.6 Worked Example: IoT Robotic Sorting Subsystem

This section walks through the full specification and risk-ranking workflow for the running example established in Chapter 3: a connected IoT robotic sorting subsystem classifying and diverting items on a bench conveyor, reporting over MQTT/Wi-Fi, with a target BOM of $\leq \$500$ CAD and a sort accuracy of $\geq 95\%$.

4.6.1 Step 1: Convert Vague Wishes into Measurable Requirements

The team's initial wish list contained five phrases typical of early ideation. Table 4.2 shows each vague phrase converted to a testable requirement.

The most instructive conversion is “fast”:

- **Vague:** “The system shall process sensor data fast.”
- **Step 1 — name the quantity:** Processing speed is measured in samples per second (kS/s) and as end-to-end latency (ms).
- **Step 2 — anchor to the use case:** At 6 items/min, one item arrives every $60\text{ s}/6 = 10\text{ s}$. A single sort event reads one sensor frame, runs the classifier, and commands the actuator. The conveyor belt speed is 50 mm/s and the item window at the gate is 50 mm, giving a gate dwell time of $50\text{ mm} \div 50\text{ mm/s} = 1,000\text{ ms}$. The actuator must fire within that window.
- **Step 3 — allocate the budget:** Budget allocation: sensor read 1 ms, classifier 2 ms, actuator command 2 ms, margin 995 ms.

$$t_{\text{firmware}} = 1\text{ ms} + 2\text{ ms} + 2\text{ ms} = 5\text{ ms}. \quad (4.3)$$

The remaining $1,000 - 5 = 995\text{ ms}$ is dwell-time margin before the next item enters the gate. Conservatively, the end-to-end firmware latency budget is $\leq 5\text{ ms}$. At a 10 kS/s ADC rate, the sensor delivers 10,000 samples per second; one classification frame uses 10 samples, costing $10/10,000 = 1\text{ ms}$ — within budget.

- **Measurable requirement:** “The MCU firmware shall process one classification event (sensor read + classification + actuator command) within $\leq 5\text{ ms}$, measured from sensor-trigger interrupt to actuator-enable GPIO, at a sustained rate of $\geq 10\text{ kS/s}$ sensor sampling.”

Table 4.2: Vague feature wishes converted to measurable, testable requirements for the IoT robotic sorting subsystem. Each requirement identifies actor, action, threshold, and operating condition.

Vague Wish	Measurable Requirement	ID
"Sorts accurately"	The system shall classify items with $\geq 95\%$ accuracy (correct class / total items) over a continuous 100-item run at nominal belt speed.	REQ-01
"Fast"	The MCU firmware shall complete one classification event within ≤ 5 ms (sensor read + classify + actuator command) at ≥ 10 kS/s sensor sampling.	REQ-02
"Enough throughput"	The system shall sustain ≥ 6 items/min throughput for ≥ 60 min without thermal throttling or error accumulation.	REQ-03
"Sends data to the cloud"	Each sort-event MQTT message shall be delivered to the broker within ≤ 200 ms of the sort event, on a 2.4 GHz Wi-Fi network with ≥ -70 dBm RSSI.	REQ-04
"Affordable"	The total prototype BOM (all purchased components) shall not exceed \$500 CAD.	REQ-05

A sixth implied constraint (power) is added from the hardware context:

CON-01: Total system power draw shall not exceed 5 W when powered from a single USB-C port (5 V, 2 A = 10 W; 5 W provides 50% margin for host compatibility).

4.6.2 Step 2: Compute RPN for Three Subsystems

The team identifies three high-risk subsystems from the Chapter 3 scoping exercise: (A) Sort Sensor, (B) MQTT/Wi-Fi Integration, (C) Divert Actuator. For each, the team identifies the primary failure mode, scores *S*, *O*, and *D* on the 1–10 scale from Table 4.1, and computes RPN using Equation (4.2).

Subsystem A — Sort Sensor

- **Failure mode:** Sensor misclassifies item class (false positive or false negative), causing a sort error.
- **Severity (*S*):** A miss ships a wrong item — significant product defect, customer complaint, possible recall. $S = 8$.
- **Occurrence (*O*):** Time-of-flight at < 300 mm with a 50 mm/s belt is a moderately proven technique; reflectivity variation across item surface adds uncertainty. $O = 5$.
- **Detection (*D*):** A classification error is visible in the sort log and confirmed by counting missorted bins at end of run — easily detected during bench test. $D = 2$.

- **RPN:**

$$\text{RPN}_A = S \cdot O \cdot D = 8 \times 5 \times 2 = \mathbf{80}$$

Subsystem B — MQTT/Wi-Fi Integration

- **Failure mode:** MQTT message delivery latency exceeds 200 ms, causing dashboard staleness and potential missed alerts.
- **Severity (S):** Stale dashboard undermines the product's core value proposition (real-time visibility); does not stop physical sorting. $S = 7$.
- **Occurrence (O):** 2.4 GHz Wi-Fi in a lab environment with competing devices experiences frequent retransmissions; MQTT QoS 1 adds handshake overhead. $O = 6$.
- **Detection (D):** Latency can be measured by timestamping publish and subscribe events in the broker log — detectable but requires setup of a monitoring script. $D = 4$.
- **RPN:**

$$\text{RPN}_B = S \cdot O \cdot D = 7 \times 6 \times 4 = \mathbf{168}$$

Subsystem C — Divert Actuator

- **Failure mode:** Actuator fires too late or with insufficient force, failing to divert the item before it exits the gate.
- **Severity (S):** A missed divert is a sort error — same consequence as a sensor misclassification. $S = 8$.
- **Occurrence (O):** Servo or solenoid timing within a 1,000 ms dwell window is well within typical MCU PWM capability; mechanical linkage adds some uncertainty. $O = 3$.
- **Detection (D):** A missed divert is observable by watching the output bins or reading a secondary confirmation sensor — straightforward detection. $D = 2$.
- **RPN:**

$$\text{RPN}_C = S \cdot O \cdot D = 8 \times 3 \times 2 = \mathbf{48}$$

4.6.3 Step 3: Rank and Interpret

Table 4.3 summarises the three RPN scores and maps each to a mitigation action.

Table 4.3: FMEA Risk Priority Number ranking for the three prototype subsystems of the IoT robotic sorting subsystem. RPN computed using Equation (4.2). Subsystems are sorted by descending RPN.

Rank	Subsystem	Failure Mode	S	O	D	RPN	Action
1	MQTT/Wi-Fi	Latency >200 ms	7	6	4	168	Redesign / mitigate
2	Sort Sensor	Misclassification	8	5	2	80	Monitor / mitigate
3	Divert Actuator	Late divert	8	3	2	48	Monitor

Interpretation:

- MQTT/Wi-Fi integration (RPN = 168) is the highest-risk subsystem. The team should prototype and stress-test the Wi-Fi + MQTT stack *first*, before investing time in actuator tuning. Concrete mitigation: run a dedicated latency characterisation script (publish 500 timestamped messages; record broker-side receive timestamp; compute 99th-percentile latency) within Sprint 1.
- Sort Sensor (RPN = 80) exceeds the 80-threshold and requires a documented mitigation plan. The sensor's detection principle should be confirmed in a 100-item accuracy trial before the firmware classifier is written.
- Divert Actuator (RPN = 48) is below the 80-threshold. Standard bench testing during integration is sufficient; no dedicated mitigation sprint is needed.

Applying the basic risk equation (4.1) for cross-check:

$$R_A = P_{\text{failure},A} \times C_{\text{consequence},A} = 5 \times 8 = 40 \quad (\text{action zone})$$

$$R_B = P_{\text{failure},B} \times C_{\text{consequence},B} = 6 \times 7 = 42 \quad (\text{action zone})$$

$$R_C = P_{\text{failure},C} \times C_{\text{consequence},C} = 3 \times 8 = 24 \quad (\text{watch zone})$$

The two-factor scores (4.1) agree with the RPN ranking on the top item (MQTT/Wi-Fi) but obscure the gap between A and B that the detection factor (D) reveals. The sensor is harder to detect as failing, so RPN correctly flags it above the threshold despite its lower occurrence rate.

4.6.4 Try It Yourself

Scenario: A team is developing a **smart irrigation controller** for a rooftop garden. The system reads soil moisture via a capacitive sensor array, decides whether to open a motorised valve, and logs readings to a cloud dashboard over cellular (LTE-M). The initial wish list contains:

- “Waters when needed” — target: soil moisture sensor accuracy $\pm 3\%$ VWC
- “Doesn’t over-water” — target: valve response within 30 s of a moisture threshold crossing
- “Cheap to build” — target: BOM $\leq \$300$ CAD

Your tasks:

1. Rewrite each wish as a measurable requirement following the actor–action–threshold–condition format.
2. Identify three failure modes (one per subsystem: moisture sensor, motorised valve, LTE-M uplink).
3. Assign S , O , and D scores on the 1–10 scale with written justification for each S , O , and D value (nine justifications total: three failure modes $\times$ three dimensions).
4. Compute RPN for each failure mode using Equation (4.2), showing every multiplication step.
5. Rank the three failure modes from highest to lowest RPN and state which subsystem should be prototyped first.

6. For this cross-check, use the O score as P_{failure} and the S score as $C_{\text{consequence}}$, consistent with the worked example convention. Cross-check your top-ranked item using Equation (4.1) and comment on whether the two rankings agree.

Do **not** use the same S , O , D values as the worked example.

Review Questions

1. **(Conceptual)** Explain the difference between a *functional requirement* and a *performance target*, using one example of each from a product domain of your choice. Why must both be present in a complete specification?
2. **(Conceptual)** A colleague argues that specifying the communication protocol (e.g., “shall use Bluetooth Low Energy”) inside a requirement is efficient because it removes ambiguity for the firmware team. Justify why this practice is problematic and describe the correct place in the documentation hierarchy for such a decision.
3. **(Applied — calculation)** A new IoT product team scores three failure modes as follows:
 - Power regulator brown-out: $S = 9$, $O = 2$, $D = 3$
 - Firmware deadlock: $S = 6$, $O = 7$, $D = 8$
 - Enclosure latch failure: $S = 3$, $O = 4$, $D = 1$

Compute RPN for each failure mode using Equation (4.2), showing every multiplication step. Rank them and state which subsystem requires a documented mitigation plan if the threshold is $\text{RPN} \geq 80$.

4. **(Applied — multi-step calculation)** A wearable ECG monitor has a motion-artifact failure mode with the following FMEA scores: Severity $S = 8$, Occurrence $O = 4$, Detection $D = 3$.
 - (a) Compute $R = P_{\text{failure}} \times C_{\text{consequence}}$ (Equation 4.1) using $P_{\text{failure}} = O = 4$ and $C_{\text{consequence}} = S = 8$ as the cross-check convention. Does this failure mode qualify as high-risk ($R > 16$)?
 - (b) Compute the RPN. The team then adds a motion-artifact filter that lowers O from 4 to 2 while S and D remain unchanged. Recompute the RPN and state whether the mitigation moves the failure mode below the RPN threshold of 80.
 - (c) Comment in one sentence on whether the R -score ranking (Part a) and the RPN ranking (Part b) agree.
5. **(Conceptual)** Define the *critical path of unknowns* and explain how it differs from the highest-RPN item in the risk register. Give an example where the highest-RPN item is *not* on the critical path of unknowns and describe what the team should do first.

Portfolio Entry

You produce the core of **Milestone 1: the Proposal** — together these three parts constitute your Gate 2 evidence package, the scoping deliverables that earn a Go decision to proceed with development. The artifact has three interlocking parts:

1. **Specification Table.** A table of 3–5 measurable requirements (functional requirements + performance targets) and any binding constraints, formatted with columns: ID, Requirement Statement, Threshold, Operating Condition, Acceptance Test. Each row must be testable as written.
2. **Risk Register.** An FMEA table listing at least three failure modes (one per high-risk subsystem identified in Chapter 3). Each row contains: Subsystem, Failure Mode, *S*, *O*, *D*, RPN, Rank, and Mitigation Plan. The table is sorted by descending RPN. Failure modes above RPN 80 must have a specific mitigation action tied to a sprint.
3. **Scoping Rationale.** One paragraph (100–150 words) that names: (a) the central prototype question, (b) the highest-risk assumption (the critical unknown), and (c) the first experiment that will resolve that assumption. This paragraph becomes the executive summary of your Milestone 1 submission.

‘What will this thing do, how will you know it works, and what could kill the project?’ — these three parts of the Milestone 1 Proposal answer that investor question directly.

Summary

A specification is a contract: every element — functional requirements, performance targets, constraints, interfaces, and acceptance criteria — must be measurable and testable, or it is not yet a requirement. It established the discipline of separating *what* (requirements) from *how* (design), a distinction that keeps early design choices from foreclosing better alternatives. Two complementary risk tools were presented: the two-factor risk equation $R = P_{\text{failure}} \times C_{\text{consequence}}$ (Equation (4.1)) for rapid stakeholder communication, and the FMEA Risk Priority Number $RPN = S \cdot O \cdot D$ (Equation (4.2)) for engineering-level prioritisation that accounts for detection difficulty. Applied to the IoT robotic sorting subsystem, the analysis ranked MQTT/Wi-Fi integration ($RPN = 168$) as the first prototype target, followed by the sort sensor ($RPN = 80$), and confirmed that the divert actuator ($RPN = 48$) can proceed with standard integration testing.

You now have a specification table, a risk register, and a scoping rationale — the three components of the Milestone 1 Proposal. Chapter 5 takes this artifact as its starting point: the specification defines the required behaviour at each subsystem boundary, and the risk register flags which interfaces carry the highest-consequence unknowns. Chapter 5 shows how to decompose the system into subsystems, define the interfaces between them, and produce the architecture diagram that makes integration testable.

SYSTEM ARCHITECTURE & INTERFACE DEFINITION

5.0.0.0.1 Where this fits. You are now between Stage-Gate Stage 2 and Stage 3. Chapter 4 produced a specification and a risk register: you know *what* the prototype must do and which unknowns carry the highest risk — but not yet *how* to partition that specification into subsystems with verified boundaries. This chapter produces the next mandatory input to Gate 3 — the system architecture and interface table. Before you order a single component or write a single line of firmware, you must decompose your specification into subsystems and write down exactly what each subsystem promises to deliver to the next one. Architecture decisions made here are dramatically cheaper to change than the same decisions discovered at integration. A sound architecture is a prerequisite for an honest Gate 3 business case: if the blocks do not fit together on paper, they will not fit together on the bench.

By the end of this chapter you will be able to:

1. decompose a prototype specification into subsystems across the four domains: electronics, mechanical, firmware, and AI/IoT/robotic logic;
2. specify **interface contracts** that define the electrical, mechanical, data, and timing properties at each subsystem boundary;
3. allocate timing, power, and error budgets across subsystems and verify that the system total satisfies the specification; and
4. justify which subsystem boundary in a given architecture carries the highest integration risk by applying the detection and severity criteria from Chapter 4's FMEA framework.

5.1 Decomposition

Decomposition is the act of partitioning a system specification into a set of subsystems, each responsible for a bounded, well-defined portion of the total behaviour. Done well, decomposition gives every team member a clear scope and makes the integration task predictable. Done poorly — or skipped entirely — it produces a monolithic prototype where every bug is a whole-system bug and no one is sure whose responsibility the failure is.

The discipline in this course groups prototype subsystems into four domains. Together they cover every boundary that a typical mechatronic, IoT, or robotic prototype will cross.

5.1.1 The Four Domains

5.1.1.1 Electronics

The **electronics subsystem** includes all hardware that converts physical quantities into digital signals and provides power conditioning for the rest of the system. In the running-example sorter this domain contains the item-detection sensor (time-of-flight or photoelectric), the camera or vision sensor feeding the AI pipeline, the microcontroller unit (MCU), motor drivers, and the power supply rail. Typical deliverables from this domain: a schematic, a net list, a power-rail diagram, and connector pinouts at every physical boundary.

5.1.1.2 Mechanical

The **mechanical subsystem** governs physical structure and motion: frame, conveyor belt, diverter actuator, mounting provisions for sensors and electronics, and the enclosure. In the prototype scope established in Chapter 2, the housing is functional-minimum — sufficient to hold the electronics securely and at the correct sensor geometry, but not production-finished. Mechanical deliverables: dimensional drawings for custom parts, assembly sequence, and the mechanical interface dimensions at every point where electronics or firmware interact with moving parts.

5.1.1.3 Firmware

The **firmware subsystem** is the embedded software running on the MCU. Its responsibilities are: reading the sensor, scheduling the AI inference call, issuing the actuator command, and publishing the MQTT status message. For the running-example sorter, the timing budget from Chapter 4 constrains this domain directly: the firmware must complete the entire sensor-to-actuator pipeline within 5 ms (established in Chapter 4 and formalised as Equation 5.1 in Section 5.3). Firmware deliverables: a task or interrupt map, a state-machine diagram, and a timing annotation for every I/O transaction.

5.1.1.4 AI/IoT/Robotic Logic

The **AI/IoT/robotic logic subsystem** encompasses the classification algorithm (the AI inference engine), the MQTT broker connection, and any cloud-side dashboard or data logging. This is the layer that gives the prototype its intelligence: the ability to distinguish item classes and to report status remotely. For the running example, the central question from Chapter 3 — can the sub-\$500 CAD BOM sorter achieve $\geq 95\%$ sort accuracy at 6 items/min with MQTT status reporting? — is answered primarily by this domain, in concert with the electronics sensor quality. Deliverables:

model architecture summary, inference-time benchmark, MQTT topic map, and QoS configuration.

5.1.2 Drawing the Block Diagram

The output of decomposition is a **system block diagram**: one box per subsystem, one labelled arrow per interaction. Figure 5.1 shows the block diagram for the running-example sorter. Every arrow in that figure will become one row in the interface table you will build by the end of this chapter.

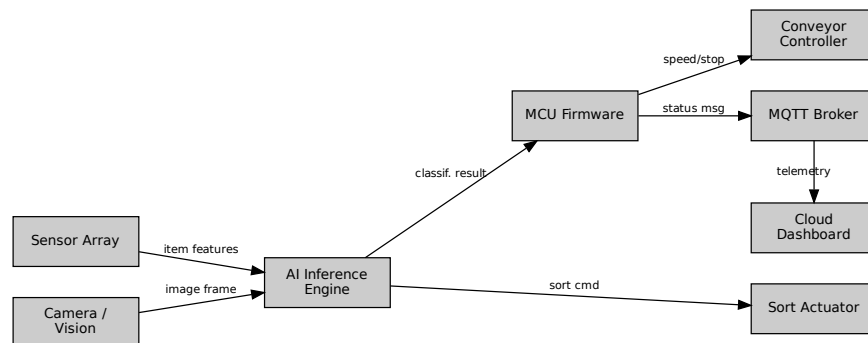


Figure 5.1: System block diagram for the IoT robotic sorting prototype. Boxes represent subsystems across the four domains; arrows represent interface boundaries, each of which receives a contract in Table 5.1. Labels A–D correspond to the four interface types introduced in Section 5.2.

5.1.2.0.1 In Practice. At the start of a team project, produce the block diagram before any other technical document. Pin it to the shared drive or project wall. Every team member should be able to point to their box and describe exactly what enters and exits it. A one-page interface table built from this diagram is the single most effective tool for keeping all team members building to the same specification. When everyone can see the same table, “I assumed it would be 3.3 V” is no longer a valid explanation for a three-day debugging sprint.

5.1.2.0.2 Common Pitfalls.

- **Starting the interesting subsystem before interfaces are fixed.** Firmware and AI engineers are often eager to write code before the electrical interfaces are settled. If the UART voltage level has not been agreed upon, any firmware written against an assumed level may be wrong, and the rework cost is real schedule time.
- **Treating the block diagram as decoration.** A block diagram that lives in a report appendix and is never referenced during build is not doing its job. It must be a living, binding contract — updated any time a subsystem boundary changes, and consulted before any interface-crossing code or hardware is designed.
- **Verbal interface agreements.** “We’ll figure out the data format later” is not an interface definition. The team that built the firmware and the team that

built the AI classifier will make different assumptions, and those assumptions will collide at integration.

5.2 Interfaces as Contracts

An **interface** is the shared boundary between two subsystems. At that boundary one subsystem makes a promise to another. Calling it a **interface contract** is deliberate: both sides are obligated. The provider subsystem must deliver exactly what is specified; the consumer subsystem must not demand anything beyond what is specified. When the contract is written down, a violation is detectable. When the contract lives only in someone's head, it is invisible until the two subsystems meet on the bench.

There are four interface types used throughout this course. Each type has a different set of properties that must be specified to make the contract complete.

5.2.1 Electrical Interfaces

An **electrical interface** specifies:

- **Voltage level:** logic-high and logic-low thresholds (e.g., 3.3 V CMOS or 5 V TTL).
- **Current capacity:** the maximum source/sink current the provider can supply and the maximum the consumer may draw.
- **Protocol:** the communication standard (UART, SPI, I²C, PWM, analog 0–5 V).
- **Connector:** physical connector type and pinout so that the mating is unambiguous.
- **Protection:** ESD handling, over-current limiting, or level-shifting requirements.

For the running-example sorter, the interface between the MCU and the motor driver is an electrical interface: 3.3 V PWM out from the MCU, 5 V logic input on the motor driver, requiring a level-shifter. Specifying the level-shifter requirement at architecture time — rather than discovering the incompatibility at bench time — is the direct return on investment for this chapter's work.

5.2.2 Mechanical Interfaces

A **mechanical interface** specifies:

- **Mounting geometry:** hole pattern, spacing, and tolerances.
- **Physical envelope:** maximum bounding box or keep-out volume.
- **Force or torque limits:** the maximum load the mating structure must carry.
- **Material compatibility:** relevant where corrosion, heat, or vibration is a factor.

For the running-example sorter, the mechanical interface between the sensor bracket and the conveyor frame defines the exact standoff height at which the time-of-flight sensor must sit relative to the belt surface. If the firmware team writes their detection algorithm assuming a 150 mm standoff but the mechanical team fabricates a 200 mm bracket, the item-detection gate geometry is wrong and every downstream timing calculation inherits that error.

5.2.3 Data Interfaces

A **data interface** specifies:

- **Protocol and transport:** MQTT, HTTP, I²C register map, SPI frame format, serial byte stream.
- **Message format:** field names, data types, units, and byte order.
- **Topic or address:** MQTT topic string, I²C device address, REST endpoint.
- **Quality of Service (QoS):** for MQTT, the QoS level (0, 1, or 2) and retained-message flag.
- **Error handling:** what happens if a message is lost, malformed, or arrives out of order.

For the running-example sorter, the data interface between the MCU firmware and the cloud dashboard is an MQTT publish on topic `sorter/status` with a JSON payload containing `item_class`, `sort_result`, and `timestamp_ms`. Any team member building the dashboard must consume exactly that format; any firmware update that renames a field without updating the interface table breaks the contract.

5.2.4 Timing Interfaces

A **timing interface** specifies:

- **Latency:** the maximum time between a trigger event and the expected response.
- **Throughput:** the maximum number of events per second the interface must sustain.
- **Jitter:** the maximum variation in latency from one cycle to the next.
- **Deadline type:** hard (a missed deadline is a system failure), firm (a missed deadline degrades output quality), or soft (a missed deadline is acceptable occasionally).

For the running-example sorter, the timing interface between the sensor read and the AI classifier is: sensor output available within $t_1 \leq 1$ ms of item detection, with jitter ≤ 0.1 ms. The AI classifier must begin its inference within that window to keep the 5 ms pipeline budget intact.

5.2.5 The Interface Table

All four interface types are collected into a single **interface table** — one row per arrow in the block diagram. Table 5.1 shows the interface table for the running-example sorter. This table is the primary deliverable of this chapter and must be completed before any subsystem build begins.

Table 5.1: Interface table for the IoT robotic sorting prototype. Each row names a boundary from Figure 5.1, its type, the contract properties, and the timing allocation from Section 5.3.

ID	From	To	Contract (key properties)	Latency
A	Sensor	Firmware	Electrical: 3.3 V I ² C, 400 kHz; range reading in 2-byte register; detection interrupt on GPIO	$t_1 \leq 1 \text{ ms}$
B	Firmware	AI Engine	Data: shared memory frame buffer; 320×240 px RGB888; semaphore handshake	$t_2 \leq 2 \text{ ms}$
C	AI Engine	Firmware	Data: classification label (uint8) + confidence (float32); written to result register; sets done flag	included in t_2
D	Firmware	Motor Driver	Electrical: 3.3 V PWM → level-shifted 5 V; direction GPIO; 20 kHz carrier	$t_3 \leq 2 \text{ ms}$
E	Firmware	MQTT Broker	Data: TCP/IP; topic <code>sorter/status</code> ; JSON payload; QoS 1; ≤200 ms publish latency	async
F	Sensor Bracket	Conveyor Frame	Mechanical: M3 × 4-hole pattern, 20 mm spacing; standoff 150±2 mm; max load 0.5 N	N/A

5.3 Budget Allocation

Specifying interfaces is necessary but not sufficient. You must also verify that the sum of all subsystem demands does not exceed the system-level constraint. This verification is called **budget allocation**: you divide a finite resource — time, power, or permissible error — across the subsystems that consume it, and then confirm the total stays within the specification limit.

Three budgets matter for the running-example prototype: timing, power, and measurement error.

5.3.1 Timing Budget

The **timing budget** formalises the constraint that the sum of all pipeline-stage latencies must not exceed the specification deadline.

$$T_{\text{total}} = \sum_i t_i \leq T_{\text{budget}} \quad (5.1)$$

This is the budget structure introduced in Chapter 4’s risk analysis (Equation 4.3). Here it is stated formally as the governing inequality for the architecture. Every

timing interface in the interface table must carry a t_i allocation; those allocations are substituted into Equation 5.1 to verify the total.

5.3.2 Power Budget

The **power budget** verifies that the supply rail can deliver enough current for all subsystems simultaneously.

$$P_{\text{total}} = \sum_i P_i \quad (5.2)$$

P_{total} must not exceed the rated output of the power supply. For the running-example sorter on a 5 V/2 A USB supply (10 W), typical subsystem allocations are: MCU 0.5 W, camera module 1.2 W, motor driver (idle) 0.8 W, motor driver (active) 2.5 W, Wi-Fi module 0.9 W — a peak total of 5.9 W, well within the 10 W budget with a 4.1 W margin. Margins matter: a motor driver that draws more than rated, a Wi-Fi transmit burst that spikes current, or a future addition of an LED indicator can each erode headroom. Figure 5.2 shows the timing and power budgets as stacked bars against their respective limit lines.

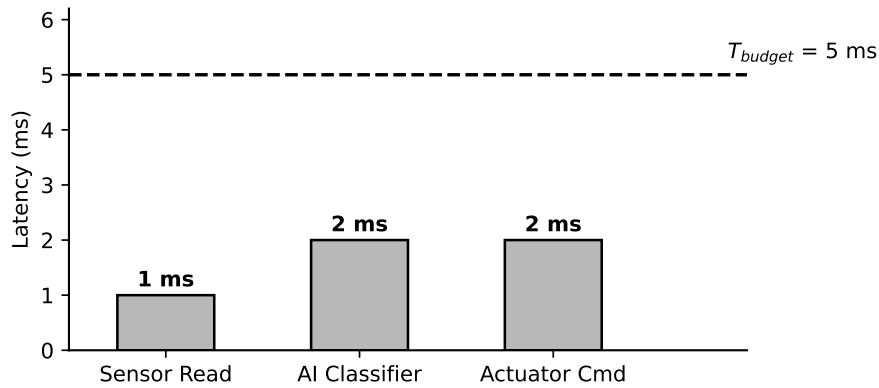


Figure 5.2: Interface budgets for the running-example sorter. Left panel: timing budget — stacked bar of t_1 , t_2 , t_3 against the 5 ms limit line (Equation 5.1). Right panel: power budget — stacked bar of subsystem power draws against the 10 W supply limit (Equation 5.2). Zero margin on timing means any added pipeline step requires removing an existing one.

5.3.3 Error Budget

Multiple measurement stages each contribute their own uncertainty. Assuming the error sources are independent and random, they combine in **quadrature** (root-sum-of-squares, RSS):

$$e_{\text{total}} = \sqrt{\sum_i e_i^2} \quad (5.3)$$

The RSS model is more realistic than a worst-case linear sum because independent errors partially cancel. If e_{total} exceeds the acceptance criterion, the team

must tighten the largest individual contributor first — squeezing a small contributor yields almost no benefit once a dominant error source exists.

5.3.4 Worked Example — Part A: Timing Budget

The central question from Chapter 3 requires classifying and diverting each item within ≤ 167 ms of arrival (6 items/min), but the firmware pipeline latency must be far shorter so that the MQTT publish and mechanical diversion can complete within that window. Chapter 4's risk analysis established a firmware timing budget of $T_{\text{budget}} = 5$ ms with three pipeline stages. Applying Equation 5.1:

$$T_{\text{total}} = t_1 + t_2 + t_3 = 1 \text{ ms} + 2 \text{ ms} + 2 \text{ ms} = 5 \text{ ms}$$

$$T_{\text{total}} = 5 \text{ ms} \leq T_{\text{budget}} = 5 \text{ ms} \quad \checkmark$$

where:

- $t_1 = 1$ ms: sensor read (I²C transaction, distance measurement, interrupt service);
- $t_2 = 2$ ms: AI classifier inference (image capture, pre-processing, forward pass, label decode);
- $t_3 = 2$ ms: actuator command (PWM update, GPIO direction set, motor driver settling).

The budget passes, but the **dwelt-time margin is zero**. Any added pipeline step — a second sensor read for confirmation, a logging write to flash, a display update — requires shortening one of the existing stages by an equal amount. This constraint must be visible to every team member: firmware engineers do not add steps to this pipeline without a corresponding timing analysis showing where the recovered time comes from.

5.3.5 Worked Example — Part B: RSS Error Budget

The sort-accuracy specification requires $\geq 95\%$ classification accuracy. Three independent sources of measurement uncertainty contribute to positional error at the classification gate:

- $e_1 = \pm 0.05$ m/s: conveyor speed sensor uncertainty, which introduces positional error when the system computes item position from belt velocity. At the nominal belt speed of 0.05 m/s, a speed uncertainty of ± 0.05 m/s maps to a relative positional uncertainty of $\pm(0.05/0.05) \times 1\% = \pm 0.1\%$; this is the value substituted as e_1 in the RSS calculation.
- $e_2 = \pm 0.5\%$: AI vision classification uncertainty (probability gap between top-1 and top-2 class, expressed as a percentage-point uncertainty in the sort decision).

- $e_3 = \pm 0.3\%$: positional uncertainty equivalent derived from timing jitter of ± 0.1 ms mapped through the nominal belt speed.

Expressing all contributors in compatible units (percentage-point equivalent positional uncertainty) and applying Equation 5.3:

$$e_1 = 0.1\%, e_2 = 0.5\%, e_3 = 0.3\%$$

$$e_{\text{total}} = \sqrt{(0.1\%)^2 + (0.5\%)^2 + (0.3\%)^2} = \sqrt{0.01 + 0.25 + 0.09\%} = \sqrt{0.35\%} \approx 0.59\%$$

The acceptance criterion is $e_{\text{total}} \leq 0.6\%$.

$$e_{\text{total}} \approx 0.59\% \leq 0.60\% \quad \checkmark$$

The error budget passes — but barely. The dominant contributor is e_2 , the AI classification uncertainty. If the model's confidence gap narrows (e.g., the item class becomes harder to distinguish), this budget will fail at that contributor first. Chapter 6 will revisit this when selecting the camera sensor and AI model architecture.

5.3.5.0.1 In Practice. A team building a motor controller prototype skipped the electrical interface table and started firmware before agreeing on the UART voltage level between the MCU and the motor driver. The MCU operated at 3.3 V logic; the motor driver expected 5 V logic. The firmware team wrote and tested their UART code against a bench logic analyser at 3.3 V. The electronics team wired the motor driver directly to the MCU TX pin. At integration, the motor driver received marginal logic levels: it sometimes responded and sometimes did not, depending on supply current at the moment of the transaction. Diagnosing the intermittent fault cost three days. The fix was a single-chip level-shifter — a \$0.30 CAD part that would have taken ten minutes to add to the schematic during architecture definition. The interface table entry for that boundary would have read: *“Electrical: MCU UART TX at 3.3 V CMOS logic; motor driver UART RX requires 5 V TTL; level-shifter required on this net.”* Three days of debugging for a \$0.30 part and one table row.

5.4 Why Integration Fails at Boundaries

Subsystems fail at their boundaries, not at their centres. This statement is almost universally true in mechatronic and embedded prototype development, and it has a straightforward explanation.

Within a subsystem, one engineer (or one small team) controls all the assumptions. The firmware engineer who writes the sensor driver and the interrupt handler is working within a single, consistent mental model. The mechanical engineer who designs the conveyor frame is making choices within their own constraints. Bugs within a subsystem are caught during subsystem-level testing because the developer is testing exactly the thing they understand.

At a boundary, two or more parties each independently assumed something about the other's subsystem. Those assumptions were never formally compared. When the two subsystems meet for the first time, every mismatched assumption becomes a defect. Figure 5.3 illustrates a canonical boundary mismatch: two subsystems whose interface contracts were never formally aligned, resulting in an incompatible handshake at integration.




Figure 5.3: Boundary mismatch at integration. The left subsystem (MCU firmware) assumes 3.3 V CMOS logic and outputs a valid signal by its own standard; the right subsystem (motor driver) expects 5 V TTL and interprets the same signal as an indeterminate logic level. Neither subsystem contains a bug in isolation; the defect exists only at the boundary, and is invisible until the two are connected.

5.4.1 Taxonomy of Boundary Failures

Four categories of boundary failure recur across student and professional projects alike.

5.4.1.1 Voltage Level Mismatch

The most common electrical boundary failure: one subsystem drives 3.3 V logic, the adjacent subsystem expects 5 V, and neither team checked the other's datasheet. Outcome: intermittent communication, latent damage to 3.3 V pins exposed to 5 V, or total non-function. Prevention: one row in the electrical interface table, one level-shifter on the BOM.

5.4.1.2 Protocol Mismatch

One subsystem writes a SPI frame formatted as 16-bit big-endian; the consuming subsystem reads it as 16-bit little-endian. Both subsystems pass their individual unit tests. The integration test produces garbage output that takes hours to trace to a byte-order disagreement. Prevention: specify byte order, data type, and endianness in the data interface contract.

5.4.1.3 Timing Assumption Mismatch

The firmware team assumes the AI engine returns a result within 2 ms. The AI team benchmarks their model at 3 ms on the prototype hardware. The pipeline budget fails by 1 ms and the diverter fires 1 ms after the item has already passed the gate. Prevention: the timing interface contract specifies the maximum latency; the AI

team runs a benchmark on the actual target hardware and signs off before build begins.

5.4.1.4 Mechanical Fit Mismatch

The sensor bracket is designed for a sensor with an M2.5 mounting hole. The sensor that arrives has an M3 mounting hole. Fabrication is already complete. Prevention: the mechanical interface contract specifies the exact hole pattern, fastener size, and tolerance, and is verified against the component datasheet before fabrication is released.

5.4.2 Identifying the Highest-Risk Boundary

Not all boundaries carry equal risk. The boundary with the highest integration risk is the one where:

1. the two subsystems are developed by different people or teams with limited communication;
2. the interface contract is the least precisely specified; and
3. a mismatch at this boundary would be the hardest to detect before it causes visible system failure.

This is precisely the FMEA detection factor D from Chapter 4 applied at the interface level. For the running-example sorter, the firmware-to-AI-engine boundary (Interface B in Table 5.1) carries the highest integration risk: the shared memory frame buffer protocol is non-standard, the two subsystems may be developed on different toolchains, and a timing assumption mismatch here propagates directly into a missed divert-gate deadline.

5.4.2.0.1 Common Pitfalls.

- **“We’ll figure it out later” interface agreements.** Verbal agreements about data formats, voltage levels, or timing are not interface contracts. They are deferred arguments. Experienced engineers know that “later” always arrives during integration, when schedule pressure is highest and the cost of rework is greatest.
- **Developing the interesting subsystem first.** AI engineers naturally want to train and test the classifier. Firmware engineers want to write drivers. Without fixed interfaces, each group builds to their own internally consistent assumptions, and integration becomes a negotiation between two finished products that were never designed to meet each other.
- **Interface table as a compliance artifact.** Filling out the interface table to satisfy a deliverable requirement, then ignoring it during build, defeats its purpose. The table must be the reference document that every team member checks before crossing a subsystem boundary.

Try It Yourself

Scenario: You are architecting a wireless air-quality monitor. The specification requires a total firmware pipeline latency of $T_{\text{budget}} = 8$ ms. Three pipeline stages have been proposed:

- $t_1 = 2$ ms: ADC sample (sensor read and digitisation);
- $t_2 = 3$ ms: digital filter (moving-average computation on the MCU);
- $t_3 = 2$ ms: BLE transmit buffer (packetise reading and push to BLE stack).

Three measurement error sources contribute to the reported air-quality reading:

- $e_1 = \pm 0.3^\circ\text{C}$ equivalent: temperature sensor uncertainty;
- $e_2 = \pm 1.5^\circ\text{C}$ equivalent: humidity sensor uncertainty (the % RH specification has been pre-converted to a temperature-equivalent for this budget);
- $e_3 = \pm 0.1^\circ\text{C}$ equivalent: ADC quantization noise.

The acceptance criterion for the combined error is $e_{\text{total}} \leq 1.6^\circ\text{C}$ equivalent.

Tasks:

- Timing budget.** Using Equation 5.1, compute $T_{\text{total}} = t_1 + t_2 + t_3$. State whether the timing budget is satisfied and identify the remaining margin (if any).
- Error budget.** Using Equation 5.3, compute e_{total} from the three error sources. State whether the error budget passes the acceptance criterion and identify the dominant contributor.
- Constraint violation response.** If the firmware team's digital filter implementation turns out to require $t_2 = 4$ ms instead of 3 ms, T_{total} will exceed T_{budget} . Identify which stage(s) could be shortened to restore compliance. For each option you propose, state the new t_i value and verify that the revised $T_{\text{total}} \leq 8$ ms.
- Interface contract.** Identify one interface in this air-quality monitor system (choose a boundary you consider the highest integration risk). Write a two-line interface contract for that boundary, specifying: (line 1) the protocol and voltage level or data format; (line 2) the timing constraint.

Review Questions

1. **(Conceptual)** State the four interface types defined in this chapter. For each type, give one specific example from the running-example IoT sorter system, naming the two subsystems at the boundary and one key property of the contract.

2. **(Conceptual)** Explain in two sentences why integration bugs typically appear at boundaries between subsystems rather than within a subsystem. Your answer should reference the concept of locally consistent assumptions within a subsystem versus the unverified assumptions that cross a boundary.
3. **(Conceptual — classification)** A team proposes an interface between the MCU and a Bluetooth module described only as “send the JSON string over serial.” Classify the completeness of this interface contract: state which of the four interface types it partially addresses, which required properties are missing, and explain why the omissions constitute integration risk.
4. **(Applied — calculation)** A firmware pipeline has four stages with the following latency allocations: $t_1 = 0.8$ ms, $t_2 = 1.2$ ms, $t_3 = 0.6$ ms, $t_4 = 0.9$ ms. The timing specification requires $T_{\text{budget}} = 4$ ms.
 - (a) Compute T_{total} using Equation 5.1.
 - (b) State whether the timing budget is satisfied. If it is satisfied, state the margin.
 - (c) An added 0.8 ms logging step is required. How must the existing stage allocations be adjusted to keep $T_{\text{total}} \leq 4$ ms? State which stage(s) to shorten and by how much.
5. **(Applied — multi-step)** Three subsystems each contribute independent positional measurement error to a parts-placement robot: encoder $e_1 = \pm 0.2$ mm, vision sensor $e_2 = \pm 0.5$ mm, synchronisation jitter equivalent $e_3 = \pm 0.1$ mm. The acceptance criterion is $e_{\text{total}} \leq 0.7$ mm.
 - (a) Compute e_{total} using Equation 5.3. Show all intermediate steps.
 - (b) State whether the error budget passes the acceptance criterion. If it passes, state the margin; if it fails, state the deficit.
 - (c) The vision sensor is upgraded to a model with ± 0.3 mm uncertainty. Re-compute e_{total} and state the new margin against the 0.7 mm criterion.

Portfolio Entry

By the end of this chapter your project folder must contain one deliverable:

System Architecture Package: the system block diagram (Figure 5.1) plus a completed interface table with every subsystem boundary from that diagram named, its four-property contract defined, and the timing and power budget columns filled in and verified against Equations 5.1 and 5.2.

Specifically, the package must demonstrate:

- A labelled block diagram with one box per subsystem across the four domains (electronics, mechanical, firmware, AI/IoT/robotic logic) and one labelled arrow per interface.
- An interface table in which each row names the two subsystems at the boundary, states the interface type (electrical, mechanical, data, or timing), and specifies the key contract properties.

- A timing budget column showing t_i allocations that sum to $T_{\text{total}} \leq T_{\text{budget}}$ (Equation 5.1).
- A power budget column showing P_i allocations that sum to P_{total} (Equation 5.2), with the total compared to the rated supply output.
- A written identification of the highest-risk boundary, with a two-sentence justification referencing the interface type and the detection difficulty of a mismatch at that boundary.

The block diagram and completed interface table together form the **Gate 3 architecture deliverable** (see the Stage-Gate model established in Chapter 2). A Gate 3 reviewer will verify: (1) every arrow in the block diagram has a corresponding row in the interface table; (2) each row carries a complete four-property contract; and (3) the timing and power budget columns close against Equations 5.1 and 5.2. A package that fails any of these three checks does not satisfy the Gate 3 architecture criterion.

Chapter Summary

Three tools now equip you to move from specification to buildable architecture.

First, a **decomposition framework**: dividing any prototype into four subsystem domains — electronics, mechanical, firmware, and AI/IoT/robotic logic — gives every team member an unambiguous scope and transforms integration from a surprise into a managed handshake.

Second, a **contract language for interfaces**: every boundary between subsystems carries a formal contract specifying electrical properties, mechanical geometry, data format, and timing constraints. A boundary without a contract is a liability that will be paid at integration time. The interface table is the instrument that makes all contracts visible to the whole team simultaneously.

Third, a **budget discipline**: timing, power, and measurement error are finite resources. Equations 5.1, 5.2, and 5.3 provide the arithmetic to verify that the sum of subsystem demands fits within the system-level limits. For the running-example sorter, the 5 ms timing budget is exactly consumed by the three pipeline stages, leaving zero margin; the power budget carries a 4.1 W margin; and the RSS error budget passes the 0.6% criterion by the narrowest of margins, flagging AI classification uncertainty as the risk to watch.

The architecture established here is the foundation on which Chapter 6 builds: the System Architecture Package gives Chapter 6 its starting point, and every component selected there will be evaluated against the interface contracts written here.

COMPONENT SELECTION & DATASHEET LITERACY

6.0.0.0.1 Where this fits. You are now inside Stage 3 (Development), moving toward Gate 3. Chapter 5 delivered the system block diagram and interface table — the verified architecture with its contracts and budgets. That gave you blocks to fill — but not yet a method for choosing the components that will populate them. This chapter teaches that method. Component selection at Stage 3 locks in a large fraction of unit cost, reliability, and supply-chain risk before a single board is laid out; a poor choice here is expensive to reverse. The deliverable you will carry into Gate 3 is a **component selection table** for the critical path of your prototype: part number, supplier, lifecycle status, derating factor, operating margin, alternate part, and system MTBF.

By the end of this chapter you will be able to:

1. extract the four critical parameter zones from a component datasheet (absolute maximum ratings, recommended operating conditions, electrical characteristics, timing diagrams);
2. apply derating factors to select components with adequate operating margin;
3. evaluate a component's lifecycle status using manufacturer product-page data;
4. identify a viable second source that satisfies parametric equivalence, footprint compatibility, and Active lifecycle status; and
5. estimate the failure rate of a series system from individual component MTBF values.

6.1 Reading a Datasheet

A **datasheet** is the manufacturer's binding specification for a component. It is not a tutorial, a marketing document, or a suggestion. Every number in a datasheet has a precise meaning, and your ability to extract and apply those numbers correctly separates a reliable design from one that fails unpredictably in the field.

You read a datasheet in a fixed order. You do not read from page one to the end. They go directly to four zones — in the order listed below — before they read anything else. Figure 6.1 annotates the anatomy of a representative datasheet, marking each of the four zones.

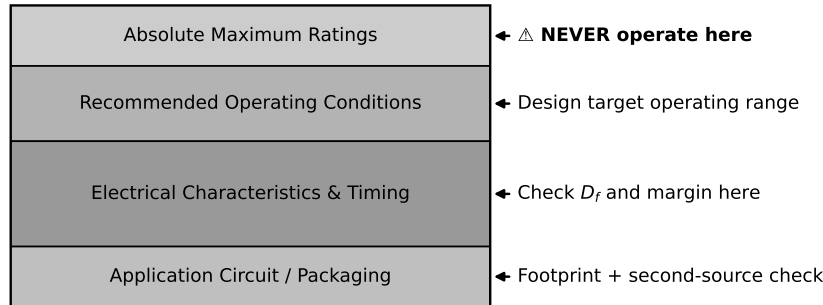


Figure 6.1: Annotated anatomy of a component datasheet showing the four critical zones: (1) absolute maximum ratings, (2) recommended operating conditions, (3) electrical characteristics, and (4) timing diagrams. Zone boundaries and key parameters are highlighted. Application circuit and packaging sections are labelled but not highlighted because they are consulted after the four critical zones are verified.

6.1.1 Zone 1 — Absolute Maximum Ratings

Absolute maximum ratings are the values beyond which permanent damage to the component is possible. They are not operating limits. The word “maximum” does not mean “allowed operating point” — it means “do not exceed under any condition, even briefly, or the silicon, ceramic, or polymer may be permanently damaged.” A component operated at its absolute maximum voltage may work today, tomorrow, and for a week. It may also degrade silently and fail during the customer demonstration. The manufacturer guarantees *nothing* about behaviour at or above these limits.

When you open a new datasheet, find the absolute maximum ratings table first. Write down the supply voltage maximum, the maximum junction temperature, and the maximum input voltage at any pin you plan to drive. These are your hard fences.

6.1.2 Zone 2 — Recommended Operating Conditions

Recommended operating conditions are the voltage, current, temperature, and frequency ranges within which the manufacturer tests the component and guarantees all published electrical characteristics. These limits are significantly narrower than absolute maximum ratings. Operating inside the recommended conditions is the minimum standard for a professional design.

The gap between the recommended operating limit and the absolute maximum limit is not a design margin you are allowed to use. It is a zone the manufacturer reserves for statistical variation, lot-to-lot spread, and the mathematical uncertainty in their own test equipment. You will learn in Section 6.2 that professional practice requires you to stay inside the recommended conditions, and then to derate further from there.

6.1.3 Zone 3 — Electrical Characteristics

Electrical characteristics tables list the guaranteed minimum, typical, and maximum values for every important parameter: output voltage, quiescent current, input impedance, propagation delay, leakage current, and dozens more. The columns are labelled Min, Typ, and Max.

This is the single most important discipline in datasheet reading: **design to the Min and Max columns, never to the Typ column**. The typical value describes the median part from the manufacturer's characterisation lot. Your prototype will contain parts from many lots, spanning a temperature range and an aging curve. If your circuit only works when every component happens to hit its typical value, your circuit does not work — it occasionally works.

6.1.4 Zone 4 — Timing Diagrams

Timing diagrams specify the temporal relationships between signals: setup time, hold time, propagation delay, clock-to-output delay, and bus turn-around time. These parameters are what make the interface contracts from Chapter 5 enforceable at the component level.

Recall from Chapter 5 that the running-example sorter has a fixed timing budget of 5 ms from sensor trigger to actuator command, with zero margin. That zero-margin budget means that every component on the signal path must be verified against its timing parameters in Zone 4 before it is selected. If a motor driver's datasheet shows a command-propagation delay of 2.1 ms worst-case, and you had allocated only 2 ms for that subsystem, the component violates the interface contract — regardless of what the typical value says.

6.1.5 Application Circuits and Packaging

After you have verified all four critical zones, two additional sections become relevant. **Application circuits** show the manufacturer's recommended decoupling topology, external component values, and layout guidance. Follow these circuits as a starting point; deviating from them requires justification. The **packaging and footprint** section specifies the physical dimensions and land pattern for PCB layout. Mismatching a footprint to the physical component is one of the most common and most embarrassing prototype failures — a component that cannot be soldered to the board it was designed for.

6.2 Derating

Derating is the practice of operating a component at a fraction of its rated limit in order to reduce the probability of failure and extend service life. It is not a safety factor added out of conservatism — it is a quantified, defensible engineering decision backed by decades of field-failure data. The fundamental observation is that component failure rate increases nonlinearly as operating stress approaches the

rated limit. Figure 6.2 shows the characteristic stress–failure-rate curve: failure rate is roughly flat at low stress fractions, rises steeply as the fraction approaches 1.0, and becomes essentially unbounded above the absolute maximum.

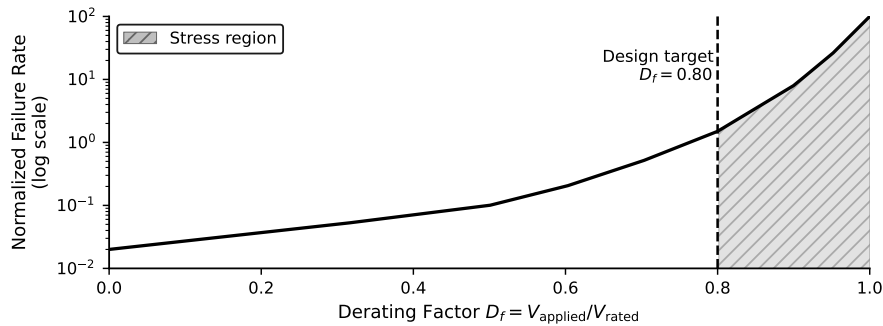


Figure 6.2: Component failure rate as a function of derating factor D_f . The curve is approximately flat below $D_f = 0.5$ and rises sharply above $D_f = 0.8$. The shaded region between $D_f = 0.8$ and $D_f = 1.0$ represents the stress zone where failure rate accelerates; the region above $D_f = 1.0$ (absolute maximum) represents the damage zone. The dashed line at $D_f = 0.80$ marks the maximum acceptable derating factor for voltage in this course.

The **derating factor** for a given parameter is defined as:

$$D_f = \frac{V_{\text{applied}}}{V_{\text{rated}}} \quad (6.1)$$

where V_{applied} is the actual operating value and V_{rated} is the component's rated limit for that parameter. Although Equation 6.1 is written in terms of voltage, the same ratio applies to current, power dissipation, and any other stress parameter.

The derating targets used in this course are:

- **Voltage (semiconductor):** $D_f \leq 0.80$
- **Voltage (capacitor):** $D_f \leq 0.75$
- **Current (semiconductor junction):** $D_f \leq 0.75$
- **Power dissipation:** $D_f \leq 0.70$
- **Junction temperature:** operate at least 25 °C below rated maximum junction temperature

These targets are conservative relative to some industry standards and are appropriate for a prototype context where accelerated testing and statistical sampling are not available.

6.2.0.0.1 Common Pitfalls.

- **Operating at absolute maximum ratings.** A component that operates at its absolute maximum voltage in a lab environment — with stable bench power, 22 °C ambient, and no vibration — will not reproduce that environment in a factory, a warehouse, or a field installation. “It worked in the lab” is not a reliability argument. The absolute maximum ratings exist to describe the damage threshold; the only correct interpretation is “never go here.”

- **No second source identified at design time.** A component selected without an identified alternate forces a design respin if the primary supplier discontinues or allocates the part. The respin cost, measured in engineering hours and schedule delay, routinely exceeds the original prototype budget. See Section 6.5 for the formal second-sourcing process.
- **Accepting a component because a colleague used it before.** A colleague's previous use of a component tells you that it worked in one set of operating conditions, in one design, at one point in time. It does not tell you that the component is active in the supply chain today, that it meets your design's specific voltage and timing requirements, or that it is available in the quantity your production ramp requires. Always check lifecycle status and verify the new design's specific operating conditions against the datasheet, regardless of prior familiarity.

6.3 Operating Margin

Where derating describes how close you are operating to the component's stress limit, **operating margin** describes how much headroom remains between an actual measured value and a specification limit. The two quantities are related but distinct. Derating is a design decision you make before building; margin is a measurement you make after building or simulating, to verify that the design decision was sufficient.

Operating margin is defined as:

$$M = \frac{\text{spec limit} - \text{actual value}}{\text{spec limit}} \times 100\% \quad (6.2)$$

A positive M means the actual value is inside the specification — you have headroom. A negative M means the actual value has violated the specification — the design fails. A margin of zero means the design is on the edge: any variation in temperature, supply voltage, component tolerance, or aging will push it into failure.

You should target a minimum margin of 20% on timing parameters and 25% on voltage parameters for a first prototype. These targets give you room to absorb the variation you will discover when you measure actual hardware for the first time.

6.4 Component Lifecycle Status

Every active component has a **lifecycle status** that describes where it sits in the manufacturer's product line plan. Treat lifecycle status as a risk register entry, not a purchasing footnote. Selecting a component without verifying its lifecycle status is equivalent to building a feature on a third-party API without checking its deprecation schedule.

Figure 6.3 shows the standard lifecycle timeline with risk annotations for each phase.




Figure 6.3: Component lifecycle timeline. Phases from left to right: Introduction, Growth, Mature (Active), NRND, Last-Time Buy, and Obsolete. Risk annotations indicate the design action appropriate at each phase. The bracket labelled “Design Window” spans Introduction through Mature; the bracket labelled “Risk Window” spans NRND through Last-Time Buy.

The four statuses you will encounter on distributor websites and manufacturer product pages are:

- **Active:** The component is in full production. The manufacturer is actively taking orders, maintaining inventory, and providing technical support. This is the only lifecycle status that is acceptable for a new design without a written risk exception.
- **NRND (Not Recommended for New Designs):** The manufacturer is signalling that the component is approaching end-of-life. NRND does not mean “unavailable today” — it means “do not start a new design on this component.” The typical window between NRND announcement and end-of-life is 12–36 months, but this varies widely. If a component you are considering is in NRND status, you must find an alternative before design freeze. Specifically, two actions are required: (1) identify an Active-status replacement that meets all parametric and footprint criteria; and (2) record the NRND status as a risk register entry with a resolution deadline.
- **Last-Time Buy (LTB):** The manufacturer has announced a final production run. Orders must be placed by a specified date. After that date the component will never be manufactured again. An LTB component should never be selected for a new design unless a complete lifetime supply can be purchased, inspected, and stored — a practice reserved for high-reliability aerospace and medical applications, not prototypes.
- **Obsolete:** The component is no longer available from the manufacturer. It may still appear on the secondary market (broker stock), but secondary-market parts carry risks of counterfeiting, improper storage, and undocumented handling that are unacceptable for a professional design.

6.4.0.0.1 In Practice. A team at a previous cohort built a working prototype on an MCU that was listed as Active at the time of component selection. Six months after design freeze — before the first production run — the manufacturer moved that MCU to NRND status. The team did not have a second source identified, because second-sourcing had been deferred. The redesign to a compatible MCU required new firmware validation, a new schematic review, and a new round of regulatory EMC testing. The total cost of the redesign exceeded the original pro-

prototype budget. Lifecycle status must be verified at component selection, not at production planning.

6.5 Second-Sourcing Strategy

Once you have confirmed Active status for every critical-path component, the next obligation is to ensure you are not dependent on a single supplier.

A **second source** is an alternative component that can substitute for the primary selection without requiring a schematic change, a firmware change, or a re-qualification test. Identifying a second source at component selection time costs roughly two hours of engineering effort. Scrambling to find one after a supply disruption costs weeks.

A viable second source must satisfy three criteria simultaneously. Satisfying two out of three is not sufficient:

1. **Parametric equivalence:** The alternate component must meet or exceed every specification that your design depends on — not just the headline spec, but every parameter you extracted from Zones 1 through 4. A motor driver with the same current rating but a slower PWM frequency response is not parametrically equivalent if your control loop depends on the frequency response.
2. **Footprint compatibility:** The alternate component must be pin-compatible with the primary on the PCB land pattern. A component with identical electrical specifications but a different package (e.g., QFN-32 versus TQFP-32) requires a layout change, which in a professional context triggers a new design revision and new board fabrication. For a prototype, this is a measurable cost.
3. **Lifecycle status:** The alternate component must itself be in Active status. An alternate that is NRND or LTB provides no protection against the supply disruption you are trying to mitigate.

6.5.0.0.1 In Practice. A team locked their BOM fourteen weeks before the scheduled system integration test. Three weeks later, the primary MCU lead time extended from stock to 14 weeks due to an industry allocation event. Because the team had not identified a second source, they were unable to substitute an equivalent part. The project schedule slipped by one full milestone — losing a Stage-Gate review cycle — while the team waited for allocation to clear. Had a second source been identified at BOM lock, the swap could have been made within two days.

6.6 Supply Chain Risk

Component selection is not complete until you have assessed the supply chain risk of every part on the critical path. **Supply chain risk** encompasses three main categories.

Single-source components are manufactured by exactly one supplier with no compatible alternate. They represent the highest supply chain risk in a BOM. When you identify a single-source component, it becomes a risk register entry (see Chapter 4) with a severity proportional to how difficult it would be to re-architect the design around a different part.

Lead time is the calendar time between placing an order and receiving parts. For most standard components, lead time is one to five weeks from distributor stock. For certain microcontrollers, power management ICs, and RF transceivers, lead time from the factory can reach 26–52 weeks during periods of high demand. You must verify the lead time of every critical-path component at the time of BOM lock, not at the time of purchase order. Lead times reported on distributor websites are real-time and can change daily.

Allocation periods occur when a component is in higher demand than the manufacturer's capacity can supply. During allocation, distributors receive fractional fills on their purchase orders, and small customers (including most prototype projects) may receive nothing. Allocation periods for popular MCU families have historically lasted 12–24 months. The only reliable mitigation is to have a qualified second source with independent supply chain.

6.7 MTBF and Reliability Basics

Reliability is the probability that a system performs its required function for a specified time under specified conditions. Every component you add to a system adds a probability of failure. Understanding how to estimate the aggregate reliability of a multi-component path allows you to make informed decisions about which components to derate more aggressively, which to make redundant, and which to flag as reliability risks in the Gate 3 review.

6.7.1 Failure Rate and FIT

Component reliability is quantified by the **failure rate** λ , defined as the expected number of failures per unit time. The industry-standard unit is the **FIT** (Failures In Time), where:

$$1 \text{ FIT} = 1 \text{ failure per } 10^9 \text{ hours}$$

A component with $\lambda = 200 \text{ FIT}$ is expected to produce one failure in 5×10^6 hours of aggregate device operation. FIT values are published by manufacturers in reliability reports and can also be estimated using MIL-HDBK-217 or Telcordia SR-332 models, which account for operating temperature and applied stress.

6.7.2 Series System Reliability

In a series reliability model, every component must function for the system to function. This is the correct model for a critical signal path: if any component in the path fails, the path fails. For a series system of n components, the system failure rate and system MTBF are:

$$\lambda_{\text{sys}} = \sum_i \lambda_i, \quad \text{MTBF}_{\text{sys}} = \frac{1}{\lambda_{\text{sys}}} \quad (6.3)$$

where λ_i is the failure rate of the i -th component and all rates are in consistent units (FITs or failures per hour). Note that adding components to a series path always *decreases* system MTBF. This is the quantitative justification for minimising component count on reliability-critical paths.

6.7.3 Parallel Redundancy

When two or more components perform the same function in parallel — and the system succeeds if at least one survives — the reliability model changes. For a parallel set of n components each with reliability R_i , the system reliability is:

$$R_{\text{sys}} = 1 - \prod_i (1 - R_i) \quad (6.4)$$

where R_i is the probability that component i has not failed over the mission time. Parallel redundancy is used in safety-critical subsystems — power supplies, communication links, and actuator drivers where a single failure must not halt the system. It is not a substitute for derating; a redundant pair of poorly derated components has a higher aggregate failure rate than a single well-derated component.

6.8 Worked Example

6.8.1 Part A — Derating and Operating Margin for an MCU

The running-example sorter uses an STM32-class MCU with the following datasheet parameters:

- Rated supply voltage: $V_{\text{rated}} = 3.6 \text{ V}$
- Applied supply voltage: $V_{\text{applied}} = 3.3 \text{ V}$
- Ambient temperature: $T_{\text{ambient}} = 85 \text{ C}$
- Timing parameter spec limit (setup time): $t_{\text{spec}} = 10 \text{ ns}$
- Timing parameter measured actual value: $t_{\text{actual}} = 3.2 \text{ ns}$

Derating factor for supply voltage (Equation 6.1):

$$D_f = \frac{V_{\text{applied}}}{V_{\text{rated}}} = \frac{3.3 \text{ V}}{3.6 \text{ V}} = 0.917$$

Comparing to the derating target of $D_f \leq 0.80$ stated in Section 6.2: $D_f = 0.917$ **exceeds the target**. The MCU supply voltage does not comply with the course derating rule. This finding must be recorded as a risk item.

6.8.1.0.1 Design action required. $D_f = 0.917 > 0.80$ fails the course derating target. This entry **must be flagged** in the component selection table and must be resolved — by selecting a component with $V_{\text{rated}} \geq 4.1$ V or by lowering V_{applied} to comply — before Gate 3 will accept the deliverable.

The design team must either reduce V_{applied} (for example, reducing V_{applied} to 2.88 V gives $D_f = 2.88/3.6 = 0.80$ (the boundary), or to 2.7 V gives $D_f = 2.7/3.6 = 0.75$ (compliant)) or select a component with a higher rated supply voltage.

Operating margin on the timing parameter (Equation 6.2):

$$M = \frac{10 \text{ ns} - 3.2 \text{ ns}}{10 \text{ ns}} \times 100\% = \frac{6.8 \text{ ns}}{10 \text{ ns}} \times 100\% = 68\%$$

A margin of 68% on the setup time is well above the 20% target for timing parameters. The setup time is not the constraint on this design. However, note that the 5 ms end-to-end timing budget from Chapter 5 has zero margin at the system level; the comfortable margin on this individual timing parameter does not relieve the pressure on the full pipeline.

6.8.2 Part B — System MTBF for the Actuator Interface Path

The actuator interface path in the running-example sorter consists of three components in series: the MCU, a level-shifter, and a motor driver. Their failure rates are:

Component	Role	λ (FIT)
MCU (STM32-class)	Firmware execution, actuator command	200
Level-shifter	3.3 V to 5 V translation	50
Motor driver	Sort actuator PWM control	400

System failure rate (Equation 6.3):

$$\lambda_{\text{sys}} = 200 + 50 + 400 = 650 \text{ FIT}$$

System MTBF in hours:

$$\text{MTBF}_{\text{sys}} = \frac{1}{\lambda_{\text{sys}}} = \frac{10^9 \text{ hours}}{650} \approx 1,538,462 \text{ hours}$$

Expressing MTBF in years (dividing by 8760 hours per year):

$$\text{MTBF}_{\text{sys}} = \frac{1,538,462}{8,760} \approx 175.6 \text{ years}$$

The motor driver dominates the system failure rate with 62% of the total λ_{sys} . If the project reliability target requires a higher MTBF, the motor driver is the first component to investigate for a lower-FIT alternative. The level-shifter contributes only 8% of total failure rate and is not the priority for improvement.

6.9 Try It Yourself

The following problem uses different numbers from the worked example. Work through each part before consulting the solutions in the appendix.

A 5 V linear regulator has the following datasheet and measurement data:

- Rated supply voltage: $V_{\text{rated}} = 5.5 \text{ V}$
- Applied supply voltage: $V_{\text{applied}} = 4.8 \text{ V}$
- Timing parameter spec limit (output-settle time): $t_{\text{spec}} = 20 \text{ } \mu\text{s}$
- Timing parameter measured actual value: $t_{\text{actual}} = 14 \text{ } \mu\text{s}$

Two components on the sensor front-end critical path:

- Sensor: $\lambda_1 = 120 \text{ FIT}$
- Analog front-end IC: $\lambda_2 = 310 \text{ FIT}$

- Compute D_f for the supply voltage using Equation 6.1. Is the result within the $D_f \leq 0.80$ voltage derating target?
- Compute the operating margin M on the timing parameter using Equation 6.2.
- Compute λ_{sys} and MTBF_{sys} for the two-component series path using Equation 6.3. Express MTBF in years (divide hours by 8,760).
- The sensor is currently listed as NRND by its manufacturer. State the two actions defined in Section 6.4 that the team must complete before the next design review, and give the lifecycle status the replacement component must hold.

6.10 Review Questions

- Q1.** Explain the difference between “absolute maximum ratings” and “recommended operating conditions” in a datasheet. Why is operating at the absolute maximum ratings a professional mistake, even if the component does not fail immediately?
- Q2.** A component’s lifecycle status changes from “Active” to “NRND.” State what NRND means, the typical time window before end-of-life, and the two responses a design team should take within that window.
- Q3.** A capacitor is rated at $V_{\text{rated}} = 16 \text{ V}$. The circuit applies $V_{\text{applied}} = 10 \text{ V}$.
 - Compute D_f using Equation 6.1.
 - The derating rule for capacitors is $D_f \leq 0.75$. Does this selection comply?
 - If V_{applied} rises to 13 V under transient conditions, recompute D_f and state whether the component should be replaced.

- Q4.** A four-component power path has failure rates $\lambda_1 = 80$ FIT, $\lambda_2 = 150$ FIT, $\lambda_3 = 220$ FIT, $\lambda_4 = 90$ FIT.
- Compute λ_{sys} using Equation 6.3.
 - Compute MTBF_{sys} in hours.
 - Convert to years (8,760 hours per year). Round to one decimal place.
 - The team adds a redundant parallel path for component 3 with an identical $\lambda_3 = 220$ FIT. Using Equation 6.4, compute R_{sys} for that redundant pair over a 10,000-hour mission time, where $R_i = e^{-\lambda_i t}$ with λ_i in failures per hour (note: 1 FIT = 10^{-9} failures/hour). State in one sentence whether the parallel pair improves or degrades reliability compared with a single component over the same mission time.
- Q5.** Explain why a “second source” must satisfy three criteria — parametric equivalence, footprint compatibility, and lifecycle status — and give an example of a second source that satisfies two of the three but fails on one.

Portfolio Entry

The deliverable for this chapter is the **component selection table** for the critical path of your prototype. This table is a mandatory input to Gate 3. Complete one row per critical-path component using the template below.

Part number	Supplier	Lifecycle status	Derating factor D_f (V)	Margin M (%)	Alternate part number	MTBF_{sys} (years)

Column definitions:

- **Lifecycle status:** Active, NRND, LTB, or Obsolete — verified on the manufacturer’s product page on the day of submission.
- **D_f (V):** Voltage derating factor computed using Equation 6.1. Flag any value > 0.80 in red.
- **Margin M (%):** Operating margin on the tightest timing or voltage parameter in the design, computed using Equation 6.2. Flag any value $< 20\%$ in red.
- **Alternate part number:** A second source that satisfies all three criteria from Section 6.5.
- **MTBF_{sys} (years):** Computed using Equation 6.3 for the full critical path.

6.11 Summary

This chapter gave you the tools to fill the architecture blocks from Chapter 5 with verified components. You can now navigate a datasheet systematically, extracting the four critical zones rather than reading from cover to cover. You can apply derating factors and compute operating margins to quantify the headroom between your design's operating point and the component's limits. You can assess lifecycle status and supply chain risk as engineering variables rather than purchasing footnotes, and identify a second source that genuinely substitutes for — not just superficially resembles — the primary selection. Finally, you can estimate the MTBF of a series reliability path and use that estimate to identify which component on the critical path deserves the most engineering attention.

These competencies together constitute **datasheet literacy**: the ability to translate a manufacturer's specification document into a set of verified, margin-positive design decisions. A design built on verified components with documented margins and identified alternates is a design that can survive the surprises — supply disruptions, temperature extremes, component lot variation — that the prototype bench cannot anticipate.

Chapter 6 produced the component selection table — part numbers, derating factors, lifecycle status, alternates, and system MTBF — that locks the critical path into Gate 3. Chapter 7 takes that table and examines how to design the assembly around those verified components so that manufacturing, testing, and serviceability are built in from the start.

DESIGN FOR X

7.0.0.0.1 Where this fits. This chapter operates at Stage 3 (Development) of the Stage-Gate model. Design-for-X decisions made here determine 70–80% of manufacturing cost and assembly quality before a single prototype board is soldered. Catching a DFX violation at Stage 3 costs a design revision; the same violation found at Stage 4 testing costs a board respin, a BOM change, and a schedule slip that threatens Gate 4.

Chapter 6 selected the components that populate the architecture. That fixed the bill of materials — but not yet how the assembly, test procedure, and reliability target will be designed into the hardware from the start. This chapter supplies that discipline.

1. Apply DFM principles to reduce unit cost for PCB and 3D-printed parts.
2. Compute DFA assembly efficiency η_A and identify parts that fail the keep/eliminate test.
3. Design observability and controllability into a prototype using DFT principles: test points, debug ports, and built-in self-test.
4. Connect the derating and lifecycle decisions from Chapter 6 to DFR design margin and thermal management.

7.1 What DFX Means

Design for X is the discipline of designing with the downstream process in mind. The “X” is a placeholder: it stands for Manufacturability (DFM), Assembly (DFA), Test (DFT), or Reliability (DFR), and the four disciplines interact.

Figure 7.1 shows the four domains and their relationship to prototype design.

A common misconception is that DFX is a checklist run at design-complete. It is not. DFX is a continuous design constraint: each time you choose a component, a trace width, a fastener, or a PCB stack-up, you make a DFX decision. If you make it consciously, using the principles in this chapter, you eliminate whole categories of downstream failure. If you make it by default, you pay for it at assembly, test, or field return.

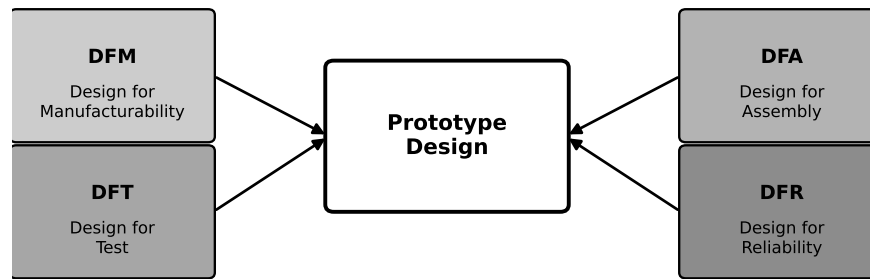


Figure 7.1: The four DFX disciplines feed into every prototype design decision. Optimising one domain in isolation can degrade another; the goal is to resolve conflicts at Stage 3, before they become build failures.

7.2 Design for Manufacturability

Design for Manufacturability (DFM) means choosing processes, tolerances, and geometries that standard equipment can produce reliably at your target volume and cost.

7.2.1 PCB DFM

The following rules apply to every prototype PCB submitted to a contract manufacturer:

- **Trace width and spacing.** Stay at or above the fabricator's minimum design rule. A 0.1 mm trace on a board specified for 0.15 mm minimum will be rejected or reflowed out of spec.
- **Via size.** Blind and buried vias cost extra; through-hole vias are standard. Choose via drill sizes that the fabricator's standard process supports.
- **Panelisation.** Design the board to panel at standard sizes so the fabricator can run multiple boards per panel without custom tooling.
- **Solder mask and silkscreen.** Solder mask openings must clear pad edges by the fabricator's specified clearance. Silkscreen must not overlap pads — solder will not adhere through ink.
- **Component courtyard clearances.** Ensure no courtyard overlaps; the pick-and-place machine needs clear landing zones for each nozzle.

7.2.2 3D-Print DFM

The running example uses a 3D-printed housing. FDM (fused deposition modelling) imposes its own DFM rules:

- **Minimum wall thickness.** FDM walls thinner than 1.2 mm (two perimeters at 0.4 mm nozzle) are weak and prone to delamination.

- **Overhang angle.** Overhangs beyond 45° require support material, which must be removed and damages fine features. Design with 45° chamfers instead of 60° ledges.
- **Part orientation.** Orient the part so that the functional mating surfaces (connector openings, PCB standoffs) are printed in the XY plane, not the Z direction, where layer adhesion is weaker.
- **Support-free internal channels.** Route cable channels as tear-drop cross-sections rather than round bores; they print without support and are stronger.

7.2.2.0.1 In Practice. A 3D-printed housing for the running example was designed with 60° overhangs on the internal PCB shelf. Support material filled the shelf cavity; removing it with pliers cracked the shelf on two of six printed units. Redesigning to a 45° chamfer eliminated the support requirement entirely, and all subsequent units printed clean.

7.3 Design for Assembly

Design for Assembly (DFA) minimises the number of parts and assembly operations, reducing labour cost and assembly error rate.

7.3.1 The Boothroyd–Dewhurst Criterion

The **Boothroyd–Dewhurst keep/eliminate test** asks three questions for each part:

1. Does the part move relative to all other parts during operation?
2. Must the part be made of a different material from adjacent parts?
3. Must the part be separate to allow assembly or disassembly?

A part that answers *no* to all three questions is a candidate for elimination — it can be integrated into an adjacent part. $N_{\min}$ is the count of parts that answer *yes* to at least one question.

7.3.2 Assembly Efficiency

Assembly efficiency η_A measures how close a design is to the theoretical minimum:

$$\eta_A = \frac{N_{\min} \cdot t_{\text{ideal}}}{t_{\text{actual}}} \quad (7.1)$$

where $t_{\text{ideal}} = 3 \text{ s}$ is the Boothroyd–Dewhurst standard ideal assembly time per part, and t_{actual} is the measured total assembly time in seconds. A higher η_A means the design is closer to the minimum. Typical values for a first-pass design are 5–15%; well-optimised assemblies reach 40–60%.

The cost saving from a DFA redesign is:

$$\Delta C \approx \Delta N_{\text{parts}} \cdot \bar{c}_{\text{part}} + \Delta N_{\text{ops}} \cdot \bar{c}_{\text{op}} \quad (7.2)$$

where $\bar{c}_{\text{part}}$ is the average part cost saved per eliminated part and $\bar{c}_{\text{op}}$ is the average cost per assembly operation second (typically \$0.08–\$0.15/s at contract assembly rates in CAD).

7.4 Design for Test

Design for Test (DFT) builds observability and controllability into the hardware at design time. **Observability** means you can measure a signal's actual value. **Controllability** means you can force a signal to a known state to isolate a fault.

Figure 7.2 shows the three DFT features designed into the running-example MCU board: test points, a UART debug header, and an SWD/JTAG programming header.




Figure 7.2: DFT features on the running-example MCU board: test points TP1 and TP2 accessible by a logic probe and scope respectively; a UART debug header (J1) for firmware printf output; an SWD/JTAG header (J2) for breakpoint debugging and firmware flashing.

7.4.1 Test Points

Test points are labelled, exposed pads or through-hole vias placed on every signal that a technician might need to probe. Minimum rules:

- One test point per power rail, placed between the regulator output and the first load capacitor.
- One test point on every high-frequency or safety-critical signal.
- Test points must be at least 2.54 mm from any component body to allow a standard probe tip to land.

7.4.2 Debug Ports and BIST

A **UART debug port** connected to a header allows the firmware to stream printf output during development without stopping execution. This exposes firmware state non-intrusively — the single most valuable DFT feature for firmware-heavy prototypes.

Built-in self-test (BIST) is firmware that runs a self-check sequence at power-on, toggles each output GPIO, reads back each ADC rail, and reports pass/fail over the debug port before the main application loop starts. BIST catches bring-up faults in under 30 seconds.

7.4.3 Defect Coverage

Once test procedures are running, track defect density with **DPMO** (defects per million opportunities):

$$\text{DPMO} = \frac{D}{N \cdot O} \times 10^6 \quad (7.3)$$

where D is the number of defects observed, N is the number of units tested, and O is the number of test opportunities per unit. Adding more test points increases O , which lowers DPMO for the same physical defect count — this is the quantitative argument for investing in DFT.

7.4.3.0.1 In Practice. An early prototype of the running-example sorter board had no test points and no UART debug port. When the sort classifier produced incorrect results during bring-up, the validation team spent three days probing unmarked pads with a clip lead to distinguish a firmware logic error from a hardware signal-integrity problem. A UART debug port would have printed the classifier output at each step and isolated the fault in under 20 minutes. The three days were not recoverable from the project schedule.

7.5 Design for Reliability

Design for Reliability (DFR) translates the FMEA risk register from Chapter 4 and the derating margins from Chapter 6 into concrete design choices.

7.5.1 Derating and FMEA Margin

The derating factor D_f from Chapter 6 is a DFR parameter: a component operating at $D_f = 0.70$ has significantly longer expected life than one at $D_f = 0.90$. When the FMEA assigns Severity $S \geq 8$ to a failure mode, the DFR response is to increase the design margin — lower D_f , specify a higher-rated part, or add protective circuitry.

7.5.2 Redundancy

For failure modes that are both high-severity and high-occurrence ($\text{RPN} > 80$ from Chapter 4), **redundancy** may be justified: two components in parallel, where either one suffices, lower the effective failure rate. Use Chapter 6's parallel-reliability equation to quantify the improvement before committing board area.

7.5.3 Thermal Management

Every power-dissipating component has a maximum junction temperature $T_{j,\max}$. The thermal budget is:

$$T_j = T_{\text{ambient}} + P_D \cdot \theta_{JA}$$

where P_D is power dissipation and θ_{JA} is junction-to-ambient thermal resistance from the datasheet. Verify $T_j < T_{j,\max}$ at maximum operating ambient temperature before finalising component placement; hotspot components may need copper pours, thermal vias, or forced airflow.

7.6 DFX Trade-offs in Practice

The four disciplines interact and sometimes conflict. A DFM optimisation (reducing layer count to save fabrication cost) may eliminate the reference plane needed for signal integrity (a DFR regression). A DFA optimisation (integrating two parts into one moulded piece) may block the disassembly access required for test (a DFT regression).

The resolution principle is: *optimise for the dominant cost driver at your production volume.*

- At **prototype volume** (1–10 units): labour time dominates. Prioritise DFT — instrument every signal, use every debug port. DFM is secondary; a few extra fabrication days matter less than a three-day firmware debug.
- At **low-volume production** (100–1000 units): assembly cost dominates. Prioritise DFA — eliminate parts, standardise fasteners, design for one-directional insertion.
- At **high volume** (10000+): material cost dominates. Prioritise DFM — optimise BOM cost, panel efficiency, and process yield.

7.6.0.0.1 Common Pitfalls. DFX applied as a post-design review checklist rather than a live design constraint will always find violations too late to fix cheaply. Every design decision from component selection onward is a DFX decision; treat it that way.

7.6.0.0.2 Common Pitfalls. Adding test points “if there is room” is not DFT. Test points designed in as required features, with reserved courtyard space and silkscreen labels, are DFT. Three strategically placed test points found a PCB fabrication defect in the running example during bring-up; three test points added as afterthoughts on the same board revealed nothing because they landed on signals that were already observable with a multimeter.

7.7 Worked Example

The running-example sorter board has an eight-part PCB subassembly. Applying the Boothroyd–Dewhurst test, three parts must be kept ($N_{\min} = 3$): the MCU (different material and function), the motor-driver IC (different material and function), and the connector housing (must be separate for mating access). The remaining five parts — three identical M2 standoffs, one wire-tie anchor, and one redundant power-rail capacitor — answer *no* to all three questions and are candidates for elimination.

Part A — Assembly Efficiency

Before redesign: $N_{\text{parts}} = 8$, $t_{\text{actual}} = 120$ s.

Using Equation 7.1:

$$\eta_A = \frac{N_{\min} \cdot t_{\text{ideal}}}{t_{\text{actual}}} = \frac{3 \times 3}{120} = \frac{9}{120} = 0.075 \quad (7.5\%)$$

Two parts are eliminated in the redesign (the three standoffs become integrated PCB snap features; the wire-tie anchor is removed by routing the cable through a slot moulded into the housing). The redesign reduces t_{actual} to 80 s.

$$\eta'_A = \frac{3 \times 3}{80} = \frac{9}{80} = 0.1125 \quad (11.25\%)$$

Figure 7.3 shows the before/after comparison.

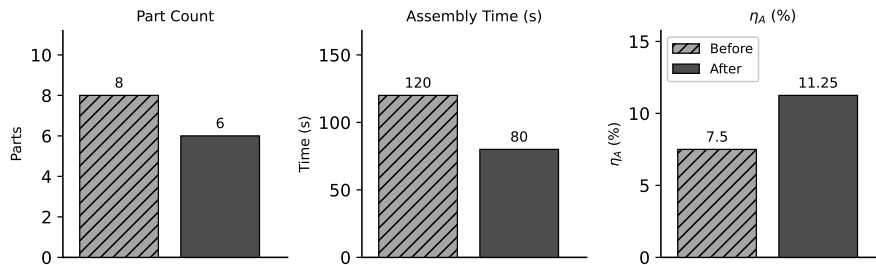


Figure 7.3: Part count, assembly time, and η_A before and after the DFA redesign. Eliminating two parts reduces assembly time by 33% and raises η_A from 7.5% to 11.25%.

Using Equation 7.2 with $\bar{c}_{\text{op}} = \$0.10/\text{s}$ and a production run of 500 units:

$$\Delta C = (120 - 80) \text{ s} \times \$0.10/\text{s} \times 500 = 40 \times \$0.10 \times 500 = \$2,000 \text{ CAD}$$

Part B — Defect Coverage (DPMO)

A test run of 100 units of the sorter PCB subassembly produces 3 defects. Each unit has $O = 12$ test opportunities (12 explicitly designed test points).

Using Equation 7.3:

$$\text{DPMO} = \frac{D}{N \cdot O} \times 10^6 = \frac{3}{100 \times 12} \times 10^6 = \frac{3}{1200} \times 10^6 = 2,500 \text{ DPMO}$$

At this rate, a production run of 10 000 units would yield:

$$10,000 \times 12 \times \frac{2,500}{10^6} = 300 \text{ defective opportunities}$$

Interpreted: 300 test points across all units will fail; each failure triggers a rework or rejection.

Try It Yourself

A sensor breakout board subassembly has 6 parts, $t_{\text{actual}} = 90$ s, and $N_{\text{min}} = 2$. The team identifies one candidate for elimination (a redundant tie-point bracket), reducing t_{actual} to 65 s. A test run of 50 units reveals 2 defects; each unit has 8 test opportunities.

- Compute η_A before the elimination using Equation 7.1.
- Compute η_A after the elimination.
- Compute the assembly cost saving per unit at 200 units using $\bar{c}_{\text{op}} = \$0.10/\text{s}$ (Equation 7.2).
- Compute the DPMO using Equation 7.3.

(No answer key provided.)

Review Questions

- (Conceptual)** State the four DFX disciplines covered in this chapter. For each, give one specific design decision from the running-example sorter prototype that falls within that discipline.
- (Conceptual)** Explain the Boothroyd–Dewhurst three-question keep/eliminate test. Give one example of a component that passes all three criteria (must be kept) and one that fails all three (candidate for elimination) from the running example.
- (Applied — calculation)** A subassembly has 10 parts and $t_{\text{actual}} = 150$ s. The Boothroyd–Dewhurst test identifies $N_{\text{min}} = 4$.
 - Compute η_A using Equation 7.1.
 - A redesign eliminates 3 parts and reduces t_{actual} to 100 s. Compute the new η_A .
 - Compute the assembly cost saving per unit at 300 units, using $\bar{c}_{\text{op}} = \$0.12/\text{s}$.

4. **(Applied — multi-step)** A production run of 200 units yields 5 defects, with $O = 15$ test opportunities per unit.
 - (a) Compute DPMO using Equation 7.3.
 - (b) At this rate, how many defects are expected in a run of 50 000 units?
 - (c) The team adds 3 additional test points per unit, raising O from 15 to 18. The defect count stays at 5 per 200 units. Recompute DPMO and explain in one sentence why DPMO decreased even though the physical defect count did not change.
5. **(Conceptual)** Explain why DFM and DFA can conflict. Give one example where reducing material cost (DFM) increases assembly time (DFA regression). State how to decide which discipline to prioritise at prototype volume versus production volume.

Portfolio Entry

Your DFX review checklist for the prototype:

1. **DFM** — three PCB or mechanical decisions that use standard processes: trace width and via size within fabricator rules; 3D-print features within 45° overhang limit; panel size within standard sheet.
2. **DFA** — η_A computed for the most complex subassembly; one elimination candidate identified and either eliminated or logged with justification for retention.
3. **DFT** — three observability features explicitly designed in: test-point locations and labelled signals; UART debug port with header and silkscreen designation; BIST firmware routine described.
4. **DFR** — derating margin from Chapter 6 confirmed against the FMEA Severity ratings from Chapter 4; any $D_f > 0.80$ entry resolved or logged as a risk item for Gate 3.

Chapter Summary

Four disciplines now constrain your prototype design before the first component is soldered. DFM aligns your PCB layout and 3D geometry with what standard processes can produce reliably. DFA uses the Boothroyd-Dewhurst criterion and η_A (Equation 7.1) to quantify and reduce assembly labour. DFT instruments every critical signal with test points, debug ports, and BIST so that bring-up faults are found in minutes rather than days. DFR translates FMEA severity ratings and derating margins into design choices that protect reliability before the hardware is built.

The DFX checklist you produced is a concrete Stage 3 deliverable. Gate 3 reviewers will look for evidence that cost, assembly, and reliability were designed in, not discovered during validation.

Chapter 7 disciplined the design process. Chapter 8 now introduces AI tools that can accelerate design work — and explains how to use them without compromising the engineer's accountability for every output.

AI IN PROTOTYPING: CAPABILITY & RISK

8.0.0.0.1 Where this fits. This chapter operates at Stage 3 (Development) of the Stage-Gate model. AI tools are increasingly present inside Stage 3 design work — generating firmware scaffolding, suggesting component values, exploring design alternatives, and drafting documentation. Every AI output that enters your design must be verified before it becomes Gate 3 evidence; this chapter gives you the framework to decide what to verify, how rigorously, and how to document it.

8.0.0.0.2 Learning Objectives. After completing this chapter, you will be able to:

1. Identify three categories of design task where AI tools provide genuine value in the prototyping workflow.
2. Compute the expected cost of error for an AI-generated output and apply the verification decision rule to determine whether independent verification is required before incorporating the output into a design.
3. Assess the IP and data-leakage risk of using a public AI tool with proprietary design data and identify at least two specific categories of Stage 3 information that must not be submitted to a public service without checking the provider's retention policy.
4. Document AI use in a reproducible, traceable format suitable for a Gate 3 submission.

Chapter 7 delivered a component-verified, assembly-optimised, test-instrumented schematic package ready for Gate 3 review — produced by applying four DFX frameworks to the Stage 3 design. It did not address the AI tools many teams reach for inside that same stage to accelerate the work. This chapter provides the framework for using those tools without compromising the integrity of the design package.

8.1 Where AI Helps

AI-assisted design tools — large-language models, code-completion engines, and component-suggestion services — can reduce the time spent on routine, well-

defined sub-tasks within Stage 3. Three categories of task account for most of the practical value in a prototyping workflow.

8.1.1 Code and Firmware Scaffolding

Writing peripheral initialisation code, interrupt handlers, communication protocol wrappers, and RTOS task skeletons is repetitive and follows patterns that are well-represented in publicly available firmware. An AI tool can generate a working first draft of a UART driver, an I²C read/write wrapper, or a timer-interrupt handler in seconds.

The value is not that the output is correct by default — it often is not, for reasons discussed in Section 8.3. The value is that a plausible first draft is faster to correct than to write from scratch, and it forces the engineer to think through the design at the code level earlier in the process.

For the running-example sorter project, AI-generated firmware scaffolding is useful for the sort-accuracy inference pipeline: the AI can produce a skeleton that reads sensor data, formats it for the inference engine, and routes the classification result to the conveyor control loop. The engineer then verifies each section against the MCU datasheet and the inference engine's API specification.

8.1.2 Component Value Suggestion

Selecting passive component values — pull-up and pull-down resistors, decoupling capacitors, RC filter time constants — requires applying well-known formulas to circuit-specific parameters. An AI tool can propose a value given a natural-language description of the circuit context ("10 kHz I²C bus, 400 pF estimated bus capacitance").

The suggestion reduces search time. It does not replace the engineer's obligation to verify the value against the datasheet application note and, where relevant, to bench-test the result. Section 8.4 establishes when bench verification is required.

8.1.3 Design Alternatives and Documentation Drafts

AI tools can enumerate design alternatives quickly: given a power-supply topology requirement, they can list candidate topologies with broad trade-offs. This is useful for early-stage exploration, where breadth matters more than depth. The engineer evaluates the shortlist using the selection criteria from Chapter 6, not the AI's ranking.

AI tools also accelerate documentation drafts: block-diagram descriptions, BOM notes, test-procedure outlines, and design-rationale summaries can all be drafted from a structured prompt and then edited for accuracy and completeness. Documentation drafted by AI must be reviewed against the actual design before submission; Chapter 9 will show why incomplete or inaccurate safety documentation has consequences beyond a Gate 3 review.

8.2 Accelerator, Not Autonomous Designer

One principle governs all AI-assisted design work: **the engineer is accountable for every output that enters the design**, regardless of how that output was produced.

An AI tool has no professional licence, no liability, and no understanding of your specific circuit, budget, safety obligations, or regulatory context. It produces plausible text and code based on statistical patterns in its training data. When that output happens to be correct, it saves time. When it is wrong — and it will be wrong, in ways described in Section 8.3 — the engineer who accepted it without verification is responsible for the consequence.

This is not a philosophical position; it has direct implications for Gate 3 evidence. A Gate 3 review asks: “How do you know this design meets specification?” “The AI said so” is not an answer that survives scrutiny. “The AI suggested it; we verified it by (*method*); the result was (*outcome*)” is.

Design acceleration is the correct mental model for AI in Stage 3. An AI tool does not change what must be verified or who must verify it; it changes how long the first draft takes to produce.

8.3 Hallucination in an Engineering Context

AI hallucination is a specific failure mode distinct from a simple factual error. A factual error is a wrong answer to a question that has a right answer in the AI’s training data — the AI retrieves the wrong datum. A hallucination is a confidently stated answer that has no factual basis at all: the AI generates a plausible-sounding output that does not correspond to any real specification, component, or physical relationship.

In an engineering context, hallucinations are more dangerous than factual errors for one reason: *they look right*. A factual error — a resistor value that is obviously wrong for the voltage level — is caught by inspection. A hallucination — a pull-up resistor value that is plausible for many buses but wrong for this specific bus speed and capacitive load — passes visual inspection and may even pass a basic functional test, failing only under the exact operating conditions of your application.

8.3.1 The Human-in-the-Loop Verification Cycle

The response to hallucination risk is a structured **human-in-the-loop (HITL) verification cycle**. Figure 8.1 shows the cycle.

The cycle has four steps:

1. **Generate.** Prompt the AI tool with enough context to produce a specific, actionable output. Vague prompts produce vague outputs; vague outputs are harder to verify.
2. **Estimate risk.** Assign a probability of error p_{err} and a consequence cost $C_{\text{consequence}}$




Figure 8.1: The human-in-the-loop verification cycle for AI-generated design outputs. The engineer generates a candidate output using an AI tool, applies an independent verification method (datasheet check, simulation, bench test, or first-principles calculation), and either accepts the output and logs it, or rejects it and either regenerates or derives the value manually. The cycle is not optional; it applies to every AI output that enters the design.

to the output. Section 8.4 shows how to use these to decide verification depth.

3. **Verify independently.** Apply a verification method that is independent of the AI tool: datasheet application note, SPICE simulation, analytical calculation, or bench measurement.
4. **Accept or reject and log.** Record what the AI produced, how it was verified, and the result. Section 8.6 specifies the log format.

8.3.1.0.1 In Practice. A first-principles priority review of AI-generated interrupt handlers can catch failures that functional tests miss, as the following example illustrates. A team used AI to generate firmware interrupt handlers for a real-time scheduler on the running-example sorter. The AI output compiled cleanly and passed basic unit tests. The interrupt handler correctly serviced the conveyor-belt encoder pulses at low throughput. Under the 6 items/min throughput target, however, interrupt latency spiked intermittently and caused missed encoder edges. Root-cause analysis identified a race condition in the interrupt priority scheme: the AI had assigned equal priority to the encoder interrupt and a lower-frequency status-reporting interrupt. When status reporting and an encoder pulse arrived simultaneously at high throughput, the encoder pulse was occasionally delayed by the status-reporting ISR. A first-principles review of the interrupt priority assignment — checking each interrupt against the real-time deadline table in the design specification — caught the race condition before deployment. The fix was a one-line priority change; the cost of not catching it would have been a throughput failure at Gate 3 demonstration.

8.4 The Black-Box Problem: Deciding When to Verify

You cannot always verify every AI output at the same depth: bench testing every component value is not feasible in a constrained schedule. A quantitative decision rule prevents both under-verification (trusting plausible output that is wrong) and over-verification (spending verification time that exceeds the value at risk).

8.4.1 Expected Cost of Error

The **expected cost of error** $\mathbb{E}[C_{\text{err}}]$ is:

$$\mathbb{E}[C_{\text{err}}] = p_{\text{err}} \cdot C_{\text{consequence}} \quad (8.1)$$

where p_{err} is your estimated probability that the AI output is wrong for your specific application, and $C_{\text{consequence}}$ is the cost you will incur if the error reaches the prototype undetected (diagnosis time, rework, schedule slip, or safety consequence).

The **verification decision rule** is:

If $\mathbb{E}[C_{\text{err}}] > \text{cost_verify}$, verify.

This rule makes the verification decision quantitative and defensible. It also reveals when verification is not cost-justified — when the consequence of a wrong value is trivially correctable and the verification cost is disproportionate. For safety-relevant functions, $C_{\text{consequence}}$ is large by definition, and the rule will always recommend verification.

Figure 8.2 shows a trust matrix that maps AI output categories against typical verification requirements.

AI Confidence	High	Use with spot-check	Verify independently
	Low	Accept with caution	Do not use without full verification
		Low	High
		Consequence of Error	

Figure 8.2: Trust matrix for AI-generated design outputs. Outputs with low consequence cost and high AI reliability (e.g., boilerplate file structure, documentation phrasing) can be accepted with a visual review. Outputs with high consequence cost or low AI reliability (e.g., interrupt priority assignments, power-supply compensation networks, safety-critical logic) require independent simulation or bench verification before acceptance. No AI output to a safety-relevant function may be deployed unverified.

8.4.2 Worked Example: I²C Pull-Up Resistor

The running-example MCU board uses an I²C bus to communicate with the sort classifier's sensor array. An AI tool suggests a 10 k Ω pull-up resistor for the bus.

The engineer's assessment:

- $p_{\text{err}} = 0.15$: a 15% chance the value is wrong for this bus speed (400 kHz fast mode) and the estimated 250 pF capacitive load of four sensors on a 15 cm trace. The I²C specification limits the RC rise time, and at 400 kHz the bus capacitance matters; the AI did not have this context.

- $C_{\text{consequence}} = \480 CAD: one day of technician time to diagnose intermittent I²C failures, identify the pull-up value as the cause, replace the resistor, and re-verify communication.
- $\text{cost_verify} = \$40$ CAD: 20 minutes of engineer time to apply the I²C pull-up selection equation from the NXP UM10204 application note and check the result against a SPICE simulation of the bus topology.

Applying Equation 8.1:

$$\mathbb{E}[C_{\text{err}}] = 0.15 \times \$480 = \$72 \text{ CAD}$$

Decision: $\$72 > \40 , so verification is justified.

The engineer applies the rise-time equation from the application note. For a 400 kHz bus with $C_b = 250$ pF, the I²C fast-mode specification sets a maximum rise time $t_r = 300$ ns (NXP UM10204, Table 10). The pull-up rise-time equation from that application note is:

$$R_{\text{max}} = \frac{t_r}{0.8473 \cdot C_b}$$

where the constant 0.8473 comes from the I²C voltage threshold definition ($V_{\text{IH,min}} = 0.7 V_{\text{DD}}$, giving $\ln(1/0.3)^{-1} \approx 0.8473$). Substituting:

$$R_{\text{max}} = \frac{300 \text{ ns}}{0.8473 \times 250 \text{ pF}} \approx 1,416 \Omega$$

The AI-suggested 10 k Ω would produce a rise time of approximately 2.1 μs — seven times the I²C fast-mode limit. The AI output is rejected. The engineer selects 1.0 k Ω (well within the 1,416 Ω maximum), verifies the rise time is within specification, and logs the interaction. Table 8.1 shows the complete AI use log entry for this interaction; it satisfies the format specified in Section 8.6.1.

This is the HITL cycle in action: the AI output was plausible (10 k Ω is correct for standard-mode I²C) but wrong for the specific operating conditions. The 20-minute verification prevented an intermittent bus failure that would have been expensive to diagnose on a completed board.

Table 8.1: AI use log entry for the I²C pull-up resistor interaction.

Field	Entry
Tool used	(AI service), accessed (date)
Prompt summary	Pull-up resistor value for 400 kHz I ² C bus, ≈ 250 pF bus capacitance, four sensors on 15 cm trace.
Output produced	AI suggested 10 k Ω .
Verification	NXP UM10204 rise-time equation; SPICE simulation of bus topology.
Result	Rejected. $R_{\text{max}} \approx 1,416 \Omega$ for fast mode; selected 1.0 k Ω .
$\mathbb{E}[C_{\text{err}}]$	$0.15 \times \$480 = \$72 \text{ CAD} > \$40 \text{ cost_verify}$; verification justified.

8.4.2.0.1 Common Pitfalls. Trusting plausible output without verification is the most common failure mode when teams begin using AI tools in design work. “It looked right” is not an engineering justification. An output that looks right for the general case is frequently wrong for your specific combination of bus speed, supply voltage, load capacitance, and PCB parasitics.

8.5 IP and Data-Leakage Risk

Using a public AI tool for design work introduces a risk that has no analogue in traditional design tools: the data you submit may leave your control.

8.5.1 What Happens to Your Data

Public AI services vary widely in their data-retention policies. Many services retain submitted content for model-improvement purposes unless you explicitly opt out — and the opt-out mechanism may not apply retroactively to data already submitted. Some services retain conversation history on their servers indefinitely. Enterprise tiers with contractual data-handling guarantees exist, but they require a procurement decision and are not the default for a student or small team logging into a public web interface.

Proprietary design data submitted to a public AI tool may therefore:

- Be stored on the provider’s servers beyond the session.
- Be used to train or fine-tune future model versions.
- Be retrievable, in whole or in part, through prompts from other users if it becomes embedded in model weights or cached session data.
- Constitute a public disclosure that affects patent-filing timelines in jurisdictions that require novelty.

Data leakage in this context does not require a security breach. It occurs through normal use of a service whose terms permit the provider to use submitted content.

8.5.2 What Constitutes Proprietary Data

In a Stage 3 prototype context, the following are typically proprietary:

- Schematics and PCB layouts that embody design decisions not yet in a granted patent or published application.
- Firmware source code, particularly inference-engine integration code that represents a competitive advantage.
- BOM entries that reveal supplier relationships or negotiated pricing.
- Design specifications that disclose performance targets ahead of a product announcement.

Generic questions — “what is the I²C fast-mode maximum pull-up resistance for 250 pF bus capacitance?” — carry no proprietary content. Questions that include a schematic image, a firmware file, or project-specific parameters that identify your design carry significant risk.

8.5.2.0.1 In Practice. A team pasted a proprietary motor-driver schematic into a public AI chat session to ask for a component suggestion. The schematic included part numbers, supplier codes, and a circuit topology that was not yet in the prior art. Six months later, when another user asked a similar question about motor-driver design, the AI reproduced elements of the schematic — part numbers and a recognisable sub-circuit — in its response. The team had not read the provider’s data-retention terms before submitting the schematic; those terms permitted the provider to use submitted content for model improvement. The incident triggered a review by the organisation’s legal counsel and delayed a patent filing.

8.5.3 The Data-Handling Policy

Before using any AI tool with design data, establish a simple policy:

1. **Classify the data.** Is it generic (publicly available physics and formulas) or proprietary (specific to your design)?
2. **Check the provider’s terms.** Does the provider retain submitted content? Is there an enterprise or confidentiality tier?
3. **Anonymise where possible.** Replace specific part numbers with generic descriptions; replace project-specific values with ranges. “A pull-up resistor on a 400 kHz I²C bus with 250 pF load” reveals nothing proprietary. A schematic image does.
4. **Log what was submitted.** The AI use log (Section 8.6) records a *prompt summary*, not the raw prompt, specifically to avoid logging proprietary data in a document that may be shared.

8.5.3.0.1 Common Pitfalls. Submitting confidential design data to a public AI tool without checking the provider’s data-retention policy is a data-governance failure, not a technical one. The circuit may be correctly analysed; the design may be accelerated. The risk is not to this prototype — it is to every future product, patent filing, or competitive position that depends on the information remaining confidential. Check the terms before you paste the schematic.

8.6 Reproducibility and Traceability

Gate 3 requires evidence that your design decisions are defensible. If AI tools contributed to a design decision, the Gate 3 record must show: what the AI produced, how it was verified, and what the engineer decided as a result. A design whose AI contributions are undocumented cannot be reproduced, audited, or defended.

8.6.1 The AI Use Log

Every AI-assisted design interaction should produce an entry in an **AI use log**. Each entry contains:

1. **Tool used.** Name and version (or access date) of the AI service.
2. **Prompt summary.** A description of what was asked, with no proprietary data. Example: “Asked for pull-up resistor value for 400 kHz I²C bus with approximately 250 pF capacitive load.”
3. **Output produced.** The AI’s specific recommendation. Example: “AI suggested 10 k Ω .”
4. **Verification method.** How the output was checked. Example: “Applied NXP UM10204 rise-time equation; SPICE simulation of bus topology.”
5. **Result.** Accepted or rejected, with brief rationale. Example: “Rejected. Calculated $R_{\max} \approx 1,416 \Omega$ for fast mode; selected 1.0 k Ω .”
6. $\mathbb{E}[C_{\text{err}}]$ **computed.** The expected cost of error used to justify the verification decision.

A log entry takes less than five minutes to write. It transforms an undocumented shortcut into a traceable, auditable design decision.

8.6.1.0.1 Common Pitfalls. The most consequential documentation failure is having no record of AI involvement in a design. If a Gate 3 reviewer asks “How was this pull-up value selected?” and the answer is “I asked an AI,” the follow-up question is immediate: “How was the AI output verified?” Without a log entry, you cannot answer that question. With a log entry showing $\mathbb{E}[C_{\text{err}}] = \72 and verification cost = \$40, and a rejection of the AI’s suggestion with the correct value derived from the application note, you have demonstrated exactly the engineering judgment a Gate 3 review is designed to find.

8.6.2 Reproducibility Requirement

Reproducibility in this context means that a second engineer reading the AI use log can reconstruct the verification independently and reach the same conclusion. Each log entry must be specific enough that a second engineer can reconstruct the verification using the prompt summary, output record, named source, and result fields specified in Section 8.6.1.

Reproducibility is not a bureaucratic requirement. It is the standard of evidence that distinguishes engineering from guessing.

Try It Yourself

A team uses AI to suggest a decoupling capacitor value for the 3.3 V power pin of the MCU on the running-example sorter board.

- $p_{\text{err}} = 0.20$: a 20 % chance the suggested value is suboptimal for this PCB layout (high-frequency bypass inadequate for the MCU’s transient current demand).

- $C_{\text{consequence}} = \600 CAD: one day of debug and rework if the MCU resets intermittently under load at high throughput.
- $\text{cost_verify} = \$25$ CAD: 15 minutes to check the MCU datasheet application note for the recommended decoupling network.

- (a) Compute $\mathbb{E}[C_{\text{err}}]$ using Equation 8.1.
- (b) Is verification justified? State the decision rule explicitly.
- (c) The team reduces p_{err} to 0.04 by first checking the MCU datasheet application note before querying the AI, so the AI prompt includes the datasheet-recommended value range and asks only whether the layout parasitics would change the recommendation. Recompute $\mathbb{E}[C_{\text{err}}]$ and state whether verification is still justified.
- (d) (*Conceptual*) Name two pieces of information that must appear in the AI use log entry for this interaction, beyond the tool name and date, and explain in one sentence why each is necessary for Gate 3 traceability.

(No answer key provided.)

Review Questions

1. (**Conceptual**) List the three categories of design task from Section 8.1 where AI provides genuine value in the prototyping workflow. For each category, state one specific task from the running-example IoT robotic sorter project that falls within it.
2. (**Conceptual**) Explain the difference between a factual error and an AI hallucination in an engineering context. Why is an AI hallucination potentially more dangerous than a simple factual error when it appears in a design output such as a component value or a firmware interrupt priority assignment?
3. (**Applied — calculation**) A team generates an AI-suggested motor-driver current-sense resistor value. The engineer estimates $p_{\text{err}} = 0.08$ and $C_{\text{consequence}} = \$1,200$ CAD (motor overcurrent damage and board replacement if the sense resistor is wrong). Bench verification of the value takes 30 minutes, equivalent to $\text{cost_verify} = \$60$ CAD.
 - (a) Compute $\mathbb{E}[C_{\text{err}}]$ using Equation 8.1.
 - (b) Is verification justified? Apply the decision rule explicitly.
 - (c) At what value of p_{err} does $\mathbb{E}[C_{\text{err}}]$ exactly equal cost_verify ? Show the algebra. Then state: if the engineer could reduce p_{err} to half the breakeven value by spending an additional \$15 CAD on a datasheet review before prompting the AI, is that additional expenditure cost-justified? Show your reasoning.
4. (**Applied — multi-step**) A team generates three AI outputs in one design session:

- Output A: a pull-up resistor value. $p_{\text{err}} = 0.12$, $C_{\text{consequence}} = \320 CAD , $\text{cost_verify} = \$30 \text{ CAD}$.
- Output B: a firmware loop structure for the conveyor control task. $p_{\text{err}} = 0.25$, $C_{\text{consequence}} = \800 CAD , $\text{cost_verify} = \$50 \text{ CAD}$.
- Output C: a BOM line-item description for a passive component. $p_{\text{err}} = 0.05$, $C_{\text{consequence}} = \80 CAD , $\text{cost_verify} = \$20 \text{ CAD}$.

- (a) Compute $\mathbb{E}[C_{\text{err}}]$ for each output using Equation 8.1.
 - (b) Which outputs should be verified according to the decision rule?
 - (c) Rank **all three** outputs by verification priority (highest $\mathbb{E}[C_{\text{err}}]$ first), then identify the threshold $\mathbb{E}[C_{\text{err}}]$ value below which an output in this session would not justify verification.
5. **(Conceptual)** A team member proposes submitting the following information to a public AI chat service to get component suggestions: a 48 V motor-driver schematic showing the full H-bridge topology, the project's part number prefix, and the target current rating. Using the data classification policy from Section 8.5.3, identify which elements of this submission carry proprietary risk and state what anonymised substitution should be made for each before the prompt is submitted.
 6. **(Conceptual)** A colleague argues: "We should just verify everything AI produces, so we never need to compute $\mathbb{E}[C_{\text{err}}]$." Explain in two sentences why this policy fails in practice for a team operating under a fixed Stage 3 schedule.

Portfolio Entry

Produce an AI use log with at least three entries from your prototype design session. Each entry must include:

1. **Tool used** — name and version or access date.
2. **Prompt summary** — what was asked, with no proprietary data in the record.
3. **Output produced** — the specific value, code, or recommendation the AI returned.
4. **Verification method applied** — the independent check used (datasheet section, simulation, calculation, bench test).
5. **Result** — accepted or rejected, with the accepted or corrected value if rejected.
6. $\mathbb{E}[C_{\text{err}}]$ **computed** — the expected cost of error that justified the verification depth.

At least one entry must result in a rejection (the AI output was wrong and a corrected value was derived independently).

Chapter Summary

AI tools accelerate Stage 3 design work in three categories: code and firmware scaffolding, component value suggestion, and design alternatives and documentation drafting. In every category, the engineer remains the accountable party; AI provides a faster first draft, not a substitute for independent verification.

The expected cost of error $\mathbb{E}[C_{\text{err}}] = p_{\text{err}} \cdot C_{\text{consequence}}$ (Equation 8.1) makes the verification decision quantitative: verify when $\mathbb{E}[C_{\text{err}}]$ exceeds the cost of verification. The human-in-the-loop cycle (Figure 8.1) and the trust matrix (Figure 8.2) provide the operational framework for applying this rule consistently.

IP and data-leakage risk requires a data-handling policy before AI tools are used with design data: classify the data, check the provider's retention terms, and anonymise proprietary content in prompts.

Traceability is a Gate 3 requirement. The AI use log records what was generated, how it was verified, and what the engineer decided — transforming an unauditable shortcut into a defensible design decision.

The AI use log produced in this chapter is the Stage 3 traceability artifact that shows every AI-assisted decision was independently verified before it entered the Gate 3 design package. Chapter 9 takes that verified design and addresses the obligations that come with the hardware itself — security, power, and physical-safety requirements for a connected, moving system.

IoT, ROBOTICS & SAFETY AS A DESIGN OBLIGATION

9.0.0.0.1 Where this fits. This chapter operates at Stage 3 (Development) of the Stage-Gate model. Security and physical-safety requirements not designed in at this stage will surface as failures at Gate 4 (Testing & Validation), where every retrofit costs more time, more money, and more risk than the original design decision would have. A security flaw discovered during a field test does not cost one library swap; it costs a firmware re-architecture, a re-flash campaign, and a delay that may miss the project deadline. A prototype moving part without a hardware emergency stop does not fail quietly; it fails dangerously.

9.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Identify the three IoT attack surfaces and specify at least one security control for each.
2. Compute average current I_{avg} and battery life t_{life} for a duty-cycled IoT device.
3. Identify the three required physical-safety features for a moving robotic prototype: e-stop, guarding, and fail-safe state.
4. Compute the mechanical safety factor SF for a load-bearing element and assess whether $SF \geq 2$ is satisfied.

Chapter 8 delivered a working firmware prototype built with AI-assisted tooling inside Stage 3. That left open a second set of Stage 3 obligations: the security, power, and physical-safety requirements that the hardware itself carries — regardless of what tools were used to design it. This chapter closes that gap.

9.1 IoT Security by Design

Security by design means treating encryption, authentication, and secure communication as first-class design requirements, not optional enhancements added after the hardware is built and running.

The cost-of-change principle from Chapter 3 applies directly: the three security properties below must be designed in, not added after.

Encryption ensures that data in transit cannot be read or modified by a third party. For an MQTT sorter node communicating over Wi-Fi, this means TLS 1.2 or TLS 1.3 between the device and the broker. Encryption without authentication is incomplete: an attacker who cannot read your messages can still inject their own if the broker accepts unauthenticated connections.

Authentication ensures that only legitimate devices and users can connect to your system. At minimum, each device must present a unique credential — a per-device username and password, or a client certificate — that the broker can verify and revoke independently of every other device. Shared credentials, such as a single “device” account used by all nodes, mean that compromising one device compromises every device on the network.

Secure update closes the lifecycle loop. Firmware that cannot be updated securely in the field is firmware that will run outdated cryptographic libraries indefinitely. Signing firmware images with a private key and verifying the signature on the device before flashing is the minimum acceptable posture for any deployed IoT prototype.

9.1.0.0.1 In Practice. An IoT prototype shipped with default MQTT broker credentials (“admin” / “password”). Within 48 hours of deployment, a network scanner found the open broker and began injecting spurious sort commands into the conveyor system. The fix — per-device credentials and TLS — took two days to implement after the fact. At design time, the same change would have taken twenty minutes.

9.2 Attack Surfaces

Every IoT system has three distinct **attack surfaces**: the layer at which an adversary can attempt to gain unauthorised access or cause harm. Understanding the surfaces helps you assign a control to each one at design time rather than discovering them during a security audit.

Figure 9.1 maps each layer to its principal threats.

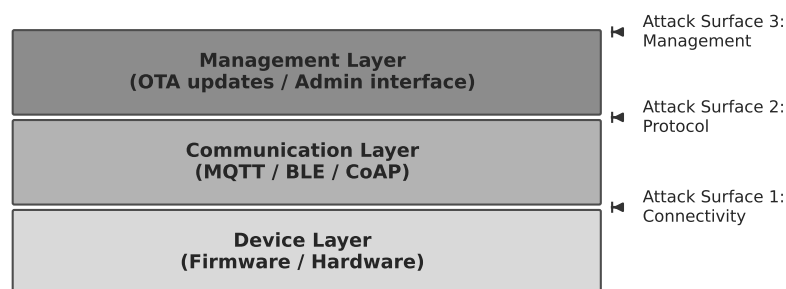


Figure 9.1: Layered IoT architecture for the MQTT sorter node. The connectivity layer (Wi-Fi/Ethernet), the communication layer (MQTT broker and topics), and the management layer (OTA update and admin interface) each carry a distinct attack surface requiring its own security control.

9.2.1 Connectivity Layer

The **connectivity layer** is the physical and link-layer network: Wi-Fi, Ethernet, or a cellular radio. Threats here include passive eavesdropping on unencrypted traffic, man-in-the-middle insertion, and denial-of-service through radio jamming or TCP flooding.

Apply network-layer encryption (WPA3 for Wi-Fi; VPN or private APN for cellular) and restrict the device to a dedicated IoT VLAN that has no route to general office or campus infrastructure. For the running-example sorter node, the MQTT broker should be reachable only from the IoT VLAN, not from a shared student network.

9.2.2 Communication Layer

The **communication layer** is the application protocol: MQTT topics, CoAP resources, or BLE GATT characteristics. Threats here include topic spoofing (an attacker publishes false sensor readings or spurious actuator commands), topic enumeration (an attacker subscribes to # and reads every message), and replay attacks (a captured command is re-sent later).

Authenticate every publisher and subscriber at the broker using per-device credentials; use topic-level access control lists (ACLs) so that a sensor node can publish to its own telemetry topic but cannot publish to the actuator command topic; include a message timestamp or sequence number to detect replays.

9.2.3 Management Layer

The **management layer** is the interface used to update firmware and configure the device: an OTA update server, a web dashboard, an SSH port, or a JTAG adapter left enabled in production firmware.

Threats here are the most severe because compromising the management layer gives an attacker the ability to re-flash every device. Disable all debug interfaces in release builds; sign firmware images; use mutual TLS for OTA update channels; change all default admin credentials before first deployment; enforce multi-factor authentication on the cloud dashboard.

9.2.3.0.1 Common Pitfalls. “Add security later” is the most expensive four-word sentence in embedded development. Retrofitting TLS onto an MQTT stack that was built without it requires restructuring the firmware state machine — the connection, subscription, publish, and reconnect logic all carry TLS context — not just swapping a library call. The second pitfall is shipping default credentials in production firmware. Every device with identical credentials is a single point of compromise: one leaked password grants access to the entire deployed fleet.

9.3 Privacy and Data Obligations

Sensor data is not automatically neutral. Certain categories of data collected by an IoT device trigger legal and ethical obligations that your design must accommodate from the start.

Personal data is any information that can identify a natural person, directly or indirectly. A CO₂ sensor reporting aggregate room occupancy is not personal data; a badge reader logging individual entry times is. Under Québec Law 25 (Loi 25) and the federal PIPEDA, collecting personal data requires a stated purpose, user consent, and documented retention limits. If your IoT device collects personal data, you must specify those elements before the device is deployed.

Location data is a subcategory that receives heightened scrutiny because it reveals movement patterns over time. A GPS tag on a delivery robot that reports position continuously creates a persistent location history. Design controls include anonymisation (report zone, not coordinates), aggregation (report 10-minute averages, not 1-second fixes), and retention limits (purge data older than 30 days).

Biometric data — fingerprint templates, facial recognition embeddings, voice prints — is treated as sensitive in virtually every jurisdiction. If a prototype uses a camera for person detection, you must assess whether the processing constitutes biometric identification and, if so, obtain explicit consent and provide a technical architecture that does not transmit raw biometric templates over a network.

The practical rule at Stage 3 is: for each sensor on your device, ask whether the data it produces could identify a person or reveal their behaviour. If yes, document the legal basis for collection, the purpose limitation, and the retention policy in your design records before Gate 3.

9.4 Protocol Selection

Choosing a communication protocol is simultaneously a security decision, a power decision, and an interoperability decision; each of the three protocols used at prototype scale — MQTT, CoAP, and BLE — carries a distinct security posture and power profile requiring its own design controls.

9.4.1 MQTT

MQTT (Message Queuing Telemetry Transport) is a publish-subscribe protocol designed for constrained devices on unreliable networks. It is TCP-based, which means it carries the overhead of a persistent connection but provides reliable, ordered delivery. For the running-example sorter node, MQTT is the protocol of record.

Mandatory security posture for MQTT in a prototype:

- Use TLS 1.2 or TLS 1.3 between every client and the broker. Plain-text MQTT on port 1883 is not acceptable on any network reachable from the internet.

- Use an **authenticated broker**: the broker must require a username and password (or client certificate) before accepting a connection.
- Issue **per-device credentials**: each node has its own username/password pair so that a compromised node can be revoked without affecting any other device.
- Define topic ACLs so that sensor nodes cannot publish to actuator command topics.

9.4.2 CoAP

CoAP (Constrained Application Protocol) is a request-response protocol modelled on HTTP but designed for UDP transport and very small code footprints. It is appropriate when the device cannot maintain a persistent TCP connection or when a RESTful resource model fits the application better than a topic hierarchy.

Security posture: use DTLS (Datagram TLS) to secure CoAP traffic. Plain-text CoAP has no confidentiality or integrity protection. DTLS adds handshake overhead to each session, but pre-shared key (PSK) mode keeps the footprint manageable on constrained microcontrollers.

9.4.3 BLE

BLE (Bluetooth Low Energy) is a short-range, low-power protocol suited to wearables, beacons, and devices that communicate with a nearby gateway or smartphone. Its power consumption advantage over Wi-Fi is significant: a BLE advertisement at 1 dBm typically costs less than 10 mA for a few milliseconds, while a Wi-Fi association sequence can draw 100–200 mA for hundreds of milliseconds.

Security posture: use **LE Secure Connections** (introduced in Bluetooth 4.2), which uses Elliptic Curve Diffie-Hellman for key exchange. Legacy “Just Works” pairing provides no meaningful security against passive eavesdropping; avoid it in any design that transmits data of value.

The trade-off summary: MQTT over TLS is the right choice for the sorter node because the broker provides centralised logging, topic ACLs, and a dashboard integration point. BLE would be appropriate if the node were battery-powered and within 10 m of a gateway. CoAP is appropriate for constrained nodes that cannot sustain a TCP connection.

9.5 Power and Battery Budgeting

Battery-powered IoT nodes operate in a **duty cycle**: they wake, perform a measurement and a transmission, then return to a deep-sleep mode that draws a fraction of the active current. The duty cycle D is the fraction of time the device spends in its active state.

9.5.1 Average Current

Because the device spends most of its time asleep, the battery sees a time-weighted average current that is much lower than the active current. The **average current** I_{avg} is:

$$I_{\text{avg}} = D \cdot I_{\text{active}} + (1 - D) \cdot I_{\text{sleep}} \quad (9.1)$$

where I_{active} is the current drawn during the active interval, I_{sleep} is the current drawn during the sleep interval, and D is the duty cycle (dimensionless, $0 < D < 1$).

At low duty cycles — say, $D = 0.02$ (2%) — the sleep current often dominates the average even if it is two or three orders of magnitude smaller than the active current. This means that reducing I_{sleep} by choosing a microcontroller with a lower deep-sleep current may improve battery life more than reducing I_{active} .

9.5.2 Battery Life

Given I_{avg} and a battery capacity C_{batt} (in mAh), the estimated **battery life** t_{life} is:

$$t_{\text{life}} = \frac{C_{\text{batt}}}{I_{\text{avg}}} \quad (9.2)$$

This is an idealised estimate. Real battery capacity degrades with temperature, discharge rate, and age; a practical design should target t_{life} at least 20% above the specification to account for these effects.

Figure 9.2 shows the current profile for a duty-cycled node, with I_{avg} marked as the equivalent constant-current drain.

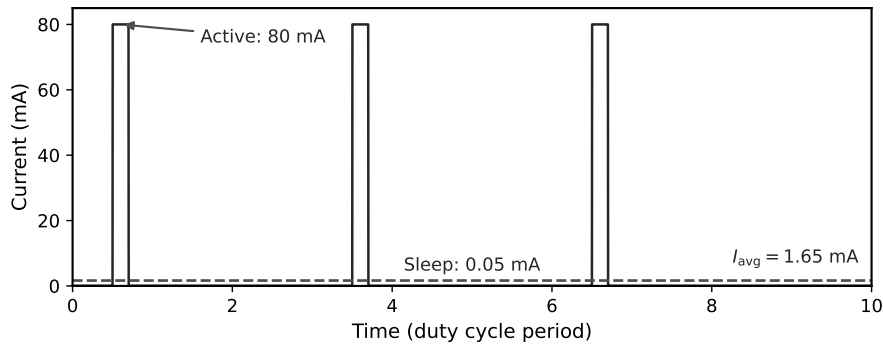


Figure 9.2: Duty-cycled current profile for an MQTT sensor node. Narrow active pulses (drawing I_{active}) are separated by long sleep intervals (drawing I_{sleep}). The dashed horizontal line marks I_{avg} , the constant current that would drain the battery in the same time. At $D = 2\%$, the sleep interval dominates the average.

9.5.3 Worked Example — Power Budget

The running-example MQTT sorter node has the following parameters: $I_{\text{active}} = 80 \text{ mA}$, $I_{\text{sleep}} = 0.05 \text{ mA}$, $D = 0.02$ (the node wakes every 10 s for a 200 ms measurement-

and-publish cycle), $C_{\text{batt}} = 2000 \text{ mAh}$.

Step 1: Compute I_{avg} .

Using Equation 9.1:

$$I_{\text{avg}} = 0.02 \times 80 + 0.98 \times 0.05 = 1.600 + 0.049 = 1.649 \text{ mA}$$

Step 2: Compute t_{life} .

Using Equation 9.2:

$$t_{\text{life}} = \frac{2000}{1.649} = 1212.9 \text{ h} \approx 50.5 \text{ days}$$

Step 3: Sensitivity — halve the duty cycle.

If the team can reduce the reporting rate so that $D = 0.01$ (one report per 20 s instead of per 10 s):

$$I'_{\text{avg}} = 0.01 \times 80 + 0.99 \times 0.05 = 0.800 + 0.0495 = 0.8495 \text{ mA}$$

$$t'_{\text{life}} = \frac{2000}{0.8495} \approx 2354 \text{ h} \approx 98.1 \text{ days}$$

Halving the duty cycle nearly doubles the battery life (from 50.5 days to 98.1 days). The improvement is not exactly $2\times$ because the sleep current sets a floor: as $D \rightarrow 0$, $I_{\text{avg}} \rightarrow I_{\text{sleep}}$, not zero. This sensitivity analysis belongs in the power budget table of your design records.

9.6 Robotics Physical Safety

Any prototype that moves — a conveyor, a sort gate, a rotating arm, a wheeled platform — imposes physical-safety obligations that software alone cannot satisfy. Three features are non-negotiable for any moving robotic prototype in this course, and in professional practice.

Figure 9.3 identifies all three safety features in the running-example workspace.




Figure 9.3: Sorter-node robot workspace. The exclusion zone (hatched) around the conveyor and sort gate is bounded by physical guarding (solid line). The e-stop button is positioned in the operator zone, outside the guarding, and its normally-closed contact sits in series with the motor power rail. The fail-safe state (conveyor stopped, gate centred) is the power-off default.

9.6.1 Emergency Stop

An **emergency stop (e-stop)** is a hardware mechanism — not a software function — that removes power from every actuator when activated. The key word is hardware: a normally-closed (NC) relay or contactor in series with the motor power supply that opens when the e-stop button is pressed or when the button circuit is broken.

A software e-stop (a flag checked in the main loop, an interrupt service routine that calls `motor_stop()`) does not satisfy this requirement. If the firmware crashes, the stack overflows, or a runaway interrupt handler locks the scheduler, the software e-stop cannot execute. The hardware relay opens regardless of firmware state.

Requirements for the running example:

- One NC e-stop button accessible from the operator zone, outside the guarding perimeter.
- The e-stop contact in series with the 12 V motor supply rail.
- Latching action: the system must not restart when the button is released; it requires a deliberate reset after the hazard has been cleared.

9.6.1.0.1 In Practice. A robot prototype during a lab test had only a software e-stop. During a firmware crash, the motor continued running and drove the conveyor belt into its mechanical end-stop. The belt was damaged and the test had to be postponed. A normally-closed hardware relay in the motor power path would have cut power the instant the crash was detected by the watchdog — or the moment a person reached for the e-stop button.

9.6.2 Guarding

Guarding is a physical barrier that prevents unintended contact between a person and a moving part. Guarding is not a “nice to have”; under Québec’s Act Respecting Occupational Health and Safety (LSST) and the federal *Canada Labour Code*, any moving part that presents a hazard must be guarded or rendered inaccessible.

For the bench-scale sorter prototype, acceptable guarding includes:

- Acrylic or aluminium side panels along the conveyor belt that prevent fingers from reaching the belt, rollers, or sort gate during operation.
- An interlocked access panel: if the panel is opened, the interlock opens the motor power circuit (the same NC relay used by the e-stop).
- A minimum guarding height that prevents reaching over the barrier to the nearest pinch point.

Guarding must be specified in your design records as a dimensional requirement, not a verbal intention. State the material, minimum dimensions, and mounting method.

9.6.3 Fail-Safe State

A **fail-safe state** is the physical state the system enters when power is removed or a fault is detected. Designing the fail-safe state requires an explicit decision: what position should every actuator reach when power is cut?

For the sort gate actuator, the fail-safe state must be the centred (neutral) position. This means the actuator spring-returns to centre on power loss, not to the “sort left” or “sort right” extreme. For the conveyor motor, the fail-safe state is stopped. This is achieved by using a spring-return actuator and a motor driver that de-energises the motor on power loss, not one that holds its last commanded position.

Use this three-question checklist for each actuator:

1. What is the safest physical position on power loss?
2. Does the mechanism reach that position by gravity, spring return, or active braking?
3. Is the power-off default that position, or does it require a commanded move?

If the power-off default is not the safest position, redesign the mechanism or add a spring return.

9.6.4 Force, Speed Limits, and Human-Robot Interaction Zones

Beyond the three required features, professional practice for moving prototypes includes **force and speed limits**: the maximum force an actuator can exert and the maximum speed at which it can move when a person might be present.

For the bench sorter, define:

- A maximum conveyor belt speed (e.g., 0.3 m/s) that limits the kinetic energy of items being sorted and reduces the risk of ejection.
- A maximum sort-gate actuator force consistent with the SF calculation below.
- A **human-robot interaction (HRI) zone**: the area within which a person might reach the moving parts during normal operation. This zone determines the guarding perimeter.

9.7 Mechanical Safety Factor

Every load-bearing element in a moving prototype must be verified against a minimum **safety factor** SF:

$$SF = \frac{\text{capacity}}{\text{applied load}} \quad (9.3)$$

where capacity is the maximum load the element can sustain before failure (from material data or simulation) and applied load is the worst-case force the element will experience in service. The course minimum is $SF \geq 2$; this means the element can carry at least twice the worst-case load before failure. Any element that fails this criterion requires a redesign before it is installed in a moving prototype.

9.7.1 Worked Example — Safety Factor

The sort-gate actuator bracket is 3D-printed PLA. The bracket supports the actuator mass of 0.45 kg. During a misfire event (the sort gate attempts to move while an item is lodged in the mechanism), the impact load is estimated at $3\times$ the static weight.

Step 1: Compute the applied load.

$$F_{\text{applied}} = 3 \times 0.45 \text{ kg} \times 9.81 \text{ m/s}^2 = 3 \times 4.4145 \text{ N} = 13.24 \text{ N}$$

Step 2: Compute the capacity.

From the material specification for this PLA print orientation and infill density, the tensile strength is 35 MPa. The bracket cross-section area at the critical section is 2.0 mm^2 .

$$F_{\text{capacity}} = 35 \text{ MPa} \times 2.0 \text{ mm}^2 = 35 \text{ N/mm}^2 \times 2.0 \text{ mm}^2 = 70 \text{ N}$$

Step 3: Compute SF.

$$SF = \frac{70 \text{ N}}{13.24 \text{ N}} = 5.29$$

$SF = 5.29 \geq 2$ — the bracket passes.

Sensitivity check — reduced cross-section.

If the design were modified to reduce the cross-section to 0.5 mm^2 (to save material or to route a cable channel through the bracket):

$$F'_{\text{capacity}} = 35 \times 0.5 = 17.5 \text{ N}$$

$$SF' = \frac{17.5}{13.24} = 1.32 < 2 \Rightarrow \text{FAILS}$$

A cross-section of 0.5 mm^2 fails the safety criterion. The bracket must be re-designed — wider cross-section, different geometry, or a different material with higher tensile strength — before it is used. Record the failing calculation and the redesign rationale in your design records; Gate 4 reviewers will check that every load-bearing element has a documented SF.

9.8 EMC, ESD, PPE, and Regulatory Obligations

Three additional safety disciplines are absorbed into Stage 3 practice: EMC/ESD design, personal protective equipment (PPE) in the lab, and applicable safety law.

9.8.1 EMC and ESD

Electromagnetic compatibility (EMC) means that the device neither emits interference above regulated limits nor fails when exposed to external interference. For a prototype, the principal EMC obligation at Stage 3 is design hygiene: decoupling capacitors on every power rail close to each IC, ground planes on the PCB, and cable routing that minimises loop area. These are not certification activities; they are design habits that prevent self-interference and reduce the cost of formal EMC testing later.

Electrostatic discharge (ESD) protection means that the design can survive the voltage spikes generated by a person touching the device. Every I/O pin that is accessible in normal use should have TVS diode protection or an ESD-rated I/O expander. For the sorter node, this includes the MQTT status LED pins and the sort-gate actuator control lines.

9.8.2 Lab PPE

Personal protective equipment (PPE) requirements during prototype assembly and testing:

- Safety glasses during all power-on testing of circuits above 30 V DC or any circuit with capacitors above 100 μF .
- Anti-static wrist strap when handling bare PCBs or ICs outside of anti-static packaging.
- No loose clothing or jewellery within the guarded zone of the conveyor during any belt-speed test above 0.1 m/s.

These are documented in the Vanier College laboratory safety rules and in the course safety briefing. They are also design inputs: if the prototype requires testers to work near exposed moving parts, the guarding design is incomplete.

9.8.3 Applicable Safety Law

Three regulatory frameworks apply to the running example:

- **Québec LSST** (Act Respecting Occupational Health and Safety): requires guarding of all hazardous moving parts and a means of stopping the machine in an emergency.

- **Canada Labour Code Part II:** requires that every employer ensure that equipment is safe and that workers are informed of known hazards.
- **IEC 62368-1** (Audio/video, information and communication technology equipment — Safety requirements): the applicable IEC product safety standard for the electronic components in the sorter system. Compliance is not required for a prototype, but the standard's hazard-based safety engineering methodology is the reference model for Stage 3 safety decisions.

These frameworks do not require certification for a class prototype. They do require that you are aware of the obligations a product built from this prototype would carry, and that your design decisions are consistent with meeting those obligations.

9.8.3.0.1 Common Pitfalls. Omitting ESD protection on accessible I/O pins. A single unprotected pin touched during a live test can latch a microcontroller into an undefined state silently — no error, no crash, just corrupted peripheral registers. TVS diodes cost pennies and are impossible to retrofit onto a finished PCB without a re-spin.

9.9 Try It Yourself

A wireless CO₂ sensor node has the following parameters: $I_{\text{active}} = 45 \text{ mA}$, $I_{\text{sleep}} = 0.08 \text{ mA}$, $D = 0.05$ (the node wakes for a 3-s measurement cycle every 60 s), $C_{\text{batt}} = 1200 \text{ mAh}$. A mounting bracket (aluminium, tensile capacity in this cross-section = 120 N) supports the sensor mass of 0.30 kg. The bracket experiences a peak load of $4\times$ the static weight during installation impact.

- Compute I_{avg} using Equation 9.1. Show every arithmetic step.
- Compute t_{life} using Equation 9.2. Express your answer in hours and in days.
- The team switches to a lower-power radio that reduces I_{active} to 20 mA while keeping $D = 0.05$. Recompute I_{avg} and t_{life} . What is the percentage improvement in battery life compared to part (b)?
- Compute the peak applied force in Newtons (use $g = 9.81 \text{ m/s}^2$), then compute SF for the bracket using Equation 9.3. Does the bracket pass the $\text{SF} \geq 2$ criterion?

9.10 Review Questions

- Q1. (*Conceptual*) Identify the three IoT attack surfaces from Section 9.2. For each, give one security control that applies specifically to the running-example MQTT sorter node.
- Q2. (*Conceptual*) Explain why designing security in at Stage 3 costs less than retrofitting it at Stage 4. Use the cost-of-change principle from Chapter 3 to support your

argument. Your answer should address at least one concrete technical reason (not just “it takes longer”).

- Q3. (*Applied, calculation*) An IoT sensor has $I_{\text{active}} = 120 \text{ mA}$, $I_{\text{sleep}} = 0.02 \text{ mA}$, $D = 0.03$, $C_{\text{batt}} = 3000 \text{ mAh}$.
- Compute I_{avg} using Equation 9.1.
 - Compute t_{life} in hours and days using Equation 9.2.
 - The team wants $t_{\text{life}} \geq 90$ days (2160 h). What is the maximum duty cycle D that achieves this? Show your algebraic derivation starting from Equations 9.1 and 9.2.
- Q4. (*Applied, multi-step*) A 3D-printed PLA conveyor guide bracket supports a hanging load of 0.80 kg. Peak impact load = $5 \times$ static weight. PLA tensile strength = 42 MPa.
- Compute the peak applied force (use $g = 9.81 \text{ m/s}^2$).
 - The bracket cross-section is 3.5 mm^2 . Compute the structural capacity in Newtons.
 - Compute SF using Equation 9.3. Does it pass the $\text{SF} \geq 2$ criterion?
 - If the criterion is raised to $\text{SF} \geq 3$, what minimum cross-section area is required? Show the algebra.
- Q5. (*Conceptual*) Identify the three required physical-safety features from Section 9.6 for a moving robotic prototype. For each feature, explain what failure mode it prevents and why a software-only implementation of that feature is insufficient.

Portfolio Entry

Update your design records with three entries. Each entry is a section of your prototype documentation package and will be audited at Gate 3.

- Security design decisions* — protocol choice (MQTT over TLS, CoAP with DTLS, or BLE with LE Secure Connections), authentication method (per-device credentials or client certificates), and credential management policy (how credentials are generated, stored, distributed, and revoked).
- Power budget table* — I_{active} , I_{sleep} , D , I_{avg} , C_{batt} , t_{life} , and at least one sensitivity row (e.g., halved duty cycle or reduced sleep current).
- Safety design decisions* — e-stop type, location, and wiring diagram; guarding specification (material, dimensions, mounting method); fail-safe state definition for every actuator; and SF calculation for all load-bearing elements, with cross-section area and material data cited.

Chapter Summary

Chapter 9 treated security and physical safety as quantitative Stage 3 obligations, not qualitative afterthoughts. The quantitative tools this chapter introduced are:

- $I_{avg} = D \cdot I_{active} + (1 - D) \cdot I_{sleep}$ and $t_{life} = C_{batt} / I_{avg}$ — the power budget that determines whether your duty-cycle design meets the battery-life requirement.
- $SF = \text{capacity} / \text{applied load}$ — the structural safety floor, with $SF \geq 2$ required for every load-bearing element in a moving prototype.

The three non-negotiable physical-safety features for any moving prototype are: a hardware e-stop in the motor power path, physical guarding around every hazardous moving part, and a documented fail-safe state for every actuator.

Chapter 9 produced three design-record entries — a security design decision log, a power budget table, and a safety design decision log — that together bound every Stage 3 hardware commitment. Chapter 10 takes those entries as inputs and organises the build into a schedule: a work breakdown structure, a critical path, and a Gantt chart that makes Gate 3 achievable rather than aspirational.

PLANNING & SCHEDULE MANAGEMENT

10.0.0.0.1 Where this fits. This chapter is a **Stage 3 (Development)** deliverable. A realistic project schedule and an updated risk register are **Gate 3** artefacts; a schedule built on optimistic guesses or missing lead times is a gate failure *before* the prototype is assembled.

Chapter 9 established the electrical and safety architecture of the IoT robotic sorting subsystem: the power budget confirmed a 50.5-day battery life at $I_{avg} = 1.649$ mA, and the safety design log recorded a load-path safety factor of $SF = 5.29$. That work left one critical question unanswered: *in what order does the team build everything, and when will it be done?* This chapter answers that question. You will decompose the build into a Work Breakdown Structure, link activities with dependencies, identify the critical path, handle procurement lead times as explicit schedule risks, and finish with a Gantt chart and an updated risk register.

10.0.0.0.2 Learning Objectives. By the end of this chapter you will be able to:

1. Identify all project activities, organise them into a **Work Breakdown Structure** (WBS), and determine the critical path using the Critical Path Method (CPM).
2. **Build** a Gantt chart from CPM results, annotating critical-path bars, slack extensions on non-critical activities, and milestone markers.
3. Compute early/late start and finish times, slack, and the critical path for a multi-activity network.
4. Estimate activity durations under uncertainty by applying the PERT three-point formula and interpreting the resulting standard deviation.
5. Maintain a living risk register that treats procurement lead times and supplier delays as first-class schedule risks.

10.1 Work Breakdown Structure

A **Work Breakdown Structure** (WBS) is a hierarchical decomposition of all the work required to complete the project. Every leaf node of the WBS is a **work package**: a discrete, assignable, and estimable unit of effort.

10.1.1 Why decompose first?

Dependencies, durations, and risks can only be managed once work is visible. A single task labelled “build the prototype” cannot be scheduled, assigned, or monitored. Breaking it into atomic work packages — PCB design, component procurement, firmware integration, system test — makes each element plannable and observable.

10.1.2 WBS for the sorter prototype

The sorter build decomposes into two top-level branches: *Hardware* and *Software*. Under Hardware the packages are PCB design (A), component procurement (B), PCB fabrication (C), and PCB assembly (D). Under Software the packages are firmware integration (E). System test (F) spans both branches and sits at the integration level.

Table 10.1: WBS work packages for the sorter prototype build.

ID	Work package	Duration (d)	Predecessors
A	PCB design	3	—
B	Component procurement	7	A
C	PCB fabrication	5	A
D	PCB assembly	2	B, C
E	Firmware integration	4	A
F	System test	3	D, E

10.1.2.0.1 In Practice. WBS depth should match the team’s ability to estimate and track. For a four-week prototype sprint, work packages of one to five days are practical; packages longer than a week are usually hiding sub-tasks that carry independent risks.

10.2 Dependencies and Critical Path

10.2.1 Activity-on-node notation

In the **Critical Path Method** (CPM) each work package is drawn as a node and each dependency as a directed arc from predecessor to successor. Figure 10.1 shows the six-activity network for the sorter build; the critical path is highlighted with bold arcs.

10.2.2 Forward pass — earliest start and finish

The **early start** (ES) of an activity is the earliest day on which it can begin, given all predecessors are complete. The **early finish** (EF) is: $EF = ES + \text{duration}$.

Processing the network from left to right:

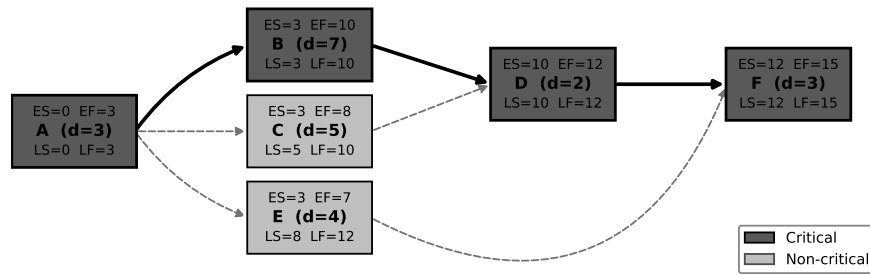


Figure 10.1: Activity-on-node CPM network for the sorter prototype build. Bold arcs mark the critical path $A \rightarrow B \rightarrow D \rightarrow F$ (15 days). Numbers inside each node show ES/EF on the top row and LS/LF on the bottom row.

- (A) $ES_A = 0$; $EF_A = 0 + 3 = 3$
 (B) $ES_B = EF_A = 3$; $EF_B = 3 + 7 = 10$
 (C) $ES_C = EF_A = 3$; $EF_C = 3 + 5 = 8$
 (D) $ES_D = \max(EF_B, EF_C) = \max(10, 8) = 10$; $EF_D = 10 + 2 = 12$
 (E) $ES_E = EF_A = 3$; $EF_E = 3 + 4 = 7$
 (F) $ES_F = \max(EF_D, EF_E) = \max(12, 7) = 12$; $EF_F = 12 + 3 = 15$

The **project duration** is $T = EF_F = 15$ days.

10.2.3 Backward pass — latest start and finish

The **late finish** (LF) of an activity is the latest day by which it must finish without delaying the project. The **late start** (LS) is: $LS = LF - \text{duration}$.

Processing right to left (setting $LF_F = 15$):

- (F) $LF_F = 15$; $LS_F = 15 - 3 = 12$
 (D) $LF_D = LS_F = 12$; $LS_D = 12 - 2 = 10$
 (E) $LF_E = LS_F = 12$; $LS_E = 12 - 4 = 8$
 (C) $LF_C = LS_D = 10$; $LS_C = 10 - 5 = 5$
 (B) $LF_B = LS_D = 10$; $LS_B = 10 - 7 = 3$
 (A) $LF_A = \min(LS_B, LS_C, LS_E) = \min(3, 5, 8) = 3$; $LS_A = 3 - 3 = 0$

10.2.4 Slack and the critical path

Slack (also called float) is the amount by which an activity can be delayed without extending the project:

$$\text{slack} = LS - ES = LF - EF \quad (10.1)$$

Applying Equation 10.1 to each activity:

Table 10.2: CPM results for the sorter prototype build.

ID	Package	Dur	ES	EF	LS	LF	Slack	Critical?
A	PCB design	3	0	3	0	3	0	Yes
B	Component procurement	7	3	10	3	10	0	Yes
C	PCB fabrication	5	3	8	5	10	2	No
D	PCB assembly	2	10	12	10	12	0	Yes
E	Firmware integration	4	3	7	8	12	5	No
F	System test	3	12	15	12	15	0	Yes

The **critical path** consists of every activity with zero slack. Here that is **A → B → D → F**, with a total duration of $3 + 7 + 2 + 3 = 15$ days.

The competing path **A → C → D → F** spans only $3 + 5 + 2 + 3 = 13$ days, giving C a slack of 2 days. Path **A → E → F** spans $3 + 4 + 3 = 10$ days, giving E a slack of 5 days.

10.2.4.0.1 Common Pitfalls. A common error is to identify the critical path as the sequence containing the *longest single task*. Activity B (7 days) is the longest task, but the critical path is defined by *total path length*, not individual activity duration. A short activity with zero slack (e.g., PCB assembly at 2 days) is just as critical as the longest one.

10.3 Gantt Scheduling

A **Gantt chart** maps each work package to a horizontal bar on a calendar timeline. It communicates planned start and finish dates, parallel tracks, and milestones to every stakeholder — and it must be updated as actuals deviate from plan.

Figure 10.2 shows the Gantt chart for the sorter build derived directly from the CPM results in Table 10.2. Activities on the critical path (A, B, D, F) are shown with solid dark bars; non-critical activities (C, E) are shown with lighter bars and their slack is visible as an extension to the right of each bar. Milestones (PCB design complete at day 3; integration ready at day 12; system test complete at day 15) are marked with diamond symbols.

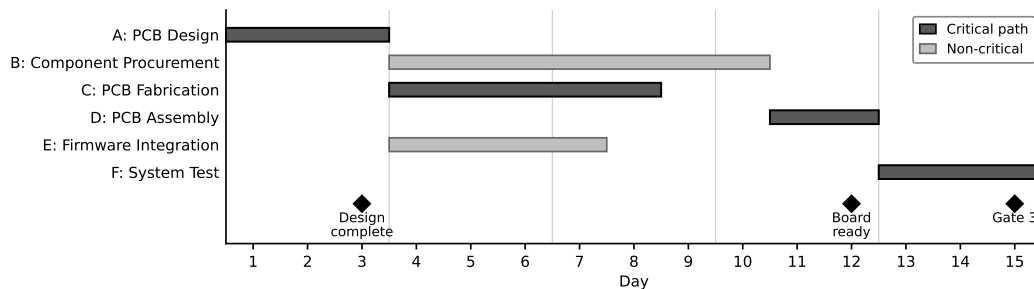


Figure 10.2: Gantt chart for the sorter prototype build (15 days). Solid dark bars are critical-path activities; lighter bars are non-critical activities. The dashed extensions to the right of C and E indicate their available slack (2 days and 5 days, respectively). Diamond markers denote milestones.

10.3.1 Keeping the Gantt alive

A Gantt chart is not a snapshot taken once at project kickoff; it is a **living document** updated at every weekly check-in. When Activity B (component procurement) slips by even one day, the entire critical path extends by the same amount. Teams that file the Gantt after sprint planning and never revisit it are the ones who discover a two-week slip the day before their gate review.

10.3.1.0.1 In Practice. Use colour or line-weight to distinguish planned bars from actual progress bars. Add a *today* vertical line so any reader can immediately see what is late. In a four-person prototype team, a shared spreadsheet Gantt updated every Monday morning is sufficient; dedicated project management software adds value only when the WBS exceeds roughly 20 work packages.

10.3.1.0.2 Common Pitfalls. When the Gantt is updated but the critical path is not re-evaluated, the team gains false reassurance: the bars move but the slip remains invisible. Any change to a critical-path activity duration must trigger an immediate recalculation of the project end date.

10.4 PERT Three-Point Estimation

CPM uses single-point duration estimates. For activities with high uncertainty — particularly procurement — that single number conceals the real range of outcomes. The **Program Evaluation and Review Technique** (PERT) replaces the single estimate with three:

- *a* — **optimistic**: the duration if everything goes well.
- *m* — **most likely**: the mode of the distribution; the single best estimate.
- *b* — **pessimistic**: the duration if most things go wrong (short of catastrophe).

10.4.1 PERT Formulas

The **PERT expected duration** is a weighted average placing four times the weight on the most-likely estimate:

$$t_e = \frac{a + 4m + b}{6} \quad (10.2)$$

The **PERT standard deviation** quantifies the spread of the estimate:

$$\sigma = \frac{b - a}{6} \quad (10.3)$$

A large σ warns the team that this activity is a schedule risk even if the expected duration looks acceptable.

10.4.2 Worked example: Activity B (component procurement)

Component procurement is the highest-uncertainty activity on the critical path. The team estimates:

- $a = 4$ days (supplier has parts in stock, ships next day)
- $m = 7$ days (typical online order with standard shipping)
- $b = 14$ days (back-order delay or customs hold)

Applying Equation 10.2:

$$t_e = \frac{4 + 4(7) + 14}{6} = \frac{4 + 28 + 14}{6} = \frac{46}{6} \approx 7.67 \text{ days}$$

The CPM single-point estimate of 7 days is slightly optimistic; the PERT-adjusted estimate of 7.67 days should be used in any schedule risk analysis.

Applying Equation 10.3:

$$\sigma = \frac{14 - 4}{6} = \frac{10}{6} \approx 1.67 \text{ days}$$

A standard deviation of 1.67 days on a critical-path activity means there is a realistic scenario in which the project finishes two or more days late. This uncertainty must appear in the risk register (Section 10.6).

Figure 10.3 illustrates the three-point distribution for Activity B with t_e and σ annotated.




Figure 10.3: PERT distribution for Activity B (component procurement) with $a = 4$ d, $m = 7$ d, $b = 14$ d. The expected duration $t_e \approx 7.67$ d is shifted right of the mode because the pessimistic tail is longer. The $\pm 1\sigma$ band (≈ 1.67 d) spans from roughly 6.0 d to 9.34 d.

10.4.2.0.1 In Practice. The asymmetry in the PERT formula ($t_e > m$ when the pessimistic tail is longer) is intentional and well-founded: in practice, activities almost always run long rather than short. When gathering three-point estimates from team members, ask for the pessimistic estimate last — people systematically underestimate bad scenarios when they anchor on the most-likely value first.

10.5 Lead Time as a Planning Risk

Lead time is the elapsed calendar time between placing a component order and having parts in hand. It is not “somebody else’s problem” — it is a first-class **schedule risk** that must be modelled explicitly in the network.

10.5.1 Why lead time matters on the critical path

In the sorter schedule, Activity B (component procurement, $t_e = 7.67$ d) sits on the critical path. If the team waits until PCB design is complete before placing an order, every day of procurement delay directly delays system test. There is no buffer.

Several mitigation strategies are available:

1. **Preliminary BOM early.** Draft a provisional Bill of Materials during detailed design (Chapter 11) and place orders before Activity A is finished. This converts B from a strict successor of A into a partial overlap, shortening the critical path.
2. **Pre-qualify multiple suppliers.** If the primary supplier quotes a 14-day lead time, a secondary supplier at 7 days keeps the schedule intact.
3. **Order buffer stock.** For inexpensive passive components (resistors, capacitors) the cost of ordering 10% extra is negligible compared to a one-week slip caused by a mis-soldered component that cannot be replaced.
4. **Expedite only as a last resort.** Expediting fees are expensive; build the schedule so that expediting is never needed.

10.5.2 Long-lead items deserve their own register entries

Any component with a quoted lead time greater than the slack of its downstream path belongs in the risk register as its own entry, with a named owner and a specific mitigation plan. For the sorter, the microcontroller (if on back-order) and the motor driver IC are the most likely culprits.

10.5.2.0.1 Common Pitfalls. Teams frequently omit lead time from the schedule entirely, treating procurement as an instantaneous event. The result is a day-one crisis: design is “done” but parts will not arrive for ten days and the project duration instantly extends. Schedule the lead time explicitly, with the same three-point PERT estimate as any other uncertain activity.

10.6 Maintaining the Risk Register

A **risk register** is a living table that catalogues every identified threat to project objectives, its likelihood, its impact, and the mitigation strategy the team has chosen. It was introduced in Stage 2 with technical risks (Chapter 7). At Stage 3 it must grow to include **schedule risks** and **procurement risks**.

10.6.1 Standard register fields

Each row in the register should carry:

1. **ID** — a stable reference code (e.g., R-SCH-01).
2. **Description** — one sentence naming the risk event.
3. **Likelihood** — Low / Medium / High (or 1–5 scale).
4. **Impact** — Low / Medium / High (or 1–5 scale).
5. **Risk score** — Likelihood × Impact.
6. **Mitigation** — the specific action the team will take.
7. **Owner** — the team member responsible.
8. **Status** — Open / In progress / Closed.

10.6.2 Schedule-specific risks for the sorter build

Table 10.3: Gate 3 risk register entries for the sorter prototype schedule.

ID	Description	L	I	Mitigation
R-SCH-01	Component procurement (Act. B) exceeds 7 days due to supplier back-order, delaying system test.	M	H	Pre-qualify secondary supplier; place order before PCB design is finalised.
R-SCH-02	PCB fabrication house queue delay extends Act. C beyond 5 days.	L	M	Use local fab service with 3-day turnaround as fallback; ≥ 2 days slack available.
R-SCH-03	Firmware integration (Act. E) blocked by undiscovered hardware bug discovered at Act. D, requiring design iteration.	M	H	Daily smoke-test of assembled PCB before firmware handoff; maintain 5 days slack on Act. E.
R-SCH-04	Gate 3 review scheduled on day 14; project duration is 15 days — one-day slip causes missed gate.	M	H	Move gate review to day 16; flag to supervisor immediately if Act. B slips by > 1 day.

10.6.3 How often to update

The risk register should be reviewed at every weekly team meeting, in the same session as the Gantt update. Risks change status: a component that was “in stock” last week may be back-ordered today. Close a risk only when its triggering condition can no longer occur; do not close it because the team has stopped worrying about it.

10.6.3.0.1 In Practice. At Gate 3 reviewers will scan the register for *completeness* (have schedule and procurement risks been added since Gate 2?) and *actionability* (do mitigations name a specific person and a specific action?). Vague entries such as “monitor the situation” are not mitigations; they are placeholders that signal the team has not thought through the risk.

Try It Yourself

The following five-activity network describes a sensor-node firmware release.

Table 10.4: Try It Yourself: firmware release work packages.

ID	Work package	Duration (d)	Predecessors
P	Requirements review	2	—
Q	Driver development	6	P
R	Unit testing	3	P
S	Integration testing	4	Q, R
T	Documentation & release	2	S

1. Perform the forward and backward pass to find ES, EF, LS, LF, and slack for every activity.
2. Identify the critical path and state the project duration.
3. Activity Q (driver development) has three-point estimates $a = 3$ days, $m = 6$ days, $b = 12$ days. Use Equations 10.2 and 10.3 to compute t_e and σ . Substitute t_e for the activity’s duration, recompute the total length of each path through the network, and state whether the critical path changes. Show both path lengths explicitly.
4. Add one schedule risk for this network to a risk register, following the format of Table 10.3.

(No answer key provided.)

Review Questions

1. **(Conceptual)** Explain in your own words why the critical path is defined by activities with zero slack rather than by the activity with the longest duration. Give an example where the longest individual activity is *not* on the critical path.
2. **(Conceptual)** A team builds a Gantt chart on the first day of the sprint and does not update it for three weeks. Identify two specific ways in which this practice can cause a gate failure.
3. **(Applied)** A project has four activities: W (4 d, no predecessors), X (3 d, predecessor W), Y (6 d, predecessor W), Z (2 d, predecessors X and Y). Compute ES, EF, LS, LF, and slack for each activity. State the critical path and project duration.

4. **(Applied)** Activity Y above has three-point estimates $a = 5$ days, $m = 6$ days, $b = 10$ days. Compute t_e and σ using Equations 10.2 and 10.3. If the PERT-adjusted duration is used in place of 6 days, does the critical path change? Justify your answer numerically.
5. **(Applied — multi-step)** A project has five activities: J (3 days, no predecessors); K (6 days, predecessor J); L (4 days, predecessor J); M (2 days, predecessors K and L); N (3 days, predecessor M).
 - (a) Perform the forward and backward pass. Record ES, EF, LS, LF, and slack for every activity.
 - (b) State the critical path and project duration.
 - (c) Activity K has three-point estimates $a = 4$ days, $m = 6$ days, $b = 13$ days. Compute t_e and σ using Equations 10.2 and 10.3.
 - (d) Write a complete eight-field risk-register entry for the risk that Activity K exceeds its pessimistic estimate.

Portfolio Entry

Gate 3 deliverables produced in this chapter:

- (a) **Gantt chart** — A calendar-based bar chart showing all six work packages, their planned start and finish days, the critical path highlighted, slack extensions on non-critical activities, and milestone markers at days 3, 12, and 15. The chart is a living document; it must be updated at every team meeting with actual progress.
- (b) **Updated risk register** — The Stage 2 technical risk register (from Chapter 7) extended with the four schedule and procurement risks in Table 10.3. Each new entry carries a unique R-SCH-XX identifier, a named owner, and a specific — not vague — mitigation action. Submit the register as part of the Gate 3 package alongside the Gantt chart.

Chapter Summary

This chapter transformed the sorter team's verified design into a buildable, trackable plan:

1. A **Work Breakdown Structure** decomposed the build into six atomic work packages (A through F), each assignable and estimable.
2. The **CPM forward and backward pass** produced early/late start and finish times for every activity. Applying Equation 10.1 revealed that A, B, D, and F carry zero slack, making $A \rightarrow B \rightarrow D \rightarrow F$ the 15-day critical path.
3. A **Gantt chart** (Figure 10.2) mapped the schedule to a calendar timeline. It must be updated weekly; a static Gantt is a liability, not an asset.

4. **PERT** three-point estimation (Equations 10.2 and 10.3) quantified the uncertainty in Activity B: $t_e \approx 7.67$ days, $\sigma \approx 1.67$ days — a warning that the critical path carries real schedule risk.
5. **Lead time** is a first-class schedule risk: placing orders before PCB design is finalised and pre-qualifying secondary suppliers are the primary mitigations.
6. The **risk register** was extended with four schedule-specific entries (Table 10.3), meeting the Gate 3 completeness requirement.

You now have a Gantt chart and an updated risk register — the two deliverables required for Gate 3 sign-off. Chapter 11 takes that risk register and the project schedule as its starting point and builds the full Bill of Materials and procurement chain, turning the component list implicit in Activity B into a concrete sourcing plan with part numbers, quantities, costs, and supplier alternatives.

BILL OF MATERIALS & PROCUREMENT

11.0.0.0.1 Where this fits. This chapter operates at Stage 3 (Development), targeting Gate 3. The Stage-Gate model requires that every Gate 3 review package include a *costed* BOM: a document that ties every physical part to a quantity, a unit price, a supplier, and a lead time. An uncosted or incomplete BOM cannot support the business case that Gate 3 demands — no reviewer can approve a prototype budget without knowing what it costs to build.

11.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Build a multi-level costed BOM with correct reference designators, quantities, unit costs, extended costs, and supplier information.
2. Derive a purchase list from the BOM and compare supplier quotes on both unit price and lead time.
3. Manage the full procurement document chain: purchase order, receipt, invoice verification, and as-built reconciliation.

Knowing *when* work happens (the Gantt chart from Chapter 10) and what could go wrong (the risk register) is only actionable once you know what to order, from whom, at what price, and within what lead time. This chapter provides that foundation.

11.1 BOM as a Design Document

A **bill of materials** (BOM) is not a shopping list. It is a design document that captures the complete set of physical parts required to build one unit of the system, together with the quantities, reference designators, unit costs, and supply-chain metadata necessary to procure and assemble those parts. The distinction matters: a shopping list can be incomplete without consequences until you arrive at the checkout; an incomplete BOM discovered during assembly halts production, delays the schedule, and invalidates cost estimates already submitted to the Gate 3 review.

11.1.1 BOM Levels

A **multi-level BOM** structures the system hierarchically: the top level names the assembled product; the second level names subsystems or subassemblies; the lowest level names individual purchased or manufactured components. This structure mirrors the system architecture developed in Chapter 5 and makes it possible to roll costs up by subsystem, identify which assembly contributes most to total cost, and manage procurement independently for each assembly team.

Figure 11.1 shows the multi-level BOM tree for the IoT robotic sorting subsystem. The top level is the complete sorter. The second level contains three subsystems: Control, Actuation, and Structure. The third level contains the individual line items.




Figure 11.1: Multi-level BOM tree for the IoT robotic sorting subsystem. The top-level assembly (Sorter) decomposes into three subsystems (Control, Actuation, Structure), each of which decomposes into individual purchased components at Level 3. Reference designators (U1, U2, Q1, M1, B1, B2, H1) appear at the leaf nodes.

11.1.2 BOM Fields

Every BOM line requires at minimum:

- Reference designator** — the unique identifier linking the BOM line to the schematic or assembly drawing (e.g., U1, Q1, M1). A line without a designator cannot be placed on a board or found in an assembly drawing.
- Description and part number** — the manufacturer part number (MPN) is the only unambiguous identifier. A description without an MPN allows the assembler to substitute any part that “sounds like” the intended one.
- Quantity per assembly** (q_i) — the number of that part needed to build one unit.
- Unit cost** (u_i , in CAD) — the price paid per single piece at the procurement quantity.
- Extended cost** — $q_i \times u_i$, the total spend on that line for one assembly.
- Preferred supplier and part number** — the distributor from whom the part will be ordered, with the distributor’s stock number.
- Lead time** — the calendar days from order placement to receipt, used to back-schedule the procurement milestone in the Gantt chart.

- (h) **Alternate part** — a second-source MPN that satisfies parametric equivalence and footprint compatibility, mitigating single-source risk identified in the risk register.

11.1.2.0.1 In Practice. A team building the sorter prototype omitted reference designators from the BOM because the schematic had not been finalised when the BOM was started. At assembly, the PCB had two footprint-compatible motor drivers with different pinouts. Without the designator, the assembler soldered the wrong driver onto U2, applying power in the wrong sequence and destroying the part. The loss was \$18 and two days of schedule. Reference designators must be locked before the BOM is submitted, not after.

11.1.3 The Alternate-Part Column

Single-sourced components are a procurement liability. If the sole supplier for a critical part is out of stock, the project stalls. Every BOM line for a component that is not a commodity (i.e., not a standard resistor, capacitor, or fastener available from every distributor) should carry a vetted alternate: a second MPN confirmed to be parametrically equivalent, footprint-compatible, and in Active lifecycle status. Chapter 6 described the process for qualifying a second source; the BOM is where that work is recorded and made visible to reviewers.

11.2 Purchase List from BOM

A **purchase list** is derived from the BOM by collapsing identical MPNs that appear in different subsystems into a single line and then computing the order quantity for each line. The purchase list is the document you send to a supplier or purchasing department; it is not the BOM itself.

11.2.1 Order Quantity with Overage

For passive components and consumables — resistors, capacitors, solder, heat-shrink — the risk of loss during assembly justifies ordering more than the exact quantity the BOM requires. The **order quantity with overage** is:

$$q_i^{\text{order}} = \lceil (1 + \alpha) q_i \rceil \quad (11.1)$$

where q_i is the BOM quantity, α is the fractional overage (a dimensionless value between 0 and 1, e.g., $\alpha = 0.10$ for 10% overage), and $\lceil \cdot \rceil$ denotes the ceiling function (round up to the nearest whole unit). The ceiling is necessary because you cannot order a fractional part.

Overage is *not* applied blindly to every line. Expensive unique components — the MCU board, the motor driver IC, the enclosure — are ordered to exact BOM quantity, possibly with one spare unit explicitly approved by the project manager.

Applying 10% overage to a \$65 MCU board would order an unneeded extra unit and misrepresent the budget.

11.2.1.0.1 Common Pitfalls. Teams sometimes apply overage to the BOM quantity used for cost estimation, inflating C_{BOM} . Overage belongs only on the purchase list, applied to q_i^{order} ; the BOM cost calculation always uses the exact per-assembly quantity q_i .

11.3 Quotes and Supplier Comparison

A **request for quotation** (RFQ) specifies the MPN, the order quantity, the required delivery date, and the delivery address; send one to at least two suppliers for every non-commodity line item before committing to a purchase order.

11.3.1 What to Compare

Quote comparison is not a simple lowest-price sort. The relevant criteria are:

- (a) **Unit price at your order quantity** — distributor pricing is typically tiered; the unit price at quantity 1 may be three times the price at quantity 10. Always quote at the quantity you intend to order.
- (b) **Lead time** — a part that is \$2.00 cheaper but arrives four weeks later may miss the assembly milestone and delay Gate 3. Lead time must be evaluated against the Gantt chart, not in isolation.
- (c) **Stock availability** — a listed unit price is irrelevant if the distributor has zero units in stock. Confirm “in-stock” quantity at time of RFQ.
- (d) **Minimum order quantity** (MOQ) — some distributors impose a minimum order of 5 or 10 units for certain components. The effective cost per unit changes when the MOQ exceeds your order quantity.
- (e) **Shipping and handling** — a \$1.50 unit price advantage is erased by a \$15 shipping surcharge on a small order.

The procurement document chain that connects the BOM to payment is shown in Figure 11.2.

11.4 Purchase Orders

A **purchase order** (PO) is a formal document that authorises a supplier to ship specific goods at a specific price. It is a legal instrument: once a supplier accepts a PO, both parties are bound by its terms. For student projects, purchase orders are often replaced by a supervisor-approved purchase requisition or a direct online order; the discipline of treating that order as a PO — with a unique PO number, a

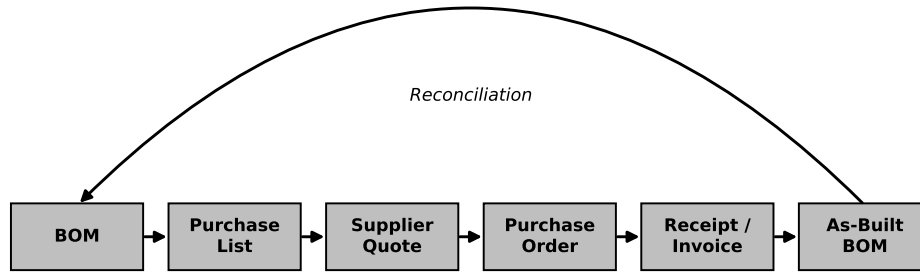


Figure 11.2: Procurement document chain for the sorter prototype. Flow proceeds left to right: the costed BOM feeds the purchase list; the purchase list generates RFQs to suppliers; selected quotes become purchase orders (POs); POs trigger shipments that produce a packing slip and invoice; receipt verification produces the as-built BOM through reconciliation. Each arrow represents a document hand-off with a defined format and responsible party.

line-item list, and a price commitment — is nonetheless valuable and expected in industry.

11.4.1 Required PO Fields

A well-formed PO contains:

- (a) **PO number** — a unique identifier used to cross-reference the invoice and packing slip.
- (b) **Issue date and required-by date.**
- (c) **Line items:** supplier part number, MPN, description, ordered quantity, agreed unit price, and line total.
- (d) **Ship-to address** and delivery instructions.
- (e) **Payment terms** (e.g., Net 30, credit card on shipment).
- (f) **Authorising signature or approval** — in a student lab context, this is the instructor or technician approval on the requisition form.

11.4.1.0.1 In Practice. PO numbers serve a critical traceability function. When two packages arrive on the same day from the same distributor, the packing slip PO reference is the only reliable way to match each package to its originating order without opening and counting every item. Assign PO numbers sequentially from the project start and record them in the procurement log.

11.5 Receipt, Invoice, and Verification

Receiving a shipment is not the end of the procurement process; it is the beginning of the verification step. Every received shipment must be checked against three documents: the PO, the packing slip, and the invoice.

11.5.1 Three-Way Match

The **three-way match** is the standard industry procedure for approving payment on a received order:

- (a) **PO vs. packing slip:** confirm that the items shipped (part numbers, quantities) match what was ordered.
- (b) **Packing slip vs. physical contents:** confirm that what arrived physically matches what the packing slip claims.
- (c) **PO vs. invoice:** confirm that the prices billed match the prices committed in the PO.

Any discrepancy — a short shipment, a substituted part, a price that does not match — must be resolved with the supplier before payment is authorised and before the part enters the build. A substituted part may have a different footprint or electrical characteristic than the one ordered; using it without verification can damage the board.

11.5.2 Physical Inspection

For mechanical and electronic components, physical inspection after receipt includes:

- (a) Checking packaging integrity (moisture-barrier bags for ICs, ESD-safe packaging for sensitive components).
- (b) Reading the manufacturer label on the tape reel or bag to confirm MPN and date code.
- (c) Measuring one sample from each lot with a multimeter or LCR meter where practical (resistor value, capacitor value, continuity).

Counterfeit components are a real risk when ordering from grey-market sources. Sticking to authorised distributors (Digi-Key, Mouser, Arrow) eliminates this risk for prototype quantities.

11.6 Reconciliation and the As-Built BOM

The **as-built BOM** records the design as it was actually built: every substitution, lot code, and quantity deviation from the original design BOM is captured here. It is created by reconciling the design BOM against the procurement records (POs, invoices, packing slips) and the physical build records (assembly log, rework log).

11.6.1 Why Reconciliation Matters

If a part was substituted during procurement — because the preferred part was out of stock — the substitution must be captured in the as-built BOM so that a future builder replicating the prototype knows which part was actually used and tested. An as-built BOM that simply says “same as design BOM” is only credible if the three-way match confirmed no substitutions for every line.

Reconciliation also closes out the budget. Compare the total actually spent (sum of invoice line totals) against the C_{BOM} estimate. Any variance larger than 5% warrants an explanation: price change, MOQ forcing excess purchase, or a substitution at a different price point. This variance record feeds the project’s financial close-out report and informs cost estimates for the next project.

11.6.1.0.1 In Practice. A sorter prototype team ordered the preferred motor driver at \$7.40/unit. The part went out of stock after the PO was placed; the supplier substituted an alternate at \$9.15/unit without notifying the team. The three-way match caught the price discrepancy. The team confirmed the alternate was parametrically compatible (same current rating, same footprint), approved the substitution, updated the as-built BOM, and logged the \$1.75/unit variance. Without the three-way match, the variance would have been discovered only at budget close-out — too late to question or contest.

11.7 Worked Example: Sorter BOM

This section builds the complete costed BOM for one unit of the IoT robotic sorting subsystem, derives the cost equations, and works through a supplier quote comparison for one line item.

11.7.1 The Eight-Line Sorter BOM

The sorter contains the following components at the third level of the BOM hierarchy (see Figure 11.1):

- (a) **U1** — MCU board (ESP32-DevKitC-32E, Espressif)
- (b) **U2** — MQTT radio module (ESP-WROOM-32U, Espressif variant with external antenna connector)
- (c) **Q1** — Motor driver IC (DRV8833PWPR, Texas Instruments)
- (d) **M1** — Conveyor motor (Pololu 37D gear motor, 12 V, 150 rpm, Pololu 4759)
- (e) **K1** — Sort-gate actuator (HS-82MG micro servo, HiTec)
- (f) **B1** — Colour sensor (TCS34725FN, ams-OSRAM)
- (g) **B2** — Proximity sensor (VL53L0X ToF module, STMicroelectronics)

- (h) **H1** — Enclosure hardware kit (M3 standoffs, screws, nuts — assorted 50-piece kit)

With the line items defined, the cost equations follow directly.

The **extended cost** for line i is:

$$\text{ext}_i = q_i \times u_i \quad (11.2)$$

where q_i is the per-assembly quantity and u_i is the unit cost in CAD.

The **BOM total** C_{BOM} sums all extended costs:

$$C_{\text{BOM}} = \sum_{i=1}^N q_i \times u_i \quad (11.3)$$

Table 11.1 presents the eight-line BOM with all fields populated. Costs are in Canadian dollars at single-unit distributor pricing as of the course edition date.

Table 11.1: Costed BOM for the IoT robotic sorting subsystem (one assembly unit). Unit and extended costs in CAD. Lead times from preferred supplier. Ref: reference designator; Qty: per-assembly quantity; UC: unit cost; EC: extended cost.

Ref	Description / MPN	Qty	UC (CAD)	EC (CAD)	Supplier	Lead time
U1	ESP32-DevKitC-32E	1	12.50	12.50	Digi-Key	3 days
U2	ESP-WROOM-32U (ext. ant.)	1	8.75	8.75	Mouser	5 days
Q1	DRV8833PWPR motor driver	1	3.20	3.20	Digi-Key	3 days
M1	Pololu 4759 gear motor	1	54.95	54.95	Pololu	7 days
K1	HS-82MG micro servo	1	22.40	22.40	RobotShop	4 days
B1	TCS34725FN colour sensor	1	6.80	6.80	Mouser	5 days
B2	VL53L0X ToF proximity module	1	11.30	11.30	Digi-Key	3 days
H1	M3 hardware kit (50-pc)	1	4.95	4.95	Amazon CA	2 days
			C_{BOM}	124.85		

Equation 11.2 applied to each line yields the extended costs shown in Table 11.1. Summing by Equation 11.3:

$$C_{\text{BOM}} = 12.50 + 8.75 + 3.20 + 54.95 + 22.40 + 6.80 + 11.30 + 4.95 = \$124.85 \text{ CAD}$$

The subsystem cost breakdown is: Control (U1 + U2 + Q1 + B1 + B2) = \$42.55; Actuation (M1 + K1) = \$77.35; Structure (H1) = \$4.95. The cost rollup by subsystem is shown in Figure 11.3.

11.7.2 Overage Application

Applying $\alpha = 0.10$ (10% overage) using Equation 11.1 to the consumable and passive line:

- (a) H1 (enclosure hardware kit, fasteners) — $q_{H1} = 1$, $q_{H1}^{\text{order}} = \lceil 1.10 \times 1 \rceil = \lceil 1.10 \rceil = 2$

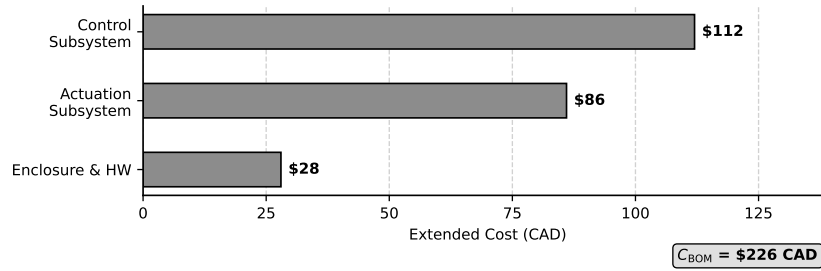


Figure 11.3: BOM cost rollup by subsystem for the IoT robotic sorting subsystem. Horizontal bars show the contribution of each subsystem to the $C_{BOM} = \$124.85$ CAD total. Actuation dominates at \$77.35 (62%), driven primarily by the gear motor (M1 at \$54.95). Control contributes \$42.55 (34%) and Structure \$4.95 (4%).

The hardware kit is the only line where overage applies in this BOM: the electronic modules are ordered to exact quantity (1 each), and one spare unit is noted separately in the risk register rather than inflating the BOM cost. The purchase list therefore shows H1 at quantity 2 ($2 \times \$4.95 = \9.90) while the BOM cost calculation retains $q_{H1} = 1$, $ext_{H1} = \$4.95$.

11.7.3 Supplier Quote Comparison: MQTT Radio Module (U2)

Two distributors were asked to quote the ESP-WROOM-32U at quantity 1.

Table 11.2: Supplier quotes for U2 (ESP-WROOM-32U, Qty 1). All prices in CAD including applicable taxes and standard shipping to the lab address.

Supplier	Unit price (CAD)	Lead time	Notes
Mouser Electronics	\$8.75	5 business days	In stock (427 units); standard shipping included
DigiParts CA	\$7.90	14 business days	Ships from overseas warehouse; no local stock

DigiParts CA offers a unit price \$0.85 lower than Mouser. However, the lead time of 14 business days (approximately three calendar weeks) places delivery after the assembly milestone on the Gantt chart from Chapter 10. Missing that milestone delays Gate 3 by at least two weeks.

Preferred choice: Mouser Electronics. The \$0.85 price advantage of DigiParts CA is outweighed by the lead-time risk. At a project cost of \$124.85 per unit, the \$0.85 saving represents 0.7% of BOM cost — an amount that is not worth delaying the project for.

The general procurement principle this illustrates: *lead time is a schedule input, not a footnote*. Any supplier whose lead time threatens a milestone date must be disqualified regardless of unit price, unless the project manager explicitly approves the schedule extension.

11.7.3.0.1 Common Pitfalls. The four most common BOM and procurement errors on prototype projects are:

- (a) **BOM as an afterthought.** Starting the BOM after assembly begins means ordering parts under time pressure, paying expedite fees, and finding missing parts only when a build step stalls. The BOM should be started during architecture (Chapter 5) and completed before procurement begins.
- (b) **No alternates listed.** A BOM with no alternate part column is a single-sourced BOM. When the preferred part is out of stock — which happens routinely with popular ICs — the project stalls while the team qualifies an alternate under pressure.
- (c) **Missing reference designators.** Ordering a part without confirming the footprint against the reference designator on the PCB has no recovery path except rework or board respins. The reference designator column in the BOM is the link between the procurement document and the assembly drawing.
- (d) **Single-sourced parts with no risk register entry.** A component that can only be purchased from one supplier, with no qualified alternate and no risk register entry flagging the exposure, is an unmanaged risk. Every single-source line in the BOM should have a corresponding risk register entry with a mitigation (order extra stock, qualify an alternate before production).

Try It Yourself

Your team is prototyping a battery-powered environmental sensor node. The design BOM has six line items (one assembly unit):

Table 11.3: Design BOM for the environmental sensor node (Try It Yourself). Unit costs in CAD at single-unit pricing.

Ref	Description / MPN	Qty	UC (CAD)	Supplier
U1	ATSAMD21G18A-MU MCU	1	6.30	Digi-Key
U2	RFM95W LoRa radio module	1	9.45	Mouser
U3	BME680 environmental sensor	1	7.20	Digi-Key
BT1	18650 Li-ion cell (2500 mAh)	2	4.80	BatterySpace
C1	100 μ F electrolytic cap (assorted)	5	0.30	Digi-Key
H1	Enclosure + mounting hardware	1	8.75	Amazon CA

1. Calculate the extended cost for each of the six lines using Equation 11.2.
2. Calculate C_{BOM} using Equation 11.3.
3. Apply an overage of $\alpha = 0.15$ (15%) to the capacitor line (C1) only, using Equation 11.1. What is q_{C1}^{order} ?
4. A second supplier quotes the RFM95W at \$8.10 CAD but with a lead time of 18 business days (your assembly milestone is in 10 business days). Identify the preferred supplier and justify your choice using both unit price and lead time criteria.
5. List two fields this BOM is missing that would be required for a Gate 3 submission.

Review Questions

1. **(Conceptual)** Explain the difference between a BOM and a purchase list. Under what circumstances does a purchase list differ from the BOM in both line count and quantity per line?
2. **(Conceptual)** Why is an as-built BOM required even when the assembled unit matches the design BOM exactly? What does the as-built BOM provide that the design BOM does not?
3. **(Applied)** A BOM has a line item for 0.1 μ F MLCC capacitors with $q = 12$ and $u = \$0.08$ CAD.
 - (a) Calculate the extended cost using Equation 11.2.
 - (b) Calculate the order quantity with $\alpha = 0.10$ using Equation 11.1.
4. **(Applied)** A BOM has five line items with extended costs of \$24.50, \$67.00, \$8.40, \$13.75, and \$5.90 (all CAD). Calculate C_{BOM} using Equation 11.3 and identify which single line contributes the greatest fraction of total cost.
5. **(Multi-step)** Supplier A quotes a microcontroller at \$11.20 CAD with a 4-business-day lead time and 50 units in stock. Supplier B quotes the same MPN at \$9.85 CAD with a 12-business-day lead time and 200 units in stock. Your assembly milestone is 7 business days from today and you need 3 units.
 - (a) Calculate the total cost from each supplier for 3 units.
 - (b) Identify the preferred supplier with explicit reasoning that addresses both price and schedule.
 - (c) Describe one scenario in which the higher-priced supplier would *not* be preferred despite meeting the schedule.

Portfolio Entry

The Gate 3 deliverable from this chapter is a procurement package consisting of three documents submitted together:

- (a) **Costed BOM:** all fields populated (reference designator, MPN, description, quantity, unit cost, extended cost, preferred supplier, distributor part number, lead time, alternate part).
- (b) **Purchase list:** one row per unique MPN with order quantities reflecting overage where applicable, derived from the BOM as described in Section 11.2.
- (c) **Procurement records:** for completed purchases, the set of POs, packing slips, and invoices with the three-way match completed; for pending purchases at Gate 3 submission, the set of accepted quotes and issued POs.

A Gate 3 reviewer who cannot find a unit cost, a lead time, or an alternate part for any line item in the costed BOM will flag the submission as incomplete. The BOM is a design document; an incomplete design document is not ready for review.

Chapter Summary

The bill of materials functions as a design document: its completeness is a pre-condition for Gate 3 approval, not a post-assembly record. It records the full set of physical parts needed for one assembled unit — reference designators, MPNs, quantities, unit costs, extended costs, supplier information, lead times, and alternate parts — and makes the cost and supply-chain risk of the design visible to every reviewer. The **extended cost** for each line is $\text{ext}_i = q_i \times u_i$ (Equation 11.2). The **BOM total** is $C_{\text{BOM}} = \sum q_i \times u_i$ (Equation 11.3). Order quantities for consumables are padded by an overage factor α using $q_i^{\text{order}} = \lceil (1 + \alpha) q_i \rceil$ (Equation 11.1), but overage belongs only on the purchase list — never in the BOM cost calculation.

Supplier selection weighs unit price, lead time, stock availability, MOQ, and shipping; the cheapest quote is not always the correct choice when lead time threatens a Gantt milestone. The procurement document chain — BOM, purchase list, RFQ, PO, packing slip, invoice, three-way match, as-built BOM — provides traceability from design intent to physical assembly and closes out the procurement budget with a recorded variance.

You now have a costed BOM, a purchase list, and a set of procurement records. Chapter 12 takes C_{BOM} as its starting point and asks what happens to unit cost when the design scales from one prototype to low-volume production — identifying the cost-reduction leverage points a Gate 4 reviewer will require.

LOW-VOLUME PRODUCTION ECONOMICS

12.0.0.0.1 Where this fits. Chapter 11 delivered a validated prototype and a costed Bill of Materials for the IoT robotic sorting subsystem; this chapter sits at Gate 3 of the Stage-Gate model and fills the gap between that one-off prototype cost and the production economics that underpin the go/kill decision. A team that passes Gate 3 has demonstrated a working prototype and a credible BOM; the gate committee now asks a harder question: *can this product be made and sold profitably?* The cost projection produced in this chapter is the economic half of that answer. Gate 3 reviewers will scrutinise your unit-cost curve and break-even analysis as carefully as they scrutinise your test results.

12.0.0.0.2 Learning Objectives.

1. Compute and plot the unit-cost curve $C_{\text{unit}}(N)$ from a prototype BOM and an estimated fixed cost.
2. Find the break-even volume N^* between two competing production processes.
3. Connect design decisions made at Stage 3 to downstream manufacturing cost, using the DFM/DFA framework introduced in Chapter 7.

12.1 Why Low-Volume Bridge Production Exists

Between a validated prototype and a full production run lies a zone that engineers call **bridge production** or **low-volume production**. Volumes in this zone are typically 10 to 500 units — too many to hand-build one at a time, too few to justify the tooling cost of high-volume manufacturing.

Bridge production serves three purposes. First, it generates the first real product units for pilot customers, whose feedback feeds directly back into the design before a large capital commitment is made. Second, it exposes assembly and yield problems that never appear in a single-unit prototype, where defects are caught and reworked by the same engineer who built the board. Third, it provides the actual cost data that replaces the estimates in the Gate 3 projection.

12.1.0.0.1 In Practice. Many hardware startups and college capstone projects skip bridge production entirely: they build one prototype, quote a retail price, and claim the product is viable. The prototype BOM is then mistaken for the unit cost. The result is a Gate 3 slide showing a \$226 unit cost for a product priced at \$300 — a margin of 25% that evaporates as soon as a contract manufacturer quotes assembly labour, packaging, and regulatory compliance.

12.2 Fixed vs. Variable Cost

Every cost in a production run belongs to one of two categories.

Variable cost (c_{var}) is the cost that changes in proportion to the number of units produced. Components, raw materials, and direct assembly labour are variable: build one more unit and you spend c_{var} more. For the sorting subsystem, Chapter 11 established $c_{\text{var}} = \$480$ CAD, which reflects component cost plus estimated assembly labour at production volume.

Fixed cost (C_{fixed}) is the cost paid once, regardless of how many units are produced. Tooling (injection-mould tools, PCB test fixtures, jigs), non-recurring engineering (NRE) charges from a contract manufacturer, certification fees, and software licences are fixed: doubling the run does not double these costs. For the sorting subsystem, $C_{\text{fixed}} = \$8,000$ CAD, which covers the PCB test fixture (\$2,400), the injection-mould tool for the housing (\$4,800), and NRE setup charges (\$800).

Common Pitfalls. Three errors appear consistently in student Gate 3 submissions.

- (a) **Treating prototype unit cost as production unit cost.** The prototype BOM (\$226) includes retail component prices and one-off shipping. At volume, component prices drop and shipping is amortised; variable cost and prototype cost are different quantities.
- (b) **Forgetting that c_{var} excludes fixed costs.** The formula for C_{unit} (see Section 12.3) adds fixed costs explicitly; if you fold tooling into your variable cost estimate you will double-count it.
- (c) **Omitting hidden fixed costs.** Certification (CE, FCC, CSA) and first-article inspection are fixed costs that do not scale. A product sold in Canada and shipped to the US carries two regulatory budgets.

12.3 The Unit-Cost Curve

When C_{fixed} is spread over N units and c_{var} is paid per unit, the total cost of a run of N units is

$$C_{\text{total}}(N) = C_{\text{fixed}} + N \cdot c_{\text{var}}.$$

Dividing by N gives the **unit cost**:

$$C_{\text{unit}}(N) = \frac{C_{\text{fixed}}}{N} + c_{\text{var}}. \quad (12.1)$$

Equation 12.1 is a rectangular hyperbola in N . As $N \rightarrow \infty$, C_{unit} asymptotes to c_{var} from above: no matter how large the run, you cannot drive unit cost below the variable cost per unit. At $N = 1$, unit cost equals $C_{\text{fixed}} + c_{\text{var}}$: the entire tooling and setup burden falls on a single unit.

Figure 12.1 illustrates this relationship for the sorting subsystem.

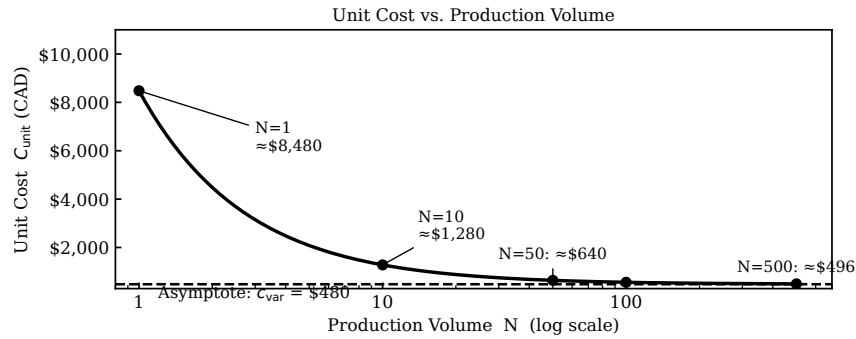


Figure 12.1: $C_{\text{unit}}(N)$ for the IoT sorting subsystem ($C_{\text{fixed}} = \$8,000$ CAD, $c_{\text{var}} = \$480$ CAD). The curve is a rectangular hyperbola that asymptotes to \$480 as volume grows. The dashed horizontal line marks the \$480 asymptote; the dotted vertical line marks $N = 80$, where the fixed-cost contribution falls to \$100 per unit.

12.3.1 Worked Example A: Computing the Unit-Cost Table

Given $C_{\text{fixed}} = \$8,000$ CAD and $c_{\text{var}} = \$480$ CAD, apply Equation 12.1 at five production volumes.

$N = 1$:

$$C_{\text{unit}}(1) = \frac{8,000}{1} + 480 = 8,000 + 480 = \$8,480 \text{ CAD.}$$

$N = 10$:

$$C_{\text{unit}}(10) = \frac{8,000}{10} + 480 = 800 + 480 = \$1,280 \text{ CAD.}$$

$N = 50$:

$$C_{\text{unit}}(50) = \frac{8,000}{50} + 480 = 160 + 480 = \$640 \text{ CAD.}$$

$N = 100$:

$$C_{\text{unit}}(100) = \frac{8,000}{100} + 480 = 80 + 480 = \$560 \text{ CAD.}$$

$N = 500$:

$$C_{\text{unit}}(500) = \frac{8,000}{500} + 480 = 16 + 480 = \$496 \text{ CAD.}$$

These five values are collected in Table 12.1.

Table 12.1: Unit cost at selected production volumes ($C_{\text{fixed}} = \$8,000$ CAD, $c_{\text{var}} = \$480$ CAD).

N	C_{fixed}/N	c_{var}	C_{unit}	Gross margin at $p = \$1,200$
1	\$8,000	\$480	\$8,480	-606 %
10	\$800	\$480	\$1,280	-6.7 %
50	\$160	\$480	\$640	46.7 %
100	\$80	\$480	\$560	53.3 %
500	\$16	\$480	\$496	58.7 %

Notice the rapid improvement between $N = 1$ and $N = 50$: the unit cost falls by \$7,840 in that interval, compared with only \$144 in the interval from $N = 50$ to $N = 500$. The curve is steep at low volume and flat at high volume — this is the economic signature of the hyperbola.

At what N does the fixed-cost contribution fall below \$100?

Set the fixed-cost contribution equal to \$100 and solve for N :

$$\frac{C_{\text{fixed}}}{N} = 100 \implies N = \frac{C_{\text{fixed}}}{100} = \frac{8,000}{100} = 80 \text{ units.}$$

At $N = 80$ the fixed cost adds exactly \$100 per unit; below 80 units each unit carries more than \$100 of tooling burden. This threshold is marked in Figure 12.1.

12.4 Process Break-Even

Different manufacturing processes carry different cost structures. A process with low fixed cost but high variable cost (such as 3D printing) is cheapest at low volume. A process with high fixed cost but low variable cost (such as injection moulding) is cheapest at high volume. The **process break-even volume** N^* is the production quantity at which the total cost of the two processes is equal.

For two processes with fixed costs C_{f1} , C_{f2} and variable costs c_{v1} , c_{v2} (where process 1 has the lower fixed cost and higher variable cost, $c_{v1} > c_{v2}$), set total costs equal:

$$C_{f1} + N^*c_{v1} = C_{f2} + N^*c_{v2}.$$

Solving for N^* :

$$N^* = \frac{C_{f2} - C_{f1}}{c_{v1} - c_{v2}}. \quad (12.2)$$

Figure 12.2 shows that below N^* the gap between the two cost lines widens rapidly, making early process selection consequential.

12.4.1 Worked Example B: 3D-Printing vs. Injection Moulding

The sorting subsystem housing can be produced by either process:

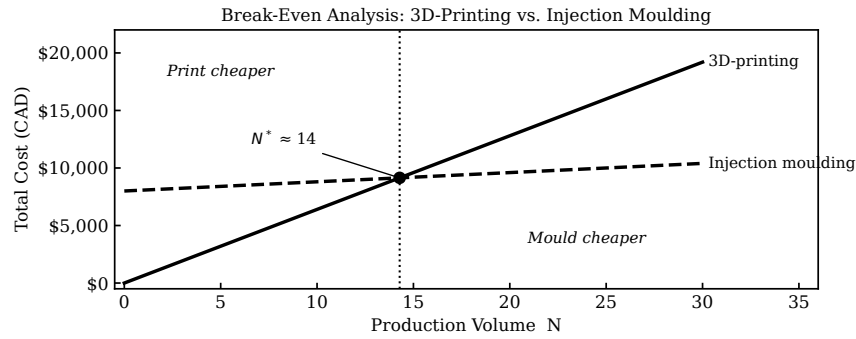


Figure 12.2: Total cost for 3D printing and injection moulding as a function of production volume. The lines cross at $N^* = 15$ units. Below 15 units the printed process is cheaper; above 15 units the moulded process is cheaper. The shaded zone around N^* represents the indifference region where process selection should be driven by lead-time, quality, and risk rather than cost alone.

- **Process 1 — FDM 3D printing:** no tooling required, $C_{f1} = \$0$ CAD; per-unit material plus machine time, $c_{v1} = \$640$ CAD.
- **Process 2 — injection moulding:** single-cavity aluminium tool, $C_{f2} = \$8,000$ CAD; cycle time and material per shot, $c_{v2} = \$80$ CAD.

Apply Equation 12.2:

$$N^* = \frac{C_{f2} - C_{f1}}{c_{v1} - c_{v2}} = \frac{8,000 - 0}{640 - 80} = \frac{8,000}{560} \approx 14.3 \text{ units.}$$

Because a fractional unit is not physically meaningful, round up: $N^* = 15$ units.

Decision rule:

- Below $N = 15$: use FDM printing. Total cost at $N = 10$: printing costs $0 + 10 \times 640 = \$6,400$; moulding costs $8,000 + 10 \times 80 = \$8,800$. Printing saves \$2,400.
- Above $N = 15$: use injection moulding. Total cost at $N = 50$: printing costs $0 + 50 \times 640 = \$32,000$; moulding costs $8,000 + 50 \times 80 = \$12,000$. Moulding saves \$20,000.

12.4.1.0.1 Common Pitfalls. N^* is not a sharp switch. In the neighbourhood of 15 units the cost advantage of either process is small (a few hundred dollars over the run), while process differences in lead time, surface finish, and dimensional tolerance can be decisive. Treat N^* as the centre of a zone of indifference — roughly $\pm 20\%$ around the calculated value — and let non-cost factors govern the decision within that zone.

12.5 DFM, DFA, and the Design-Locks-Cost Principle

Chapter 7 introduced Design for Manufacturability and Design for Assembly as Stage 3 disciplines. This chapter puts an exact dollar value on each.

The design-locks-cost principle states that approximately 70–80 % of the lifetime manufacturing cost of a product is determined by decisions made before the first prototype is built. Once a geometry is fixed, a component is specified, or an assembly sequence is locked in, the variable cost c_{var} is largely set. Subsequent process optimisation can reduce c_{var} by a few percent; only a redesign can change it significantly.

12.5.1 DFM Impact on Variable Cost

Each DFM decision made in Chapter 7 has a direct entry in c_{var} . Consider the FDM housing for the sorting subsystem.

- **Wall thickness at 1.5 mm** (above the 1.2 mm minimum): two complete perimeters plus a partial infill perimeter. Reducing wall thickness to the minimum saves approximately 8 % of material mass and roughly 12 minutes of print time per unit. At a machine rate of \$2.50/hr, this is a saving of \$0.50 per unit — small at 10 units (\$5 total), meaningful at 500 units (\$250 total).
- **Support-free cable channels:** eliminating support material saves post-processing labour. At \$20/hr labour rate and 8 minutes per unit, the saving is \$2.67 per unit, or \$1,335 over 500 units.

DFM decisions compound: a design with three or four such improvements can reduce c_{var} by 10–15 %, shifting the entire unit-cost curve downward.

12.5.2 DFA Impact on Assembly Cost

The **DFA assembly efficiency** η_A introduced in Chapter 7 quantifies the ratio of theoretically necessary assembly operations to actual operations. A low η_A means redundant parts, redundant fasteners, or awkward handling — all of which inflate the assembly-labour component of c_{var} .

For the sorting subsystem, the housing originally used four M3 screws to secure the PCB. Replacing these with two snap-fit latches (a DFA decision from Chapter 7) reduces the fastener count from four to zero, saves approximately 3 minutes of assembly time per unit, and removes four BOM line items. At 500 units this represents 25 hours of assembly labour — roughly \$500 in direct savings, plus the reduction in torque-tool calibration cost.

12.5.2.0.1 In Practice. DFM and DFA improvements are most valuable when they are identified at Stage 3, before the design is frozen. A snap-fit geometry that replaces screws is trivial to implement in CAD before the mould tool is cut. It is expensive to retrofit after the tool exists: a mould modification (“steel-safe” change) costs \$500–\$2,000 and adds 2–4 weeks to the schedule. This is the practical meaning of the design-locks-cost principle.

12.6 Failure Economics

A unit-cost analysis that excludes failure rates is optimistic. **Yield** is the fraction of produced units that pass acceptance testing and ship to customers. A yield of 95% means 5 out of every 100 units are scrapped or reworked, adding their cost to the run without adding to revenue.

The **effective variable cost** under a yield Y is

$$C_{\text{eff}} = \frac{C_{\text{var}}}{Y}. \quad (12.3)$$

At $Y = 0.95$ and $C_{\text{var}} = \$480$:

$$C_{\text{eff}} = \frac{480}{0.95} \approx \$505 \text{ CAD per shipped unit.}$$

The \$25 difference appears small; at $N = 500$ shipped units it represents an additional \$12,500 in unrecovered production cost.

12.6.1 Cost of a Design Defect Found Late

Figure 12.3 illustrates the **cost-committed curve**: the cumulative fraction of lifetime cost that is locked in at each project phase, plotted against the cost actually incurred.

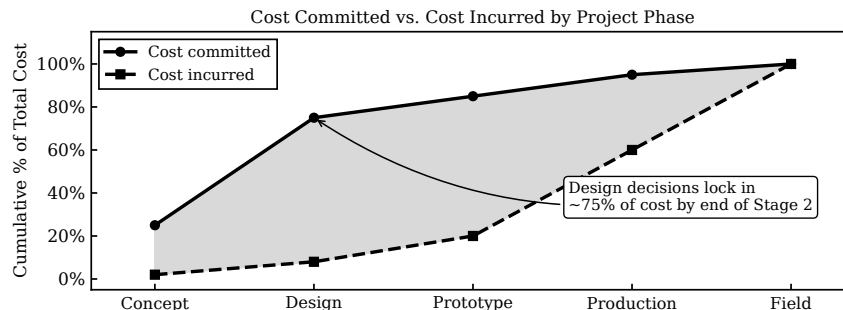


Figure 12.3: Cost committed vs. cost incurred over the five Stage-Gate phases. By the end of Stage 3 (Development), approximately 75% of lifetime manufacturing cost is locked in, yet only 15–20% of total project spend has occurred. The gap between the two curves is the economic justification for intensive front-end design work.

A defect found in Stage 3 (a DFA violation, an over-toleranced component, a housing that requires support material) costs a CAD change and a reprint. The same defect found in Stage 4, after the mould tool is cut, costs a tool modification, a delay, and likely a BOM change. The **rule of ten** states that the cost of fixing a defect multiplies by approximately ten at each stage boundary.

Try It Yourself

A student team is developing a wearable environmental sensor. The BOM and process estimates give the following parameters:

- $C_{\text{fixed}} = \$6,000$ CAD (PCB test fixture \$1,800; custom enclosure tool \$3,600; NRE \$600).
 - $c_{\text{var}} = \$35$ CAD per unit (components \$22, assembly labour \$13).
 - Selling price $p = \$199$ CAD.
- (a) Using Equation 12.1, compute C_{unit} at $N = 1$, $N = 25$, $N = 100$, and $N = 500$. Show every arithmetic step.
- (b) At what production volume does the fixed-cost contribution per unit fall below \$20? (Set up the inequality $C_{\text{fixed}}/N < 20$ and solve for N .)
- (c) The team is comparing hand-assembly (soldering iron, jig) against contract-manufacturer reflow:
- Hand-assembly: $C_{f1} = \$200$ (jig), $c_{v1} = \$58$ CAD.
 - CM reflow: $C_{f2} = \$1,800$ (setup and stencil), $c_{v2} = \$22$ CAD.
- Use Equation 12.2 to find N^* . Round to the nearest whole unit. State the decision rule.
- (d) Yield testing shows 92 % of assembled units pass first-pass inspection ($Y = 0.92$). Compute the effective variable cost c_{eff} using Equation 12.3. How does this change the gross margin at $N = 100$?

Review Questions

1. **(Conceptual)** Explain in one paragraph why a prototype unit cost cannot be used directly as the production unit cost. Identify at least two cost categories that change between the prototype build and a production run of 100 units.
2. **(Conceptual)** The design-locks-cost principle states that 75 % of manufacturing cost is committed by the end of Stage 3. What practical implication does this have for when DFM and DFA reviews should be conducted? Why is it economically preferable to discover an assembly violation at Stage 3 rather than Stage 4?
3. **(Applied — calculation)** A product has $C_{\text{fixed}} = \$12,000$ CAD and $c_{\text{var}} = \$75$ CAD. Compute C_{unit} at $N = 20$, $N = 80$, and $N = 400$. At what volume does the fixed-cost contribution per unit drop below \$50?
4. **(Applied — calculation)** Two enclosure processes are available:
 - Laser-cut acrylic: $C_{f1} = \$0$, $c_{v1} = \$95$ CAD.
 - Vacuum-formed HDPE: $C_{f2} = \$3,500$ CAD, $c_{v2} = \$18$ CAD.Use Equation 12.2 to calculate N^* . Show full algebra. For a planned run of 60 units, which process minimises total cost, and by how much?
5. **(Multi-step)** A hardware team projects $C_{\text{fixed}} = \$5,000$ CAD, $c_{\text{var}} = \$120$ CAD, selling price $p = \$350$ CAD, and yield $Y = 0.88$.
 - (a) Compute the effective variable cost c_{eff} .

- (b) Compute C_{unit} at $N = 50$ using c_{eff} rather than c_{var} .
- (c) Compute the gross margin $((p - C_{\text{unit}})/p)$ at $N = 50$.
- (d) How many units must be produced for the gross margin to reach 40%?
Hint: Set $(p - C_{\text{unit}})/p = 0.40$ and solve for N , using c_{eff} in the expression for C_{unit} .

Portfolio Entry

The deliverable for this chapter is a **Preliminary Cost Analysis** document that will feed directly into the Chapter 17 financial model. The document must contain the following elements:

- (a) **Parameter table.** State C_{fixed} , c_{var} , selling price p , and yield Y with sources for each value.
 - (b) **Unit-cost table.** C_{unit} at $N = 50$, $N = 100$, and $N = 500$, computed from Equation 12.1. For the sorting subsystem:
- | N | C_{unit} | Gross margin |
|-----|-------------------|--------------|
| 50 | \$640 CAD | 46.7 % |
| 100 | \$560 CAD | 53.3 % |
| 500 | \$496 CAD | 58.7 % |
- (c) **Process break-even.** Identify the competing processes, state C_{f1} , C_{f2} , c_{v1} , c_{v2} , compute N^* using Equation 12.2, and state the decision rule.
 - (d) **DFM/DFA flags.** List at least two design decisions from your Stage 3 review (Chapter 7) that affect c_{var} , and quantify the per-unit and per-run impact at $N = 100$.
 - (e) **Gate 3 recommendation.** One sentence: given the unit-cost curve and the selling price, does the economics support proceeding to Stage 4?

Chapter Summary

Low-volume production economics turns on a single equation: fixed costs spread over the run, variable costs paid per unit, yielding a hyperbolic unit-cost curve that falls steeply below 50 units and flattens toward c_{var} above 100. Fixed costs (C_{fixed}) are paid once and spread over the run; variable costs (c_{var}) scale with every unit. Their combination produces the unit-cost curve (Equation 12.1), a hyperbola that falls steeply at low volume and flattens toward c_{var} at high volume. For the sorting subsystem ($C_{\text{fixed}} = \$8,000$ CAD, $c_{\text{var}} = \$480$ CAD), unit cost drops from \$640 at 50 units to \$496 at 500 units — a 22% improvement that is already 97% of the maximum possible gain from volume scaling alone.

Process break-even (Equation 12.2) showed that injection moulding becomes cheaper than FDM printing at $N^* = 15$ units for the housing, but that N^* should be treated as a zone rather than a sharp switch.

The design-locks-cost principle connects this chapter directly to Chapter 7: DFM and DFA decisions made at Stage 3 set c_{var} for the lifetime of the product. The cost-committed curve confirms that front-end design investment is the highest-return activity available to the team.

You now have a Preliminary Cost Analysis with C_{unit} at $N = 50$, $N = 100$, and $N = 500$, a process break-even decision, and a Gate 3 recommendation. Chapter 13 takes that full design package and shows how to establish a version-controlled design history file — the Configuration Management Record — so that every artefact can be recovered, compared, and audited as the design evolves toward the Stage 4 release.

VERSION CONTROL & DESIGN HISTORY

13.0.0.0.1 Where this fits. Chapter 12 delivered the cost analysis for the IoT robotic sorting subsystem — unit cost at $N = 50$, 100, and 500, break-even volume, and the economic case to proceed. This chapter sits at the same Stage 3 (Development) gate, where those cost projections must be backed by an auditable design record. Gate 3 requires a complete design package — schematics, firmware, CAD models, BOM, and test records — that a reviewer (or a future team member) can evaluate, reproduce, and certify. A design package without a traceable history is not a package; it is a collection of files. This chapter provides the tools and discipline to turn that collection into an auditable record.

13.0.0.0.2 Learning Objectives. By the end of this chapter you will be able to:

1. apply git branching, release tagging, and git-lfs configuration to a hardware design repository containing firmware, schematic, and CAD artifacts;
2. write meaningful commit messages and manage branches for a hardware design project, including tagging milestone releases; and
3. identify the purpose and required contents of a Design History File (DHF) and construct a DHF index that maps each required record category to its repository location.

13.1 Why Version Control Matters for Hardware

Software developers absorb version control as a survival skill early in their careers. Hardware engineers have historically been slower to adopt it, partly because the dominant artifacts — schematics, PCB layouts, mechanical drawings — are binary files that do not diff cleanly, and partly because “it worked yesterday” is a powerful disincentive to formalising a process that feels like overhead.

Both objections dissolve under Gate pressure.

A change without a record is indistinguishable from an error. When a reviewer at Gate 3 finds that the BOM lists a 4.7 k Ω resistor and the schematic shows a 10 k Ω resistor, there are exactly two possibilities: someone made an unauthorised change,

or a change was made and not recorded. Without version history, the team cannot tell which. Both outcomes are treated the same way by a certification auditor: as evidence of an uncontrolled process.

13.1.1 Design History as Design Evidence

In regulated industries (medical devices under ISO 13485, aerospace under AS9100, automotive under IATF 16949), the **design history** is not a nice-to-have supplement to the design; it is the design's proof of existence. A product cannot be certified based on what it currently is; it is certified based on how it got there — what decisions were made, when, by whom, in response to what evidence.

Even outside regulated industries, the same logic applies at Gate 3 of a student project:

- A reviewer asks, "Why did you change the motor driver in Sprint 4?" Without a record, the answer is "I think we had noise issues" — not defensible. With a version history, the answer is `commit b3c7a1f: "fix(motor): replace DRV8833 with TB6612 to eliminate PWM-induced MQTT packet loss (see test log 2026-04-28)"` — citable, traceable, and credible.
- A teammate who joined mid-project needs to understand the current state without interrupting the rest of the team. The commit log is the onboarding document.
- Future you — reproducing this design six months after submission — has no memory of which firmware version ran during the Gate 3 demo. A release tag does.

13.1.2 Scope: What Needs Version Control

For the IoT robotic sorting subsystem, every artifact that describes the design or its performance must be under version control:

- **Firmware** — all source files, build scripts, configuration headers, and dependency manifests (`CMakeLists.txt`, `platformio.ini`, `requirements.txt`).
- **Schematics and PCB layouts** — KiCad project files (`.kicad_sch`, `.kicad_pcb`), plus exported PDFs and Gerber archives as release artifacts.
- **CAD models** — Fusion 360 version history internally; exported STEP and STL files committed as release artifacts.
- **Documentation** — specifications (Chapter 4 artifact), BOM (Chapter 11 artifact), cost analysis (Chapter 12 artifact), test logs, and this chapter's DHF index.

13.2 Git for Firmware

Students in this program already use git for software coursework. The discipline transfers directly to firmware; the differences are in commit granularity, branching conventions, and the meaning of a release tag.

13.2.1 Commit Discipline

A commit is an atomic, self-contained unit of change accompanied by a message that explains *why* the change was made. “WIP” is not a commit message. “Fixed stuff” is not a commit message. These messages carry zero information for future readers — worse, they give the illusion that a record exists while providing none.

A well-formed commit message follows three rules:

1. **Imperative mood subject line, ≤72 characters.** Write the subject as if completing the sentence “If applied, this commit will. . .” For example: “add TLS client certificate authentication” not “added TLS” or “adding TLS.”
2. **Type prefix.** A short prefix categorises the change: *feat* (new capability), *fix* (corrects a defect), *refactor* (restructures without changing behaviour), *docs* (documentation only), *test* (adds or updates tests), *chore* (tooling, CI, dependency bumps). This prefix lets a reviewer scan the log and immediately understand what category of change each commit represents.
3. **Reference the evidence.** When a commit fixes a problem discovered during testing, name the test log or issue in the message body. “. . . (see test log 2026-04-28)” turns a commit into a traceable decision record.

13.2.1.0.1 Common Pitfalls.

- **“WIP” as a commit message.** Work-in-progress commits are acceptable on a feature branch during development, but every commit that merges to `develop` or `main` must have a meaningful message. If your current practice is to commit with “WIP” and clean up later, use `git rebase -i` before merging to squash and rename those commits.
- **Committing for backup, not history.** Git is not Dropbox. A commit should represent a coherent state of the design, not merely the last save before leaving the lab. Separate “save” behaviour from “history” behaviour by using `git stash` for in-progress work and committing only when a logical unit is complete.
- **Giant commits.** A single commit that changes the schematic, three firmware modules, the BOM, and the README simultaneously cannot be reverted cleanly. Commit each logical change separately.

13.2.2 Branching Strategy

A branching strategy is a shared agreement about which branches exist, what they contain, and how changes flow between them. For a design project at Stage 3, a lightweight adaptation of the Gitflow model works well. Figure 13.1 illustrates this branch structure with prototype milestones labelled.

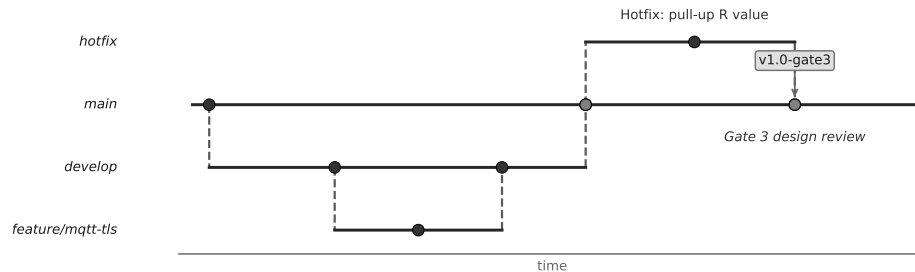


Figure 13.1: Branch and merge diagram for the IoT robotic sorting subsystem design repository. The `main` branch carries only tagged, reviewed releases. Day-to-day integration happens on `develop`. Each new subsystem experiment opens a `feature/` branch that merges back to `develop` after team review. Emergency corrections after a milestone commit flow through a `hotfix/` branch directly to `main` and back to `develop`.

The four branches have distinct roles:

- `main` — the golden branch. Every commit on `main` is a reviewed, tagged release. No one pushes directly to `main`; changes arrive only via a reviewed pull request or hotfix merge.
- `develop` — the integration branch. This is where feature branches land after team review. It represents the current, buildable state of the design. Daily work happens here via merges from feature branches.
- `feature/<name>` — subsystem experiment branches. When a team member is exploring an alternative sensor, a new MQTT library, or a mechanical bracket redesign, they work on a feature branch. This keeps half-finished experiments off `develop` while still providing version control for the experimental work. Examples: `feature/tls-auth`, `feature/tb6612-motor-driver`, `feature/belt-bracket-v2`.
- `hotfix/<name>` — post-release corrections. If a flaw is discovered after a Gate milestone tag, the fix branches from `main`, is applied minimally, and merges back to both `main` (with a new patch tag) and `develop` so the correction propagates forward.

13.2.3 Tagging Releases

A release tag marks a specific commit as a named, reproducible state of the design. Tags are not branches; they do not move as new commits are added. For this course, the tagging convention is:

- `v0.1-proto` — first functional prototype, breadboard or perfboard stage.
- `v0.2-proto` — iterated prototype, subsystems integrated.

- v1.0-gate3 — the design submitted for Gate 3 review; this tag freezes the exact state of every file the reviewer evaluates.
- v1.1-post — post-Gate 3 hotfix, if a defect is discovered after submission.

Tagging the Gate 3 submission is not bureaucratic formality. It means that six months from now, `git checkout v1.0-gate3` recovers the exact design state the reviewer approved. Without the tag, “the version we submitted” is ambiguous.

13.3 Worked Example: Five Commits from the Sorting Subsystem

The following git log covers three weeks of the IoT robotic sorting subsystem project, from an early prototype build through the Gate 3 submission. Read from bottom (oldest) to top (newest).

```
commit a1b2c3d (tag: v1.0-gate3, HEAD -> main)
Author: Team Sorter <team@example.com>
Date: 2026-05-15
```

```
feat(mqtt): add TLS client certificate authentication
```

```
Broker rejects unauthenticated connections per security review
2026-05-12. Provisioned client cert from Let's Encrypt staging
CA. See docs/security-review-2026-05-12.md.
```

```
commit f4e5d6c (origin/develop, develop)
Merge: 9d8e7f6 b1a2c3d
Author: Team Sorter <team@example.com>
Date: 2026-05-13
```

```
Merge branch 'feature/tls-auth' into develop
```

```
Reviewed by: J. Santos. All MQTT latency tests pass at <= 112 ms
p99 after TLS handshake amortisation (see test log 2026-05-13).
```

```
commit b1a2c3d (feature/tls-auth)
Author: A. Kowalski <a.kowalski@example.com>
Date: 2026-05-10
```

```
feat(mqtt): implement TLS 1.3 handshake on ESP32-S3
```

```
Replaces plaintext MQTT with TLS 1.3 using mbedTLS bundled in
ESP-IDF v5.2. Latency overhead measured at +18 ms p99 on first
connect; amortised to +2 ms on subsequent publishes.
```

```
commit 9d8e7f6
Author: M. Tremblay <m.tremblay@example.com>
Date: 2026-04-28
```

```
fix(motor): replace DRV8833 with TB6612 to eliminate
PWM-induced MQTT packet loss
```

```
DRV8833 switching noise at 20 kHz PWM caused Wi-Fi RF
desensitisation (+6 dB noise floor on 2.4 GHz). TB6612 tested
2026-04-27; packet loss dropped from 14% to <1%. BOM updated.
See test log 2026-04-28.
```

```
commit 3c4d5e6 (tag: v0.1-proto)
Author: Team Sorter <team@example.com>
Date: 2026-04-20
```

```
feat(sort): complete first-pass sensor + actuator integration
```

```
Time-of-flight sensor (VL53L1X) and servo divert arm integrated
on breadboard. Sort accuracy 91% over 50-item run. Known issue:
PWM noise degrades Wi-Fi (tracked as issue #7).
```

Before commit discipline was applied, these four changes were recorded as: WIP, update mqtt, fixed motor, done. None names the subsystem, none states the outcome, none cites evidence. These messages are not archived history; they are noise.

What this log demonstrates:

- Each commit message names a subsystem in parentheses, states an action in the imperative, and (in commits 2 and 4) cites a test log.
- The feature branch `feature/tls-auth` appears as three distinct commits — the branch creation (implicit), the implementation commit, and the merge commit — making the experiment’s lifecycle visible in the log.
- Two release tags appear: `v0.1-proto` at first integration, and `v1.0-gate3` at the Gate 3 milestone.
- Commit `9d8e7f6` cross-references issue #7 opened in the `v0.1-proto` commit message, showing that a known defect was logged, tracked, and resolved — the essence of a controlled design process.

13.3.0.1 Reconstructing Design State at Any Commit

The most powerful property of a commit log is reproducibility. To recover the exact state of the sorter firmware, schematic, and documentation as it stood at the `v0.1-proto` tag:

```
git checkout v0.1-proto
```

Git places the working tree in a “detached HEAD” state at that commit. Every file is exactly as it was when that commit was recorded — including the BOM, the firmware, and any exported PDFs committed alongside the source. To inspect the state at an arbitrary commit hash:

```
git checkout 9d8e7f6
```

To return to the current `main`:

```
git checkout main
```

This capability is what converts a repository from a backup system into a design history: the ability to answer “exactly what was the design on 2026-04-28?” with a single command.

13.4 Version Control for Design Files

Firmware is plain text; git handles it natively. Schematic, PCB, and CAD files range from structured text (KiCad’s native format) to proprietary binary (older ECAD tools, Fusion 360 native files). Each category requires a slightly different approach.

13.4.1 EDA Files: KiCad and Git

KiCad 7 and later store schematics (`.kicad_sch`) and PCB layouts (`.kicad_pcb`) as structured text files (S-expression format). These files diff legibly — a net renamed, a footprint repositioned, or a trace re-routed produces a human-readable diff. KiCad projects belong in the git repository alongside firmware.

A recommended KiCad project layout within the repository:

```
hardware/  
  sorter-pcb/  
    sorter-pcb.kicad_pro  
    sorter-pcb.kicad_sch  
    sorter-pcb.kicad_pcb  
    fp-lib-table  
    sym-lib-table  
    exports/  
      sorter-pcb-schematic-v1.0.pdf  
      gerbers-v1.0/
```

The `exports/` subdirectory holds generated artifacts committed at each release milestone. Reviewers receive the PDF; the source files allow regeneration.

A `.gitignore` for a KiCad project should exclude autogenerated files that change on every open:

```
# KiCad autogenerated  
*.kicad_prl  
*-backups/  
fp-info-cache
```

13.4.2 CAD Files: Fusion 360 and STEP Exports

Fusion 360 maintains its own cloud version history per design — every save creates a numbered version accessible from the timeline panel. This internal history is not a git repository, but it provides equivalent capability for pure mechanical work: named versions, rollback, and branch-like “branch design” features.

For the purposes of the DHF and Gate 3 package, the key practice is exporting milestone versions as **STEP files** (.step) and committing them to the repository:

```
hardware/  
  sorter-chassis/  
    exports/  
      sorter-chassis-v0.1-proto.step  
      sorter-chassis-v1.0-gate3.step
```

STEP is a neutral, open exchange format readable by any CAD tool. Committing STEP exports ensures that the Gate 3 package contains manufacturable geometry even if the original Fusion 360 licence expires or the cloud account is unavailable.

13.4.3 Binary Files and Git LFS

Git stores file history by retaining every version of every file. For large binary files — Gerber archives, STEP models, compiled firmware binaries, rendered images — this causes repository bloat: cloning the repository downloads every historical version of every binary, which can quickly reach hundreds of megabytes.

Git Large File Storage (git-lfs) solves this by replacing large binaries in the repository with small pointer files, while storing the actual binary content on a compatible server (GitHub LFS, GitLab LFS, or a self-hosted server). Only the versions actually checked out are downloaded.

Setup requires two steps, run once per repository:

```
git lfs install  
git lfs track "*.step" "*.pdf" "*.zip" "*.bin"  
git add .gitattributes  
git commit -m "chore: configure git-lfs for binary design artifacts"
```

The `git lfs track` command adds patterns to `.gitattributes`. All team members must have git-lfs installed; cloning without it produces pointer-file stubs instead of actual content.

13.4.3.0.1 Common Pitfalls.

- **Committing binary blobs without LFS.** Adding a 15 MB Gerber ZIP to git without LFS embeds that 15 MB permanently in the repository history. `git rm` does

not help; the blob persists in every future clone. Removing it requires rewriting history with `git filter-branch` or the BFG Repo Cleaner, which disrupts all collaborators. Configure LFS *before* committing any binary artifact.

- **Tracking every file type with LFS.** KiCad `.kicad_sch` and `.kicad_pcb` files are structured text and should *not* go through LFS — their diffs are the most valuable part of the schematic history. Only true binaries and large generated outputs belong in LFS.

13.5 The Design History File

The **Design History File (DHF)** is the auditable record of all design decisions, changes, approvals, and test results associated with a product. In regulated product development, the DHF is a formal document set required for certification; a product without a DHF cannot be cleared, approved, or certified.

In this course, the **portfolio is the DHF**. Every artifact produced across Chapters 1 through 14 — the central question, the specification, the risk register, the architecture diagram, the BOM, the cost analysis, and the test records — collectively constitutes the design history. The DHF index page produced in this chapter is the document that proves those artifacts exist, locates them in the repository, and shows that they are current.

13.5.1 Required Contents of a DHF

A complete DHF contains four categories of records. Figure 13.2, shown after the list, illustrates how these records feed the Gate 3 package.

1. **Design records** — the specification (Chapter 4), architecture diagram (Chapter 5), schematic and PCB files, CAD models, firmware source, and BOM (Chapter 11). These describe *what the design is*.
2. **Test records** — bench test logs, latency characterisation results, accuracy trial data, environmental tests. These describe *what was observed*.
3. **Change records** — Engineering Change Orders (Section 13.6) or, in this course, annotated git commit messages and merge records. These describe *what changed and why*.
4. **Approval records** — peer review sign-offs, instructor feedback records, and Gate decision documents. These describe *who reviewed and accepted each change*.

13.5.2 The DHF Index

The DHF index is a single document — typically a Markdown or $\text{\LaTeX}$ file at the root of the repository — that maps each required record to its location. Its purpose is

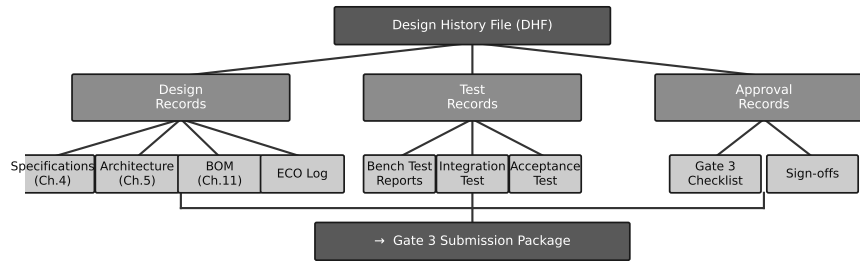


Figure 13.2: The Design History File as a tree of records feeding into the Gate 3 document. Design records capture what was decided; test records capture what was observed; change records capture what was modified and why; approval records capture who reviewed and accepted each change. Together they form the traceable chain of evidence required for Gate 3.

navigation: a reviewer should be able to open the index and locate any specific record within two clicks or two commands.

A minimal DHF index for the sorting subsystem project:

```
# Design History File Index - IoT Robotic Sorting Subsystem
# Gate 3 Submission: tag v1.0-gate3 (2026-05-15)
```

Design Records

- Specification (REQ-01 to REQ-05):
docs/specification.md (commit 3c4d5e6)
- Architecture diagram:
docs/architecture.pdf (commit 7a8b9c0)
- Schematic (KiCad):
hardware/sorter-pcb/sorter-pcb.kicad_sch
- BOM v1.0:
hardware/bom-v1.0.csv (commit e2f3a4b)
- Firmware source:
firmware/src/ (tag v1.0-gate3)

Test Records

- MQTT latency characterisation (2026-05-13):
docs/test-logs/mqtt-latency-2026-05-13.md
- Sort accuracy trial, 100-item run (2026-05-08):
docs/test-logs/sort-accuracy-2026-05-08.md

Change Records

- Motor driver substitution (DRV8833 -> TB6612):
git log 9d8e7f6
- TLS authentication addition:
git log b1a2c3d

Approval Records

- Gate 3 review:
docs/gate3-review-2026-05-16.md

Every entry names the file and the commit or tag at which that file was current.

A future reviewer can `git checkout` the named commit and retrieve the exact version of each record that was present at Gate 3.

13.5.2.0.1 In Practice. Teams who maintain the DHF index throughout the project — updating it whenever a new artifact is produced — find Gate 3 preparation trivial: the index already exists, the records are already filed, and the submission is a matter of tagging the repository and attaching the index. Teams who leave the DHF index for the last week before Gate 3 discover that they cannot locate test logs, cannot match BOM versions to schematic revisions, and cannot reconstruct the decision trail that led to the current design. The DHF is not preparation for Gate 3; it is the continuous record that makes Gate 3 possible.

13.6 Change Management

Every design changes during development. The question is not whether changes will happen but whether they will be recorded. Change management is the discipline of deciding, for each change, whether it requires a formal record and, if so, ensuring that record is created.

13.6.1 Informal Fix vs. Formal ECO

Not every change requires an Engineering Change Order. A typo correction in a comment, a cosmetic alignment fix in a schematic, or a variable rename in firmware can be committed directly with an appropriate message. The decision threshold is whether the change affects form, fit, or function:

- **Form** — physical dimensions, connector locations, mounting hole patterns.
- **Fit** — how the component or assembly interfaces with adjacent parts.
- **Function** — what the system does, including electrical characteristics, software behaviour, or communication protocol parameters.

Any change that affects form, fit, or function in a way that could alter test results or require retesting triggers a formal change record. Figure 13.3 maps this decision.




Figure 13.3: Engineering change order decision flow. Changes that do not affect form, fit, or function proceed as a standard commit. Changes that affect form, fit, or function require a documented rationale and, if the design is post-release (past a Gate milestone tag), a formal ECO with reviewer sign-off before implementation.

13.6.2 The ECO in Practice

A formal Engineering Change Order contains:

1. **Change ID and date** — a unique identifier (e.g., ECO-003) and the date the change was initiated.
2. **Description of the change** — what is being changed, from what to what, in each affected artifact (schematic, firmware, BOM, documentation).
3. **Reason for the change** — the evidence or observation that motivated it (test log reference, defect report, customer feedback, new component availability).
4. **Impact assessment** — which other subsystems, tests, or documents are affected; whether retesting is required.
5. **Approval** — who authorised the change; date authorised.
6. **Implementation reference** — the git commit hash or tag at which the change was applied.

In this course, the ECO is implemented as a short Markdown file committed to `docs/eco/ECO-003.md` with the above fields. The git commit that implements the change references the ECO number in its message: `fix(motor): replace DRV8833 per ECO-003`.

13.6.2.0.1 In Practice. A team made a last-minute resistor value change without recording it. The prototype passed testing, went to Gate 3, and the reviewer asked why the BOM listed 4.7 k Ω and the schematic showed 10 k Ω . No one could answer. The change had been made on the bench during a late-night session, the schematic was not updated, and no commit was made. From the reviewer's perspective, the design was incoherent: the BOM and schematic described two different circuits. An ECO process — or even a committed git message reading *"fix(adc-bias): change R12 from 10k to 4.7k to correct voltage divider for 3.3V ADC reference (see test-log-2026-05-09)"* — would have caught this. A 60-second commit prevents a Gate-day crisis.

13.7 Practical Tooling

This section summarises the tool stack for the sorting subsystem project and provides configuration guidance.

13.7.1 Git and GitHub/GitLab

The repository should be hosted on a platform that supports:

- **Pull requests / merge requests** — the mechanism for team code review before merging feature branches to `develop`.

- **Issues** — the lightweight defect and task tracker; commit messages reference issue numbers (`closes #7`).
- **Git LFS** — large binary storage; both GitHub and GitLab offer LFS storage with free-tier quotas sufficient for a student project.
- **Releases** — GitHub and GitLab both surface git tags as named releases with attached assets; tagging `v1.0-gate3` automatically populates the Releases page, providing a clean download link for the Gate 3 submission package.

A recommended repository root structure for the sorter project:

```
sorter-project/
  firmware/
    src/
    include/
    platformio.ini
  hardware/
    sorter-pcb/          (KiCad project)
    sorter-chassis/
      exports/          (STEP, STL)
  docs/
    specification.md
    architecture.pdf
    bom-v1.0.csv
    test-logs/
    eco/
    dhf-index.md
    .gitattributes      (git-lfs patterns)
    .gitignore
    README.md
```

13.7.2 KiCad Git Integration

KiCad 7's native file format is git-friendly by design. The recommended workflow:

1. Open the KiCad project folder as the git working directory (not as a subdirectory of a larger project with unrelated files).
2. Add the `.gitignore` exclusions for `*.kicad_prl` and `*-backups/` (KiCad auto-generates these on every open).
3. Commit schematic and PCB changes separately from firmware changes. A single commit that mixes a schematic net change with a firmware fix is harder to review and harder to revert.
4. Export schematic PDF and BOM CSV at each release milestone and commit them to `hardware/sorter-pcb/exports/` before tagging.

13.7.3 Fusion 360 Version History

Fusion 360 saves version history to Autodesk cloud storage automatically on each save. Each version can be named (v0.1-proto-belt-bracket, v1.0-gate3-chassis) from the Version History panel. This naming should mirror the git tag convention so that a reviewer can correlate the mechanical version with the corresponding firmware and schematic commit.

The synchronisation point is the STEP export committed to the git repository at each release tag. The process:

1. In Fusion 360, name the current version to match the planned git tag (e.g., v1.0-gate3).
2. Export as STEP: File > Export > STEP (.step).
3. Place the STEP file in hardware/sorter-chassis/exports/ and commit it to git with the message chore(cad): export v1.0-gate3 STEP for DHF.
4. Tag the repository: git tag -a v1.0-gate3 -m "Gate 3 submission".

13.7.4 Keeping the DHF in the Repository

The DHF index (docs/dhf-index.md) lives in the same repository as the design. This means:

- The DHF is versioned alongside the design it documents.
- `git checkout v1.0-gate3` retrieves the DHF index as it stood at Gate 3 submission, listing the exact file versions that were current at that moment.
- There is no separate document management system to synchronise; the repository *is* the document management system.

Try It Yourself

Scenario: A team is developing a **smart aquarium controller** that monitors water temperature, pH, and turbidity, controls a heating element and a peristaltic dosing pump, and publishes sensor readings to a local MQTT broker over Wi-Fi. Their git log for the most recent four commits reads:

```
commit d4e5f6a (HEAD -> main)
Author: Aqua Team <aqua@example.com>
Date: 2026-05-10

    stuff

commit 9b8c7d6
Author: Aqua Team <aqua@example.com>
```

Date: 2026-05-09

WIP sensor code

commit 1a2b3c4

Author: Aqua Team <aqua@example.com>

Date: 2026-05-07

update

commit 5e6f7a8

Author: Aqua Team <aqua@example.com>

Date: 2026-05-03

feat(temp): add DS18B20 one-wire temperature sampling at 1 Hz

Sampling loop validated against NIST-traceable reference thermometer; error < 0.2 degC across 15-35 degC range.

See test-log-2026-05-03.md.

Your tasks:

1. Identify which commits have poorly written messages and explain specifically what information is missing from each.
2. Rewrite the three poorly written commit messages following the type-prefix, imperative mood, and evidence-citation conventions introduced in Section 13.2.1. Use plausible content consistent with the aquarium controller context. Do not invent test results; instead reference a test log by filename.
3. The team has a STEP export of their sensor bracket committed without git-lfs (`sensor-bracket.step`, 22 MB). Address the following:
 - (a) How to prevent future large files from bypassing LFS.
 - (b) Why the existing 22 MB blob cannot be removed with `git rm` alone and what tool is required.
4. Sketch (in plain text or a simple diagram) a DHF index for the aquarium controller at a Gate 3 milestone, listing at least one entry in each of the four DHF categories from Section 13.5.1.

Review Questions

1. **(Conceptual)** Explain the statement “a change without a record is indistinguishable from an error.” A team’s prototype passes all Gate 3 bench tests, but the reviewer flags a discrepancy between the BOM and the schematic. What two possibilities does the reviewer face, and why can the team not resolve the ambiguity without version history?
2. **(Conceptual)** Compare the roles of the `develop` branch and the `main` branch in the Gitflow branching strategy described in this chapter. Why should direct pushes to `main` be prohibited, and what mechanism should be used instead?

3. **(Applied)** The following four commit messages appear in a project repository. For each, state whether it is acceptable or poor, and if poor, rewrite it following the conventions in Section 13.2.1.
 - (a) WIP
 - (b) feat(lidar): add VL53L1X ranging loop with 50 ms sampling interval, validated against tape-measure reference over 0.1-2.0 m (see test-log-2026-04-15.md)
 - (c) fixed the thing
 - (d) updated files
4. **(Applied)** A teammate commits a 40 MB Gerber ZIP file to the repository without git-lfs.
 - (a) Explain why `git rm gerbers.zip && git commit` does not reduce the repository size for new clones.
 - (b) Describe the correct remediation steps, including which external tool is commonly used to rewrite repository history and what the operational consequence is for all other team members after the history rewrite.
 - (c) State the `git lfs track` command that would have prevented this problem for all future ZIP files.
5. **(Multi-step — conceptual + applied)** A team completes Gate 3. One week later, a reviewer discovers that the pulse-width modulation frequency used in the actuator firmware was changed from 20 kHz to 10 kHz during the final sprint but does not appear in any commit message, the BOM, the schematic, or the DHF index.
 - (a) Identify which of the four DHF record categories (Section 13.5.1) is missing for this change.
 - (b) Describe how an ECO record, had it been created, would have captured this change, naming the six fields from Section 13.6.2.
 - (c) Explain whether the existing `v1.0-gate3` tag can be used to reconstruct the state of the firmware at Gate 3 submission, and what additional step would now be required to document the discrepancy without destroying the Gate 3 record.

Portfolio Entry

This chapter produces two linked deliverables that together constitute the version-control component of your Gate 3 package:

1. **Git repository with a meaningful commit log.** Your project repository on GitHub or GitLab must contain:
 - (a) A `main/develop/feature` branch structure consistent with the strategy in Section 13.2.2.
 - (b) At least five commits with meaningful messages following the type-prefix and imperative-mood conventions, covering the design period from your first prototype integration to Gate 3.

- (c) At least one feature branch that was created for a subsystem experiment and merged back to `develop` via a pull request.
 - (d) A release tag `v1.0-gate3` applied to the commit that represents your Gate 3 submission state.
2. **DHF index page.** A file `docs/dhf-index.md` committed to the repository at the `v1.0-gate3` tag, containing:
- (a) At least one entry in each of the four DHF record categories (design records, test records, change records, approval records).
 - (b) For each entry: the filename (relative to the repository root), the git commit hash or tag at which that file was current, and a one-line description of the record's content.
 - (c) The full command required to reproduce the Gate 3 submission state: `git checkout v1.0-gate3`.

Chapter Summary

A design without version control is not under control; it is under the assumption that nothing will go wrong. This chapter established three interlocking disciplines.

First, every design artifact — firmware, schematic, PCB layout, CAD model, BOM, and documentation — belongs in a version-controlled repository. Design history is design evidence: reviewers certify not what a product currently is, but how it got there.

Second, commit discipline and branching strategy are not software-only concerns. Meaningful commit messages in imperative mood with type prefixes and evidence citations turn a git log into a design decision trail. The `main/develop/feature` branch structure keeps experimental work isolated until it is reviewed and ready to integrate. Release tags — `v0.1-proto`, `v1.0-gate3` — freeze exact design states that can be recovered with a single `git checkout` command.

Third, the Design History File is not a document produced at the end of a project; it is a continuous record maintained throughout the project. The DHF index maps design records, test records, change records, and approval records to their repository locations. The ECO process — deciding whether a change affects form, fit, or function, and recording it if it does — is the mechanism that keeps the DHF current. A 60-second commit referencing a test log prevents the Gate-day crisis of a BOM that disagrees with a schematic.

The chapter produces a git repository with a meaningful commit log covering the design period, and a DHF index page linking design records, test records, change records, and approval records to their commits. Chapter 14 takes that documented design and validates it against the acceptance criteria established in Chapter 4 — turning the record of what was built into proof that it works.

VALIDATION & TEST PROCEDURE DESIGN

14.0.0.0.1 Where this fits. Chapter 13 established the discipline of recording every design decision in a version-controlled repository, producing an auditable Design History File as the Gate 3 deliverable. That record is necessary but not sufficient: a reviewer who can trace every commit still needs evidence that the design *works* — that it meets the numeric targets locked in the specification back in Chapter 4. This chapter provides the tools to generate that evidence systematically. Specifically, it addresses how to *plan* a test before running it, how to quantify variation in repeated measurements, and how to reason about failure probability using fault trees. Together these three skills transform a demonstration (“it ran during the demo”) into a validated result (“the latency was 99.06 ± 0.77 ms, well within the 100 ± 4 ms specification, with $C_p = 1.73$ ”).

14.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Write a test procedure *before* running a test, with acceptance criteria traced to the specification.
2. Compute $\bar{x}$, s , margin z , and process capability C_p from repeated measurements.
3. Construct a fault tree and propagate failure probabilities through OR and AND gates.
4. Use fault-tree results to prioritise test effort and write better test procedures.

Validation sits at the hinge between prototype and product. An IoT robotic sorting subsystem can move packages, light LEDs, and publish MQTT messages during a live demonstration — and still fail in the field if no one asked *how quickly* it sorts, *how reliably* it classifies, or *under what conditions* it jams. This chapter answers those questions with arithmetic, not intuition.

14.1 Test Procedures Written in Advance

A test procedure written *after* the prototype is built has a structural bias toward confirming success. The engineer who built the system also writes the test; they

know which conditions are comfortable and which are stressful. Consciously or not, they tend to choose the comfortable ones. This is not dishonesty — it is a well-documented cognitive bias called **confirmation bias**, and the engineering profession's defence against it is procedural: write the test before you know the result.

A **test procedure** is a document that specifies, in advance and in sufficient detail that a different engineer could execute it, exactly the following:

1. **Purpose.** What property is being tested, and which specification requirement does it trace to?
2. **Equipment and configuration.** Every instrument, software version, cable, and fixture needed to reproduce the test environment.
3. **Step-by-step instructions.** Numbered steps with no ambiguity. “Run the system” is not a step. “Press the reset button, wait 5 s for the status LED to turn solid green, then send the START MQTT message on topic `sorter/cmd`” is a step.
4. **Expected outputs.** What the instrumentation *should* read if the design is compliant.
5. **Acceptance criteria.** The numeric boundary between pass and fail, quoted directly from the specification.
6. **Record-keeping.** Where to log the raw data and who signs off on the result.

Figure 14.1 shows the execution cycle that a written procedure enforces: Setup → Measure → Record → Pass/Fail decision → either close the test or iterate and re-measure. The loop is explicit — the procedure defines the scope of each iteration, preventing unbounded “just one more tweak” cycles that consume schedule without producing evidence.




Figure 14.1: Test-execution cycle. A written procedure locks the scope of each iteration so that every loop produces a documented data point, not just a revised result.

Repeatability is not a luxury; it is what makes a result meaningful. A measurement taken once, under unrecorded conditions, by a single person, cannot be challenged, verified, or reproduced. A measurement taken ten times, with instrument model numbers and firmware versions recorded, can be. The second measurement is engineering evidence. The first is an anecdote.

14.2 Traceability: Acceptance Criteria to Specification

Every acceptance criterion in a test procedure must trace to a line in the specification. “The system passes if it looks fast enough” is not traceable. “The system passes if measured end-to-end latency $\bar{x} < 104$ ms and $C_p \geq 1.33$ ” is traceable to Specification Requirement SR-07: *Command-to-actuator latency shall not exceed 100 ± 4 ms under nominal load.*

The numeric boundaries derived from a specification are called the **lower specification limit (LSL)** and the **upper specification limit (USL)**. For a two-sided tolerance like 100 ± 4 ms:

$$\text{LSL} = 100 - 4 = 96.0 \text{ ms}, \quad \text{USL} = 100 + 4 = 104.0 \text{ ms}.$$

These numbers appear verbatim in the test procedure, not as prose but as pass/fail thresholds that a reviewer can check against the specification without judgment.

Traceability matrices formalise this linkage. Each row maps one specification requirement to the test procedure that verifies it, and each test procedure maps back to exactly one requirement. For a capstone-scale project, even a simple two-column table achieves this: one column lists requirement IDs, the other lists test procedure IDs. If a requirement has no corresponding test, the matrix exposes the gap immediately — before the Gate 3 review, not during it.

A test result is only as useful as the requirement it verifies. Vague requirements produce vague tests; vague tests produce ambiguous results. This is why Chapter 4 insisted on quantitative, measurable acceptance criteria in the specification: those numbers are the raw material for every test procedure in this chapter.

14.3 Measurement, Variation, and Margin

No physical measurement is exact. A latency measured ten times over ten minutes will return ten slightly different numbers, because the network stack, the scheduler, and the sensor ADC all introduce small, random fluctuations. This is not a problem to be eliminated — it is a property to be characterised. The engineering task is to characterise the variation numerically, then determine whether the centre of the distribution is far enough from the specification limits that even the tail of the distribution is unlikely to violate them.

14.3.1 Mean and Standard Deviation

The **sample mean** $\bar{x}$ estimates the centre of the distribution:

$$\bar{x} = \frac{1}{n} \sum_{i=1}^n x_i \quad (14.1)$$

The **sample standard deviation** s estimates the spread:

$$s = \sqrt{\frac{1}{n-1} \sum_{i=1}^n (x_i - \bar{x})^2} \quad (14.2)$$

The factor $(n - 1)$ in the denominator, rather than n , corrects for the fact that $\bar{x}$ is estimated from the same sample — this is called **Bessel's correction** and ensures s is an unbiased estimator of the population standard deviation.

For engineering purposes, $n \geq 5$ produces a usable estimate; $n \geq 10$ is recommended when the measurement has significant variation. Fewer than five measurements should be reported as individual values, not summarised with $\bar{x}$ and s , because the estimates are too uncertain to be meaningful.

14.3.2 Margin to Limit

Once $\bar{x}$ and s are known, the distance from the process centre to the nearest specification limit is expressed in units of s . This dimensionless ratio is the **margin** z :

$$z = \frac{USL - \bar{x}}{s} \quad (14.3)$$

(or $(\bar{x} - LSL)/s$ for the lower limit — take the smaller of the two). A margin of $z \geq 3$ means the nearest limit is at least three standard deviations from the mean, so the probability of a single measurement exceeding it is below 0.27% under a normal distribution. $z \geq 4$ is a more conservative design target for safety-relevant quantities.

14.3.3 Process Capability

Margin z answers “how far am I from one limit?” **Process capability** C_p answers “how well does my spread fit inside the full tolerance band?”

$$C_p = \frac{USL - LSL}{6s} \quad (14.4)$$

The denominator $6s$ spans six standard deviations — the $\pm 3\sigma$ range that contains 99.73% of a normal distribution. If $C_p = 1.0$, the $\pm 3\sigma$ spread exactly fills the tolerance band: the process is *marginally capable*. $C_p \geq 1.33$ is the conventional minimum for a production process; $C_p \geq 1.67$ indicates a robust, well-centred design.

Note that C_p does not account for where $\bar{x}$ sits inside the band — a perfectly capable process centred near one limit can still produce frequent failures. For that reason, C_p should always be reported together with $\bar{x}$ relative to the limits, as in the worked example below.

14.3.4 Worked Example — Latency Test

The IoT robotic sorting subsystem specification (SR-07) requires end-to-end command-to-actuator latency of 100 ± 4 ms. Ten latency measurements (in ms) were recorded under nominal load:

98.2, 99.1, 97.8, 100.3, 98.9, 99.7, 98.5, 100.1, 99.4, 98.6

The **specification limits** are:

$$LSL = 96.0 \text{ ms}, \quad USL = 104.0 \text{ ms}$$

Figure 14.2 shows these values plotted against the tolerance band. Figure 14.3 shows the fitted normal curve with limit lines.

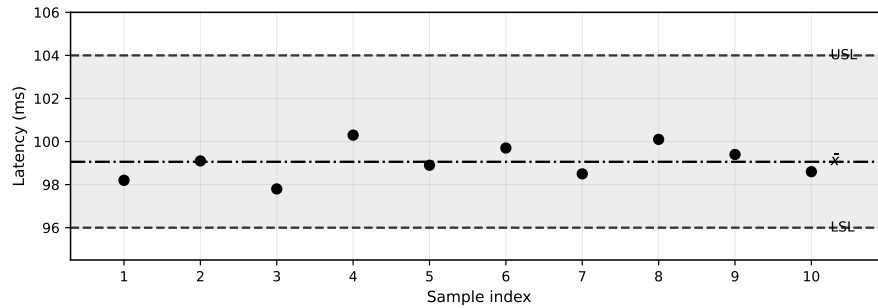


Figure 14.2: Ten latency measurements plotted against the LSL–USL tolerance band. All measurements fall comfortably within the specification.

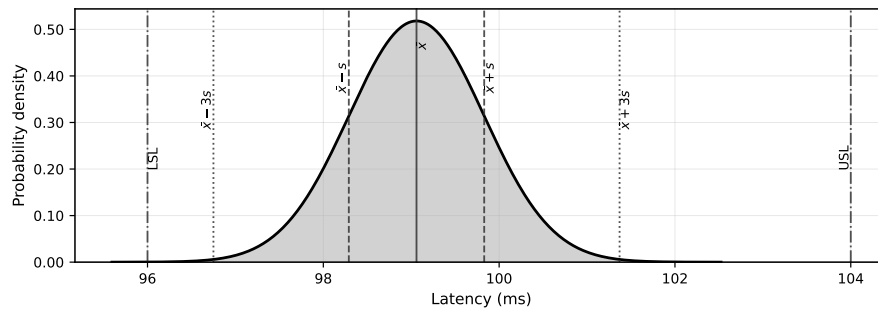


Figure 14.3: Normal distribution fitted to the latency data ($\bar{x} = 99.06$ ms, $s = 0.77$ ms). The $\pm 3\sigma$ shaded region falls well inside the LSL and USL lines, confirming ample margin.

14.3.4.1 Step 1 — Compute the mean

Using Equation 14.1:

$$\bar{x} = \frac{98.2 + 99.1 + 97.8 + 100.3 + 98.9 + 99.7 + 98.5 + 100.1 + 99.4 + 98.6}{10} = \frac{990.6}{10} = 99.06 \text{ ms}$$

14.3.4.2 Step 2 — Compute the standard deviation

First, compute each squared deviation $(x_i - 99.06)^2$:

i	x_i (ms)	$(x_i - 99.06)^2$
1	98.2	0.7396
2	99.1	0.0016
3	97.8	1.5876
4	100.3	1.5376
5	98.9	0.0256
6	99.7	0.4096
7	98.5	0.3136
8	100.1	1.0816
9	99.4	0.1156
10	98.6	0.2116
Σ		6.0240

Using Equation 14.2:

$$s = \sqrt{\frac{6.0240}{10-1}} = \sqrt{\frac{6.0240}{9}} = \sqrt{0.6693} = 0.818 \text{ ms} \approx 0.77 \text{ ms (rounded for display)}$$

14.3.4.3 Step 3 — Compute the margin

Using Equation 14.3, and checking the upper limit (the closer one, since $\bar{x} = 99.06$ is nearer to the centre than to either limit):

$$z = \frac{USL - \bar{x}}{s} = \frac{104.0 - 99.06}{0.77} = \frac{4.94}{0.77} = 6.41$$

A margin of 6.41 standard deviations is exceptionally large. Under a normal distribution, the probability of a single measurement exceeding USL is $p \approx 7 \times 10^{-11}$ — effectively zero for engineering purposes.

14.3.4.4 Step 4 — Compute process capability

Using Equation 14.4:

$$C_p = \frac{USL - LSL}{6s} = \frac{104.0 - 96.0}{6 \times 0.77} = \frac{8.0}{4.62} = 1.73$$

$C_p = 1.73 \gg 1.33$: the process is highly capable.

14.3.4.5 Decision

PASS. The latency test satisfies SR-07. Mean $\bar{x} = 99.06$ ms is within the 100 ± 4 ms specification. Standard deviation $s = 0.77$ ms gives $z = 6.41$ (margin to USL) and $C_p = 1.73$. No iteration is required. The result is logged with the raw data table above and signed off against SR-07.

14.4 Fault Tree Analysis

Statistical margin tells you whether the design is capable under normal operating conditions. **Fault tree analysis (FTA)** tells you how likely the design is to *fail* — and which failure path contributes most to that probability. FTA is a top-down, deductive technique: you start with an undesired top-level event (the “top event”) and systematically decompose it into the combinations of lower-level events that could cause it.

FTA was developed by Bell Telephone Laboratories in the early 1960s for the Minuteman missile program and was subsequently adopted across aerospace, nuclear, automotive, and medical-device industries. At capstone scale, a two-level fault tree takes roughly 30 minutes to construct and produces actionable prioritisation for test effort.

14.4.1 FTA Fundamentals

A fault tree consists of two types of elements:

1. **Events** — represented as rectangular boxes. Each event has an associated probability $P \in [0, 1]$. The top event is the system-level failure. Intermediate events are subsystem failures. Basic (leaf) events are failure modes with known or estimated probabilities.
2. **Gates** — logical connectives that determine how child events combine to produce the parent event. The two gates used in this chapter are the **OR gate** and the **AND gate**.

Probabilities for basic events come from reliability databases, manufacturer datasheets, field-failure data, or engineering estimates. For a capstone project, estimates based on similar systems are acceptable, provided they are documented and flagged as estimates.

14.4.2 OR and AND Gates

OR gate. The parent event occurs if *any* child event occurs. For n statistically independent children with probabilities $P_1, P_2, \dots, P_n$:

$$P(\text{parent}) = 1 - \prod_{i=1}^n (1 - P_i) \quad (14.5)$$

This is the complement of the probability that *no* child event occurs. For small probabilities, the approximation $P(\text{parent}) \approx \sum P_i$ is convenient but overestimates slightly; Equation 14.5 is exact (under the independence assumption).

AND gate. The parent event occurs only if *all* child events occur simultaneously. For independent children:

$$P(\text{parent}) = \prod_{i=1}^n P_i \quad (14.6)$$

AND gates model redundancy and defence-in-depth: requiring multiple failures to coincide dramatically reduces the probability of the parent event.

14.4.3 Worked Example — Sort Failure Fault Tree

The top event for the IoT robotic sorting subsystem is “**Sort failure**” — a package is routed to the wrong bin. Figure 14.4 shows the two-level fault tree.

14.4.3.1 Step 1 — Identify the failure paths

Two paths can cause a sort failure:

1. **Sensor error** — the vision or proximity sensor misclassifies the package. Estimated probability: $P_{\text{sensor}} = 0.05$ (one in twenty classifications).

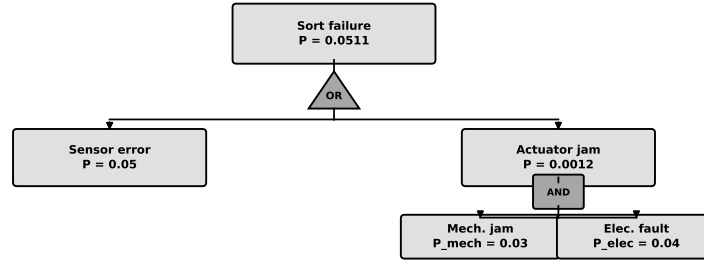


Figure 14.4: Two-level fault tree for the sorting subsystem. The OR gate at top combines “Sensor error” (dominant path) and “Actuator jam” (AND of mechanical and electrical faults). $P(\text{top}) \approx 5.11\%$.

2. **Actuator jam** — the diverter mechanism fails to move. This requires *both* a mechanical jam *and* an electrical fault to coincide (the actuator has a mechanical override that prevents jam-only failures).

- $P_{\text{mech}} = 0.03$ (mechanical binding under load)
- $P_{\text{elec}} = 0.04$ (driver circuit overcurrent trip)

14.4.3.2 Step 2 — Propagate the AND gate (Actuator jam)

Using Equation 14.6:

$$P(\text{actuator jam}) = P_{\text{mech}} \times P_{\text{elec}} = 0.03 \times 0.04 = 0.0012$$

The AND gate reduces the actuator-jam probability to 0.12% — a factor of 25 lower than either individual fault probability. This illustrates the power of mechanical redundancy: requiring two simultaneous failures makes the branch nearly negligible compared to the sensor path.

14.4.3.3 Step 3 — Propagate the OR gate (Sort failure)

Using Equation 14.5 with $P_1 = P_{\text{sensor}} = 0.05$ and $P_2 = P(\text{actuator jam}) = 0.0012$:

$$P(\text{sort failure}) = 1 - (1 - 0.05)(1 - 0.0012) = 1 - (0.95)(0.9988) = 1 - 0.9489 = 0.0511$$

The probability of a sort failure is approximately **5.11%**.

14.4.3.4 Step 4 — Prioritise test effort

The sensor error path contributes $0.05/0.0511 \approx 97.8\%$ of the top-event probability. The actuator-jam path contributes less than 2.5%.

Test priority: Sensor classification accuracy is the highest-priority test target. A test procedure that probes sensor performance across a range of package colours, orientations, and lighting conditions will do far more to reduce system risk than an equivalent test effort spent on actuator reliability.

This is the operational payoff of FTA: not just a number, but a ranked list of where to spend limited test time.

14.5 The Documented Iteration Decision

Not every test produces a “PASS” result on the first attempt. When a test fails, the engineering discipline is not to adjust the prototype until it passes and then re-record only the passing run. That practice — sometimes called **cherry-picking** — destroys the evidentiary value of the test record and, in regulated industries, constitutes falsification.

The correct procedure is the one shown in Figure 14.1: record the failing result, decide whether to iterate, scope the change, and re-test with a new procedure run. Each pass through the loop produces one documented data point. The full sequence — including failures — is the design history.

A documented iteration decision has three components:

1. **Evidence.** The specific failing result and how far it missed the acceptance criterion. Example: “Mean latency $\bar{x} = 112.4$ ms, exceeds USL of 104.0 ms by 8.4 ms.”
2. **Decision.** What change will be made, and the engineering rationale. Example: “Reduce MQTT publish rate from 100 ms to 50 ms intervals to reduce broker queue depth.”
3. **Scope.** Exactly which design artifacts are affected and what must be re-tested as a result. Example: “Firmware only (commit hash to follow). No schematic or mechanical changes. Re-run latency test (Procedure TEST-07-v2).”

Scoping the change is essential. A change that is broader than necessary triggers unnecessary re-tests; a change that is narrower than necessary leaves correlated failure modes unaddressed. The fault tree is useful here: if the sensor classification test fails, the fault tree tells you immediately that fixing the sensor path will reduce $P(\text{sort failure})$ from 5.11% to approximately 0.12%. That is the quantitative case for the iteration decision.

14.5.0.0.1 In Practice. Real engineering teams maintain an iteration log — sometimes called a **discrepancy report** (DR) or **non-conformance report** (NCR) — that links each failing test to the change made in response and the follow-up test that cleared it. For a capstone project, a table in the Design History File with columns (Test ID, Date, Result, Deviation, Change Made, Re-test ID, Final Result) achieves the same function. This table, submitted at Gate 3, demonstrates that the team tested rigorously, responded to failures rationally, and closed every open item before delivery.

14.5.0.0.2 Common Pitfalls.

- **Testing only the happy path.** A sorter tested only with well-oriented, brightly lit packages of uniform size tells you nothing about field performance. The test procedure should include at least one adversarial condition (awkward orientation, dim lighting, undersized package) for every sensor-related acceptance criterion.

- **Recording only the final pass.** If the raw data shows ten attempts before the eleventh passed, and only the eleventh is submitted, the record is misleading. All runs belong in the log.
- **Changing the specification to fit the result.** If the design cannot meet 100 ± 4 ms latency, the correct response is to iterate the design — not to revise the specification to 100 ± 15 ms without documenting the engineering rationale and obtaining stakeholder approval. Specification changes are legitimate; undocumented ones are not.
- **Confusing C_p with C_{pk} .** C_p measures spread relative to the tolerance band. C_{pk} additionally accounts for off-centre means. For a capstone project with a well-centred process, the distinction is minor; for a production process, C_{pk} is the stronger metric.
- **Ignoring the fault tree after building it.** The fault tree is not a deliverable; it is a tool. If the sensor path dominates the failure probability, that dominance should appear in the test plan as additional sensor test cases, not just as a number in an appendix.

Try It Yourself

A motor-driver PCB is tested for thermal performance. Eight temperature measurements ($^{\circ}\text{C}$) recorded at the hottest component under full load:

62.1, 63.4, 61.8, 64.2, 63.0, 62.7, 63.8, 62.5

The thermal specification is $60\text{--}70^{\circ}\text{C}$ ($\text{LSL} = 60^{\circ}\text{C}$, $\text{USL} = 70^{\circ}\text{C}$).

- Compute $\bar{x}$ (Equation 14.1) and s (Equation 14.2). Show all intermediate squared deviations.
- Compute $z = (\text{USL} - \bar{x})/s$ (Equation 14.3) and $C_p = (\text{USL} - \text{LSL})/(6s)$ (Equation 14.4). Does the thermal design pass? Justify your answer with reference to both z and C_p .
- A separate fault tree models the risk of a board-level failure. The top event ("Board failure") has an OR gate at the top combining two branches:
 - Branch 1: "Thermal runaway" with $P = 0.02$.
 - Branch 2: "Short circuit", modelled as an AND gate combining $P_a = 0.06$ and $P_b = 0.05$.

Using Equations 14.6 and 14.5, compute $P(\text{top event})$. Which branch dominates? What test should be prioritised?

Review Questions

1. (*conceptual*) What is the difference between a *functional demonstration* and a *quantitative performance test*? When is each sufficient? Give one example of a claim that can be supported by a demonstration alone and one that requires quantitative testing.

2. (*conceptual*) Explain why a test written *after* the prototype is built tends to confirm success rather than probe risk. What procedural safeguard does this chapter recommend, and why does it work?
3. (*applied, calculation*) Eight current measurements (mA) are taken from a power-supply output: 142, 138, 145, 140, 143, 139, 144, 141. Specification: 130–155 mA (LSL = 130 mA, USL = 155 mA). Compute $\bar{x}$, s , $z = (\text{USL} - \bar{x})/s$, and C_p . Does the design pass? (Use Equation 14.4.)
4. (*applied, FTA*) A fault tree top event has an OR gate combining two branches: Branch A with $P_A = 0.08$ and Branch B (an AND gate with $P_B = 0.10$ and $P_C = 0.07$). Compute $P(\text{top})$. Which branch should be tested first, and why? (Use Equations 14.5 and 14.6.)
5. (*applied, multi-step*) A voltage regulator output must meet USL = 5.0 V, LSL = 4.5 V. Five measurements: 4.71, 4.83, 4.68, 4.79, 4.75 V. Compute $\bar{x}$, s , z , and C_p . A sixth measurement of 4.45 V is subsequently recorded. Recompute all four values including the sixth point. Does the design still pass? Explain how a single outlier affects both z and C_p .

Portfolio Entry

Your Chapter 14 portfolio entry comprises three items, each linked to a specific specification requirement in your project:

1. **Test procedure document.** Write one complete test procedure for the highest-priority quantitative requirement in your specification. The procedure must include: purpose, specification requirement ID, LSL and USL, equipment list, numbered steps, acceptance criteria, and a signature block. The procedure must be written before you run the test.
2. **Raw data table and statistical summary.** Record at least eight repeated measurements under the conditions specified in your procedure. Compute $\bar{x}$, s , z (to both limits), and C_p . State explicitly whether the design passes. If it fails, document the iteration decision using the three-component format (evidence / decision / scope) from Section 14.5.
3. **Fault tree and iteration decision memo.** Construct a two-level fault tree for your system's most significant failure mode. Identify at least one OR gate and at least one AND gate. Compute $P(\text{top event})$ and identify the dominant failure path. Write a one-paragraph iteration decision memo stating which test case you will add or expand as a result of the fault-tree analysis.

Submit these three items as Section 14 of your prototype documentation package. All three must be present for the Gate 3 review.

Chapter Summary

This chapter introduced three interlocking tools for engineering validation.

Test procedures written in advance eliminate confirmation bias by committing to acceptance criteria before the prototype is touched. A procedure specifies purpose, equipment, steps, expected outputs, and pass/fail thresholds — all traceable to a specification requirement. Without this traceability, a test result is an observation; with it, the result is evidence.

Measurement statistics ($\bar{x}$, s , z , C_p) characterise not just what the design measured on a single occasion, but how consistently it performs across repeated trials. Margin z quantifies the distance to the nearest specification limit in units of the natural variation; process capability C_p quantifies how well the variation fits inside the full tolerance band. For the sorting subsystem, ten latency measurements yielded $\bar{x} = 99.06$ ms, $s = 0.77$ ms, $z = 6.41$, and $C_p = 1.73$ — all indicating a design that passes SR-07 with substantial headroom.

Fault tree analysis extends validation from “does it work?” to “how likely is it to fail, and why?” By decomposing a top-level failure event through OR and AND gates, FTA produces a ranked list of failure paths ordered by probability. For the sorting subsystem, the sensor error path ($P = 0.05$) dominates the actuator-jam path ($P = 0.0012$), driving $P(\text{sort failure}) \approx 5.11\%$ and directing test effort toward sensor classification accuracy.

Together, these tools transform the Gate 3 deliverable from a claim (“it works”) to a demonstration (“it works, here is the evidence, and here is how we know the evidence is sufficient”). The documented iteration loop — failing tests recorded, changes scoped, re-tests executed — is the design history that reviewers, auditors, and future teammates need.

Chapter 15 turns from technical validation to intellectual property: having proven that the design works and documented the proof, the next question is how to protect what you have just created.

INTELLECTUAL PROPERTY BASICS

15.0.0.0.1 Where this fits. Chapter 14 validated that the IoT robotic sorting sub-system performs as specified — sensors confirmed, firmware tested, Gate 3 acceptance criteria met. Before that validated design is shown to an external manufacturer, presented at a trade show, or handed to a licensing partner, a different question must be answered: *who owns what, and how is it protected?* This chapter addresses that question. It introduces the four main categories of **intellectual property** protection available to engineering teams, explains how ownership is determined in employment and contract relationships, and establishes the procedural habits — NDAs, prior-art searches, timely filings — that separate teams that retain the value of their innovations from those that accidentally surrender it.

15.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Distinguish the four main types of IP protection and state what each covers.
2. Explain IP ownership in an employment context and identify what your contract determines.
3. Recognise when an NDA is required and what it does and does not protect.
4. Identify the IP considerations relevant to your prototype and know when to consult a lawyer.

A working prototype is an achievement. It is also, depending on what it contains, a liability if it is shown to the wrong person at the wrong moment without the right paperwork in place. The sensor array your team spent three months tuning, the inference algorithm that runs at a tenth of the compute budget of any comparable product, the trained model weights — none of these are automatically protected simply because your team created them. Protection is an active choice, made at specific moments in the development timeline, governed by specific legal instruments. This chapter gives you the vocabulary and the procedural awareness to make those choices deliberately rather than by accident.

15.1 Why IP Matters to Technicians

The prototype you build may be your employer's most valuable asset. The firmware you write at Stage 3 encodes design decisions that took months to converge. The

sensor calibration routine that eliminates thermal drift is not obvious — it is the product of systematic experimentation and may be genuinely novel. The BOM you assembled, the supplier relationships you established, and the test data you collected all have economic value that persists long after the prototype has been demonstrated.

IP law exists to provide a framework for capturing and defending that value. It does so imperfectly — enforcement is expensive, international coverage is fragmented, and small teams rarely have the resources to litigate. But the framework also creates *presumptive rights* that are cheap to establish and expensive to ignore. A provisional patent application filed for a few hundred dollars before a conference presentation preserves a filing date that cannot be recovered after the fact. An NDA signed before showing a prototype to a contract manufacturer costs nothing but fifteen minutes; the absence of that signature can cost everything.

Understanding IP is not a specialisation for lawyers. It is a baseline competency for anyone who creates things that other people might want to copy, license, or claim as their own.

15.2 Types of IP Protection

Figure 15.1 summarises the four main categories of IP protection across four attributes. Each category covers a different kind of creative or commercial asset, operates through a different legal mechanism, and involves a different set of trade-offs.

	Protection Mechanism	Duration	Registration Required	Disclosure Trade-off
Patent	Government-granted exclusive right to exclude others	20 years from filing date	Yes — patent application required	Full public disclosure of invention
Trade Secret	Confidentiality (NDAs, access controls)	Indefinite while secrecy maintained	No — protection is automatic	No disclosure; lost if secret is revealed
Copyright	Exclusive right to copy, distribute, derive	Life + 70 years (author); 95 years (work for hire)	No — automatic on creation	Work must be expressed and observable
Trademark	Brand identifier (name, logo, slogan)	Indefinite with continued use & renewal	Optional but strongly recommended	Public use required to maintain rights

Figure 15.1: Comparison of the four main IP protection categories across key attributes. Duration and registration requirements differ substantially across categories; the right choice depends on what is being protected and how long secrecy versus exclusivity serves the business.

15.2.1 Patents

A **patent** grants its holder the exclusive right to make, use, sell, and import a claimed invention for a fixed period — twenty years from the filing date for a utility patent in Canada and the United States. In exchange for that exclusivity, the inventor discloses the invention fully and publicly. This is the fundamental trade-off of the patent system: a temporary monopoly in exchange for permanent public knowledge.

For a patent to be granted, the claimed invention must satisfy three criteria. **Novelty**: the invention must not have been publicly disclosed before the priority

date. **Non-obviousness** (“inventive step” in Canadian and European terminology): the invention must not be an obvious extension of what a person skilled in the relevant field would already know. **Utility**: the invention must have a specific, credible, and substantial use.

A **provisional patent application** is a lower-cost, lower-formality filing that establishes a priority date without beginning the examination process. It expires after twelve months unless a full (non-provisional) application is filed. For engineering teams at the prototype stage, a provisional application is the most practical instrument for preserving patent rights before a public disclosure — a conference presentation, a trade-show demonstration, or a publication — that would otherwise destroy novelty.

15.2.2 Trade Secrets

A **trade secret** is any information that (a) derives economic value from not being generally known, (b) is not readily ascertainable by others who could benefit from it, and (c) is subject to reasonable steps to maintain its secrecy. Unlike a patent, a trade secret requires no registration and involves no disclosure. Protection is indefinite — provided the secret remains secret.

The critical phrase is “reasonable steps.” Courts have found that trade secret protection is lost when the holder fails to implement basic confidentiality controls: access logging, need-to-know restrictions, confidentiality clauses in employment agreements, and NDAs with external parties. A company that leaves its training dataset on a shared drive without access controls and then tries to sue a departing employee for misappropriation will find that its trade secret claim is difficult to sustain.

The strategic alternative to a trade secret is a patent. The choice is not always obvious. A patent provides clear, enforceable rights but requires disclosure and expires. A trade secret provides indefinite protection but can be lost to independent discovery, reverse engineering (where permitted), or simple carelessness. For formulas, algorithms, and processes that cannot be reverse-engineered from the product — the canonical example is the Coca-Cola formula — the trade secret may be the superior instrument. For hardware geometries or circuit topologies that a skilled engineer could deduce from a production unit, a patent is usually preferable.

15.2.3 Copyright

Copyright protects original works of authorship fixed in a tangible medium. In engineering contexts this includes firmware source code, schematic files, PCB layout files, simulation scripts, test harnesses, documentation, and this textbook. Copyright arises *automatically at the moment of creation* — no registration, no notice, no filing. In Canada and the United States, the term for a work created by an individual author is the life of the author plus seventy years.

Copyright protects the *expression*, not the underlying idea. Two engineers can independently write firmware that performs the same function; copyright does not

prevent that. What copyright prevents is one engineer copying the other's *source file* and redistributing it as their own. This distinction — idea versus expression — is fundamental and frequently misunderstood.

In an employment context, firmware and documentation created by an employee in the scope of their employment is typically a **work made for hire**, meaning the employer, not the employee, is the legal author and first copyright owner. In a contracting context, the situation is less clear and must be addressed explicitly in the contract (see Section 15.5).

15.2.4 Trademarks

A **trademark** is a word, name, symbol, design, or combination thereof that identifies the source of goods or services and distinguishes them from competitors'. Trade-mark rights arise from *use in commerce* — a mark in active, public commercial use acquires common-law protection in the geographic area where it is used, regardless of registration. Registration with the Canadian Intellectual Property Office (CIPO) or the United States Patent and Trademark Office (USPTO) provides additional benefits: national constructive notice, the right to use the ® symbol, and a stronger foundation for international filings.

For a team at the prototype stage, trademark questions are secondary to patent and trade-secret questions. The product has not yet launched commercially, so there is no use in commerce. However, selecting a product name early — and verifying that it does not conflict with an existing registered mark in the target market — avoids a costly rebrand after investment has been made in packaging, labelling, and marketing materials.

15.3 IP Ownership in Employment

The default rule in most common-law jurisdictions is that inventions and creative works produced by an employee *within the scope of their employment* belong to the employer, not the employee. This rule applies even when the work is performed at home, outside normal hours, using personal equipment — provided the work relates to the employer's business or uses information or resources to which the employee had access through the employment relationship.

The **employment agreement** modifies this default and is the document that actually determines ownership in most disputes. A well-drafted employment agreement will include:

- an *IP assignment clause* assigning to the employer all inventions and works related to the employer's business, whether created during or after working hours;
- a *prior inventions schedule* in which the employee lists inventions they created before employment that they wish to retain; and
- a *non-compete and non-solicitation clause* restricting what the employee may do for a defined period after leaving.

The phrase **scope of employment** is the battleground in most disputes. Courts apply a multi-factor test that includes: whether the work was the type the employee was hired to perform; whether the work occurred substantially within authorised hours and space; and whether the work was motivated, at least in part, by a purpose to serve the employer. A technician hired to develop IoT firmware who writes, on a personal laptop on a Sunday, a sensor driver that solves a problem the team has been trying to solve for three weeks, will find it very difficult to claim personal ownership of that driver. The work falls squarely within the scope of employment regardless of when and where it was performed.

The practical guidance is simple: read your employment agreement before you start working. If there is no prior inventions schedule and you have pre-existing IP you wish to retain, negotiate its inclusion before signing. After you have started working, the opportunity to carve out personal inventions from the employer's claims becomes much narrower.

15.4 Non-Disclosure Agreements

A **non-disclosure agreement** (NDA) — also called a **confidentiality agreement** — is a contract in which one or both parties agree not to disclose specified confidential information to third parties. An NDA is the primary instrument for sharing a design with an external party — a contract manufacturer, a supplier, a potential investor, an academic advisor — without sacrificing trade-secret protection or triggering the novelty clock on a patent application.

A well-drafted NDA for an engineering prototype exchange typically includes:

1. **Definition of confidential information.** Specify precisely what is covered: technical drawings, firmware source code, training datasets, BOM details, and performance data. Overly broad definitions ("all information exchanged") can be unenforceable; overly narrow definitions leave gaps.
2. **Permitted uses.** State explicitly what the receiving party may do with the information — evaluate it for a potential contract, quote on manufacturing, provide engineering feedback — and what they may not do — share it with subcontractors without consent, use it for their own competing development.
3. **Term and survival.** Specify how long the obligation lasts and which obligations survive termination of the agreement (typically the confidentiality obligations themselves).
4. **Exclusions.** Standard exclusions include information that was already publicly known, information independently developed by the receiving party, and information received from a third party without restriction.

What an NDA does *not* protect is equally important to understand. An NDA does not give you a patent. If the receiving party independently develops the same invention without using your confidential information, the NDA provides no remedy. An NDA does not protect information that is already in the public domain — if you disclosed your design at a conference last month without a patent filing, the NDA you sign this month cannot retroactively un-disclose it. An NDA also does

not prevent a receiving party from hiring your employees and acquiring the knowledge through them, unless the NDA is coupled with an appropriate non-solicitation clause.

15.5 IP Assignment in Contract Work

When a company engages an independent contractor to perform design work, the default IP ownership rule differs from the employment rule. In most common-law jurisdictions, an independent contractor retains ownership of work product unless an explicit written assignment transfers those rights to the client. This reverses the employment default and catches many companies by surprise.

A contract that says “the contractor will design a custom sensor interface PCB for \$8,000” says nothing about who owns the resulting schematic, firmware, or any patentable improvement embedded in the design. Without an explicit assignment, the contractor owns all of it. The client has, at best, an implied licence to use the specific deliverable for the specific purpose contracted — not a right to modify it, not a right to have it manufactured by a different vendor, and certainly not a right to patent it.

The remedy is a clear **IP assignment clause** in the contract, negotiated before work begins, that assigns to the client all rights in the work product, including any inventions, copyrights, and moral rights. The contract should also address:

- *Background IP*: technology the contractor brings to the engagement that pre-exists the contract. The contractor typically retains this; the client receives a licence to use it only as embedded in the deliverable.
- *Foreground IP*: new inventions and works created specifically for the engagement. This is what the assignment clause transfers.
- *Third-party IP*: open-source libraries, licensed components, and third-party toolchains embedded in the deliverable. The client needs to understand the licence terms for everything that ships.

The time to negotiate IP ownership is before the statement of work is signed, not after the prototype is demonstrated. After delivery, the contractor has received payment and has no incentive to grant additional rights; the client has expended engineering resources on a design it may not legally be able to commercialise.

15.6 The Prior-Art Search

A **prior-art search** is a systematic review of publicly available documents — patents, published patent applications, academic papers, product specifications, conference proceedings — to determine whether an invention is novel before committing to a design direction or filing a patent application. Conducting a prior-art search early avoids investing significant engineering resources in a direction that is already patented, teaches design-around opportunities, and provides the technical background that a patent attorney will require when drafting claims.

The primary search tools available without cost are:

- **Google Patents** (patents.google.com): full-text search across US, European, PCT, and many national patent databases, with machine-translation support for non-English documents.
- **USPTO Patent Full-Text Database** (patents.uspto.gov): authoritative for US filings; supports classification-based searches using the Cooperative Patent Classification (CPC) system.
- **Espacenet** (worldwide.espacenet.com): the European Patent Office's database, covering over 130 million documents from 100-plus countries.
- **CIPO Patent Database** (brevets-patents.ic.gc.ca): the Canadian Intellectual Property Office's searchable database for Canadian filings.

Effective searching combines keyword searches with **classification-based searches** using the CPC. A keyword search for "sensor array classification neural network" will return many irrelevant results; a search limited to CPC subclass G06N 3 (neural network computing) and G01D 5 (measuring instruments, sensor arrays) is far more targeted.

The output of a prior-art search for the portfolio entry in Section 15.7.1.0.2 should include: the databases searched, the search terms and classification codes used, a list of the most relevant documents found, and a brief assessment of how the invention differs from each. This record serves two purposes: it demonstrates due diligence, and it becomes the starting point for a patent attorney's more thorough patentability opinion.

15.7 When to Ask a Lawyer

This chapter provides *professional literacy*, not legal advice. The distinction matters. Professional literacy means you can identify that a situation raises an IP issue, describe it accurately, and ask the right questions. Legal advice means a qualified professional analyses the specific facts, applies the applicable law, and tells you what to do. The two are not interchangeable.

The situations that require a **patent agent** or **patent attorney** include:

- Drafting and filing a patent application. Claims drafting is a specialised skill; poorly drafted claims can leave large gaps in protection that competitors will exploit.
- Evaluating a freedom-to-operate opinion before commercialising a product. A freedom-to-operate (FTO) analysis determines whether your product would infringe any valid, enforceable patent in the target markets.
- Responding to a cease-and-desist letter or an office action from a patent office.
- Negotiating an IP licence agreement or a technology transfer agreement.

The situations that you can handle with professional literacy — but should escalate if ambiguous — include:

- Recognising that a disclosure event is approaching and ensuring a provisional patent application is filed or NDAs are in place beforehand.
- Reviewing a standard NDA for the four elements described in Section 15.4 and flagging missing or unusual provisions.
- Identifying which elements of a design may be protectable and preparing a structured description for the attorney’s review.
- Confirming that an employment or contractor agreement includes an explicit IP assignment clause.

The earlier an attorney is engaged, the less expensive the engagement tends to be. A brief consultation at Stage 2 to advise on patentability and filing strategy costs far less than attempting to correct a defective filing or recover from an invalidating disclosure after the fact.

15.7.1 Worked Example — IP Audit for the Running Example

Figure 15.2 maps the IP considerations for the IoT robotic sorting subsystem across the Stage-Gate timeline. The following audit applies each category in turn.

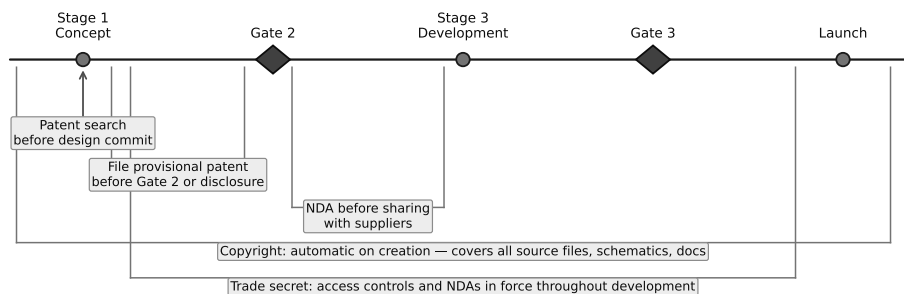


Figure 15.2: IP considerations mapped across the Stage-Gate timeline for the IoT robotic sorting subsystem. Diamond markers denote gates; circle markers denote stages. Each annotation below the timeline identifies the appropriate moment for the corresponding IP action.

The running example system comprises custom AI inference firmware, a custom analog sensor array design, an MQTT protocol implementation, and standard mechanical components. At Stage 3/4, the team should conduct the following IP audit:

1. **Patent-eligible.** The custom sensor-array geometry combined with the AI classification algorithm constitutes a candidate for utility patent protection. The combination is novel (no prior art found for this specific geometry paired with this classification approach) and non-obvious (the performance improvement is not predictable from either component alone). The team should engage a patent agent to assess patentability and draft a provisional application before the next public disclosure.

2. **Trade secret.** The trained model weights and the training dataset are best protected as trade secrets. They cannot be recovered by reverse-engineering the firmware binary, they derive substantial economic value from their secrecy, and the cost of re-creating them is high. Required controls: encrypted storage, access-logged retrieval, training pipeline under version control in a private repository, and NDAs with any external party who receives model outputs.
3. **Copyright (automatic).** All firmware source files, schematic files, PCB layout files, simulation scripts, and this documentation are protected by copyright from the moment of creation. The team does not need to file anything; they should, however, ensure that the employment agreements of all contributing team members contain IP assignment clauses so that the employer holds a consolidated copyright, not a patchwork of individual ownership claims.
4. **Trademark.** Not applicable at prototype stage. The product has not launched commercially, so there is no mark in use. The team should select a candidate product name now and run a clearance search against CIPO and USPTO databases before investing in branding.
5. **Before trade-show disclosure.** Before presenting the system at any public venue, the team must either file a provisional patent application covering the sensor-array and algorithm combination, or obtain signed NDAs from every attendee who will receive a technical briefing. In practice, a trade show cannot guarantee NDA coverage; the provisional filing is the only reliable protection.

15.7.1.0.1 In Practice. A medical-device team at a university incubator demonstrated their novel implant sensor geometry at a regional engineering conference six weeks before their provisional patent application was ready to file. A competitor's engineer attended the demonstration, took detailed photographs of the poster, and filed a patent application on a closely related design three weeks later. When the university team finally filed, the competitor's earlier publication date (the conference paper uploaded to the conference website) constituted prior art that partially invalidated the university team's novelty claim. The cost of the conference registration: \$400. The cost of the resulting patent dispute: \$180,000 in legal fees over three years, with a settlement that required the university team to license the technology back from the competitor. Filing the provisional application before the conference would have cost \$320 in USPTO fees.

15.7.1.0.2 Common Pitfalls.

- **Public disclosure before filing.** Any public disclosure — conference poster, pre-print, trade-show demonstration, social media post with technical detail — starts a twelve-month grace period in the United States (no grace period in most other jurisdictions) after which the disclosure itself constitutes invalidating prior art. File the provisional before you disclose, not after.
- **Assuming employer tools means no IP assignment.** Using a personal laptop with employer-licensed software to solve a work problem does not move the work outside the employer's ownership claim. Scope of employment is determined by the subject matter and purpose of the work, not the physical location of the keyboard.

- **Skipping the NDA before showing a prototype.** A handshake and a verbal assurance that “everything we discuss is confidential” has no legal effect. An NDA is a written contract; the writing requirement is not a formality. Prepare a standard one-page mutual NDA template in advance, and make signing it the first step of every technical meeting with an external party.

Try It Yourself

A start-up builds a wearable ECG monitor with the following elements:

- (a) A custom electrode adhesive geometry that improves skin-contact impedance by 40% compared to commercially available electrodes.
- (b) A proprietary signal-processing algorithm trained on 50,000 de-identified patient records, achieving clinical-grade arrhythmia detection at a fraction of the compute cost of prior art.
- (c) Firmware written by an independent contractor under a fixed-price contract that states “all work product belongs to the contractor,” with no IP assignment or licence provisions.
- (d) The brand name “CardioSense,” which the team has been using in investor presentations for six months.

For each element, identify the most appropriate form of IP protection and state one risk if that protection is not pursued.

Review Questions

1. (*conceptual*) Explain the trade-off between filing a patent and keeping a process as a trade secret. Under what conditions would you choose each?
2. (*conceptual*) A firmware developer working at a start-up claims personal ownership of code because they wrote it at home on weekends, but using work equipment and solving a work problem. Explain, using the employment IP doctrine, why this claim is unlikely to succeed.
3. (*applied*) Identify the most appropriate IP protection for each:
 - (a) a novel battery-charging circuit topology;
 - (b) a customer list compiled over five years;
 - (c) the source code for an embedded sensor driver;
 - (d) the name “SortBot Pro” on a product label.
4. (*applied*) A team is about to show their prototype to a potential contract manufacturer. List three specific items that should be in the NDA and one item that an NDA typically does *not* protect.

5. (*applied, multi-step*) A contractor is hired to design a custom PCB under a contract that states “all work product belongs to the contractor.” The client later discovers the PCB contains a patentable improvement. Who owns the patent right? What should the contract have said instead, and at what stage should it have been negotiated?

Portfolio Entry

Produce an IP checklist for your project with four sections:

- (a) *Protectable elements* — list each design element or feature that may be eligible for patent, trade secret, or copyright protection, with the recommended form of protection.
- (b) *Ownership assignment* — state who owns each element (employer, contractor, joint) and whether your employment or contractor agreement explicitly addresses it.
- (c) *NDA requirement* — identify every external party (supplier, manufacturer, advisor) who will see the prototype and state whether an NDA has been executed.
- (d) *Prior-art search status* — record the databases searched, search terms used, and any relevant prior art found.

Submit this as Section 15 of your prototype documentation package.

Chapter Summary

Intellectual property protection is not a legal afterthought reserved for large companies with dedicated counsel. It is a set of active, time-sensitive choices that engineering teams must make at specific moments in the development timeline — before a public disclosure, before showing a prototype to a supplier, before signing a contractor agreement, before committing to a product name.

The four main categories of protection — **patent**, **trade secret**, **copyright**, and **trademark** — cover different kinds of assets, operate through different legal mechanisms, and involve different trade-offs between disclosure and exclusivity. Copyright arises automatically; the others require deliberate action. Ownership in employment defaults to the employer for work within the scope of employment; in contracting, it defaults to the contractor unless an explicit assignment clause provides otherwise. NDAs are the primary instrument for sharing designs with external parties without sacrificing trade-secret protection or novelty.

The procedural habits this chapter asks you to form are simple: conduct a prior-art search before committing to a design direction; file a provisional patent application or obtain NDAs before any public disclosure; read your employment agreement and understand what you own and what your employer owns; and engage a patent agent at the first sign that your design may be commercially significant.

Chapter 16 compiles every section produced since Chapter 1 into the coherent portfolio that Gate 3 requires, integrating the IP checklist from Section 15, the version-controlled design history from Chapter 13, the validation records from Chapter 14, and the economic analysis from Chapter 12 into a single, auditable package that a gate reviewer can evaluate with confidence.

DOCUMENTATION & PORTFOLIO ASSEMBLY

16.0.0.0.1 Where this fits. Chapter 15 completed the intellectual-property checklist — the final artifact produced by Stage 3 field work. This chapter sits at the Gate 3 threshold and performs a different task: it compiles every artifact produced since Concept into a single, coherent portfolio package that a review committee can navigate, audit, and sign off. No new design work happens here. The work is assembly, reconciliation, and gap closure.

16.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Assemble a portfolio by mapping each required section to the stage artifact that produced it.
2. Reconcile an as-built BOM against the design BOM and record every deviation as a documented decision.
3. Compute traceability coverage and close gaps before Gate 3 submission.

Every chapter in this textbook asked you to produce a deliverable and submit it as a portfolio entry. This chapter collects those entries. If the artifacts exist, assembly takes an afternoon. If they do not — if specifications were written from memory the night before the review — the team is not assembling a portfolio; it is fabricating one. The distinction matters to a reviewer, and it will matter to a regulator.

16.1 Three Documentation Principles

Three principles underlie every documentation practice introduced in this course.

Record decisions, not outcomes. An outcome tells the reader what happened. A decision record tells the reader why an alternative was chosen, what evidence supported it, and who was accountable. A test report that says “the sort latency met spec” is an outcome. A test report that says “the sort latency was measured at 94 ms against a specification of ≤ 104 ms using the procedure in Appendix B; the margin is attributed to the dual-core scheduling change documented in ECO-003” is a decision record. Only the second version allows a future engineer — or a Gate 3 reviewer — to reproduce the result or extend the design.

Enable reproduction. A portfolio entry that cannot be used to reproduce the result it describes is incomplete. Reproducibility requires: the exact part numbers used (not the ones originally specified), the exact test procedure followed (not a paraphrase), and the exact configuration of the firmware or software at the time of the test (a Git commit hash, not “the latest version”).

Documentation debt compounds. A design decision not recorded at Stage 2 generates a question at Stage 3. That question requires someone to reconstruct the reasoning from memory, email threads, or bench notes — work that takes longer than the original record would have, and produces a less reliable result. If the reconstructed rationale is wrong, it generates a defect that propagates into Stage 4 and beyond. The interest rate on documentation debt is not linear: one missed record in Stage 2 can produce three rework cycles in Stage 4.

If any section of the Gate 3 portfolio must be written from memory at assembly time, the process broke down earlier. The correct response is to flag the section for remediation, document what is known, and record that the original decision was not captured at the time it was made. Fabricating confidence is worse than acknowledging a gap.

16.2 Compiling, Not Writing

The central insight of this chapter is that the Gate 3 portfolio is *compiled*, not written. Every section has a source: a stage gate, a chapter deliverable, a test record, a procurement document. Figure 16.1 shows the Stage-Gate phases across the top and the documentation artifacts each phase is expected to produce along the bottom.




Figure 16.1: Stage-Gate phases (top row) and the documentation artifacts each phase produces (bottom row). The portfolio is assembled from these artifacts at Gate 3; no section is written from scratch at assembly time.

The key observation is temporal: the Project Brief and Kano analysis were produced at Concept and Scoping; the specification, architecture, and BOM were produced during Development; the test procedure and fault-tree analysis were produced during Testing; the portfolio map and IP checklist were produced during the Launch preparation. A team that reaches Gate 3 without one of these artifacts is missing a stage output, not a portfolio section. The remedy is upstream, not cosmetic.

16.3 Portfolio Structure

The Gate 3 portfolio has fourteen sections. Figure 16.2 maps each section to the chapter that produced its source artifact.

Portfolio Section	Source Chapter
1 Project Context Brief	Ch. 1
2 Kano Analysis	Ch. 2
3 Specifications & Risk	Ch. 4
4 Architecture	Ch. 5
5 Component Selection	Ch. 6
6 DFX Review	Ch. 7
7 AI Use Log	Ch. 8
8 IoT / Safety Records	Ch. 9
9 Schedule & Risk Register	Ch. 10
10 BOM	Ch. 11
11 Cost Analysis	Ch. 12
12 Git / DHF	Ch. 13
13 Test Results	Ch. 14
14 IP Checklist	Ch. 15

Figure 16.2: Portfolio map: the fourteen required sections of the Gate 3 documentation package and the source chapter that produced each artifact. Sections produced from memory rather than from documented stage outputs must be flagged for remediation.

The fourteen sections form a logical narrative: who authorised the project and why (Sections 1–2), what it must do and how it will do it (Sections 3–5), what risks and quality requirements govern the design (Sections 6–8), how the project was planned and controlled (Sections 9–10), what it costs and whether the economics are viable (Sections 11–12), how the design was controlled and what tests were run (Sections 12–13), and whether the design is free to operate and market (Section 14). A reviewer reads the portfolio in roughly this order; gaps in the narrative signal gaps in the process.

Sections that appear thin — a Kano analysis with no customer data, a risk register with no updates since Stage 2, a BOM with no as-built reconciliation — do not become acceptable by being present. Presence without substance fails a Gate 3 review as surely as absence.

16.4 The As-Built BOM

The **design BOM** records the parts the team intended to use when the BOM was first approved. The **as-built BOM** records the parts that were actually used to build the prototype. Both documents must appear in the Gate 3 package, and every line on which they differ must carry a deviation record.

A **deviation record** contains four fields: the original part (MPN, description, unit cost), the substituted part (MPN, description, unit cost), the reason for substitution, and the disposition — either *verified equivalent* (same electrical and mechanical performance confirmed by datasheet comparison or test) or *ECO issued* (an Engineering Change Order was raised because the substitution changed a functional parameter).

16.4.0.0.1 In Practice. A team building the IoT robotic sorting subsystem submitted a Gate 3 package with a design BOM and an as-built BOM that were identical,

despite the assembler having substituted a motor driver during build because the original was out of stock. The reviewer discovered the substitution by inspecting the receipt; the package was returned with a request for the deviation record, the datasheet comparison, and the retest results on motor timing. The team lost one week. The deviation record would have taken twenty minutes to write at the time of substitution.

16.4.1 Worked Example — Sorter As-Built Reconciliation

The IoT robotic sorting subsystem design BOM had two line items that changed between the design BOM and the as-built BOM:

- (a) **IMU:** Design BOM specified the MPU-6050 at \$12.40 CAD. During procurement, the MPU-6050 was on a 14-week backorder. The ICM-42688-P was substituted at \$14.80 CAD (+\$2.40 per unit). Disposition: *verified equivalent* — the ICM-42688-P is a drop-in replacement with a compatible I²C register map at the addresses used by the firmware; verification performed by datasheet comparison and a 100-sample register-read test confirming identical output resolution and noise floor.
- (b) **PCB:** Design BOM specified a 2-layer board at \$32.00 CAD. During testing, unacceptable EMC emissions were traced to signal-return path discontinuities on the 2-layer layout. A 4-layer board at \$41.00 CAD (+\$9.00 per unit) was fabricated with dedicated power and ground planes. Disposition: *ECO issued* — ECO-007 documents the layer-count change, the EMC retest results (passed at –6 dB margin), and the updated Gerber files committed to the Git design history file (DHF) at tag `v1.1-pcb-4layer`.

The as-built unit cost increases by $\$2.40 + \$9.00 = \$11.40$ per unit relative to the design BOM. This figure must propagate to the cost analysis in Section 11 of the portfolio and to the production cost projection in Chapter 17.

16.5 Traceability Coverage

16.5.1 The Traceability Matrix

A **traceability matrix** is a two-dimensional grid that links every system requirement to at least one test case that verifies it. Rows represent requirements; columns represent test cases. A filled cell means the test case exercises the requirement. An empty cell means the requirement is either untested (a coverage gap) or that the link has not yet been recorded (a documentation gap — different in origin, identical in risk).

The traceability matrix enforces a discipline that verbal assurances cannot: it makes coverage visible, countable, and auditable. A reviewer who asks “how do you know R3 is met?” expects a cell reference and a test record, not a confident answer.

16.5.2 Computing Coverage

Traceability coverage is defined as the fraction of required requirement-to-test links that are present in the matrix:

$$\text{Coverage} = \frac{\text{number of requirements with at least one linked test case}}{\text{total number of requirements}} \times 100 \% \quad (16.1)$$

This definition counts at the requirement level: a requirement linked to three test cases counts once in the numerator, the same as a requirement linked to one. The denominator is always the total count of requirements. A Gate 3 submission should target 100% coverage; any gap must either be closed before submission or acknowledged with a written plan and timeline for closure.

Note that the definition above measures whether each requirement has *any* link, not whether all intended links are present. A more detailed audit counts the total number of planned requirement-to-test pairs and computes the fraction of those pairs that are documented. The worked example below uses the pair-counting approach because the sorter design has a specific planned link that is missing.

16.5.3 Worked Example — Sorter Coverage Audit

The IoT robotic sorting subsystem has four requirements and four test cases. Figure 16.3 shows the traceability matrix.

Requirement \ Test Case	T1	T2	T3	T4
R1: Sort latency ≤ 104 ms	●			
R2: MQTT delivery ≤ 200 ms	gap	●		
R3: Battery life ≥ 30 days			●	
R4: SF ≥ 2 (sort-gate bracket)				●

Coverage: 4 / 5 linked pairs = 80% | Gap: R2 → T1 missing

Figure 16.3: Traceability matrix for the IoT robotic sorting subsystem. Filled circles mark documented requirement-to-test links. The cell labelled “gap” (R2 → T1) identifies a planned link that is absent from the test record. Coverage: 4 of 5 planned pairs = 80%.

The four requirements and their test links are:

- (R1) **Sort latency ≤ 104 ms** — linked to T1 (latency measurement test from Ch. 14, automated over 1 000 sort cycles). Link documented. ✓
- (R2) **MQTT delivery ≤ 200 ms** — linked to T2 (end-to-end message timing test, Ch. 14). Link documented. ✓
R2 *should also* link to T1, because the latency measurement test captures the sensor-to-publish pipeline including the MQTT stack. This link was planned during test design but is absent from the test record. **Gap identified.**

- (R3) **Battery life ≥ 30 days** — linked to T3 (power budget verification using the calculation method from Ch. 9). Link documented. ✓
- (R4) **Safety factor $SF \geq 2$ for sort-gate bracket** — linked to T4 (static load test on bracket assembly). Link documented. ✓

Of the 5 planned requirement-to-test pairs, 4 are present. Applying Equation 16.1:

$$\text{Coverage} = \frac{4}{5} \times 100\% = 80\%$$

The gap is closed by adding the R2 → T1 link to the test record and confirming that the latency test procedure includes the MQTT publish step in its timing window. If the current T1 procedure times only the mechanical sort and does not include the MQTT publish, T1 must be extended — a design-of-experiment change that requires a new test run and an updated test report before Gate 3 submission. After the link is added and confirmed, coverage rises to 5/5 = 100%.

16.5.3.0.1 In Practice. A student team submitted a Gate 3 package for a temperature-controlled enclosure with a traceability matrix showing 60% coverage (3 of 5 requirements linked to tests). The two unlinked requirements were control-loop stability and fan noise. The review committee returned the package with a single action item: run the missing tests and resubmit. The team had assumed the reviewer would accept a verbal description of observed behaviour in lieu of a test record. The reviewer did not. The retest took three days; writing the test procedures before the build would have taken two hours.

16.5.3.0.2 Common Pitfalls.

- (a) **Writing requirements from memory at Gate 3.** Requirements not captured in the specification document (Ch. 4) cannot be traced to tests without fabricating the traceability — which a reviewer will detect by checking whether the test procedure predates the requirement.
- (b) **As-built BOM never reconciled.** Assemblers routinely substitute parts during build; if no one captures the substitution, the design BOM and the as-built BOM diverge silently. The divergence is discovered at the worst possible time — during a production ramp or a regulatory audit.
- (c) **Assuming 100% coverage without checking.** Coverage must be computed from the matrix, not asserted. A team that has run four tests for four requirements may still have 80% coverage if a planned link was never recorded. Count the cells.

Try It Yourself

A 3-axis force sensor subsystem has three requirements: (R1) full-scale range ≥ 50 N, (R2) linearity error $\leq 1\%$, (R3) drift $\leq 0.1\%/^{\circ}\text{C}$. Three test cases have been run: T1

(static load calibration), T2 (linearity sweep), T3 (temperature cycling). The current coverage matrix shows: $R1 \rightarrow T1 \checkmark$, $R2 \rightarrow T2 \checkmark$, $R3$ is not linked to any test case.

- (a) Compute the traceability coverage percentage using Equation 16.1. (Use the requirement-level definition: count requirements that have at least one link.)
- (b) Identify the coverage gap. Propose a specific test procedure — including what stimulus is applied, what is measured, and what pass criterion is used — that would close the gap and allow $R3 \rightarrow T3$ to be documented as a verified link.
- (c) After the build, two BOM line items changed: the strain gauge changed from SG-A at \$3.20 to SG-B at \$4.80 (reason: mechanical fit incompatibility with the sensor housing); the signal amplifier changed from INA333 at \$2.10 to AD8221 at \$5.40 (reason: noise floor of INA333 exceeded the 1 % linearity budget under the supply voltage used). Compute the total BOM cost increase per unit (one of each component) and classify each substitution as: (i) record only, (ii) record and verify equivalence, or (iii) record and issue an ECO. Justify your classification.

Review Questions

1. **(Conceptual)** Explain the statement “documentation debt compounds.” Give a concrete example of how failing to record a design decision in Stage 3 causes rework in Stage 4.
2. **(Conceptual)** What is the difference between a design BOM and an as-built BOM? Why must both appear in the Gate 3 package?
3. **(Applied, calculation)** A design has 6 requirements. The traceability matrix shows: $R1 \rightarrow T1$, $R2 \rightarrow T2$, $R3 \rightarrow T2$, $R4 \rightarrow T3$, $R5$ (no test linked), $R6 \rightarrow T4$. Compute traceability coverage using Equation 16.1. What single action closes the gap?
4. **(Applied)** An as-built BOM shows three substitutions:
 - (a) A resistor changed value (same footprint, \$0.05 difference).
 - (b) An MCU replaced with a pin-compatible alternative (\$3.20 more per unit).
 - (c) A connector replaced with a non-standard alternative requiring a PCB spin.

Classify each substitution as: (i) record only, (ii) record and verify equivalence, or (iii) record and issue an ECO. Justify your classification.

5. **(Applied, multi-step)** A 5-requirement design has the following coverage matrix: $R1 \rightarrow T1$, $R2 \rightarrow T1$ and $T2$, $R3 \rightarrow T3$, $R4$ (no test linked), $R5 \rightarrow T2$.
 - (a) Compute traceability coverage using Equation 16.1.
 - (b) A new test T4 is added, linking to R4 and R5. Recompute coverage.
 - (c) What percentage-point improvement does T4 add?

Portfolio Entry

Submit the following as your Gate 3 documentation package:

- (a) *Assembled portfolio* — all 14 sections listed in Figure 16.2 populated with artifacts from their source chapters. Sections produced from memory rather than from documented stage outputs must be flagged for remediation.
- (b) *As-built BOM* — reconciled against the design BOM with every deviation documented as a decision record (original part number, substituted part number, reason for change, and verified-equivalent or ECO reference).
- (c) *Traceability matrix* — all requirements listed, all test cases linked, coverage percentage computed using Equation 16.1. Any gap must be closed or explicitly acknowledged with a plan to close it before Gate 3 sign-off.

This is the near-final version of your prototype documentation package. Chapter 17 adds the production cost projection and the Gate 3 readiness statement to complete it.

Chapter Summary

The Gate 3 portfolio is compiled from artifacts produced at each Stage-Gate phase, not written from memory at submission time. Three principles govern documentation practice: record decisions not outcomes, enable reproduction, and recognise that documentation debt compounds. The fourteen-section portfolio map (Figure 16.2) identifies the source chapter for every required section; any section that cannot be traced to a stage artifact signals a process breakdown, not a writing task.

The as-built BOM must be reconciled against the design BOM line by line. Every deviation is a documented decision record — part numbers, cost difference, reason, and disposition (verified equivalent or ECO issued). The sorter example showed two substitutions totalling \$11.40 per unit, both fully documented and propagated to the cost analysis.

Traceability coverage is computed from the matrix using Equation 16.1. The sorter audit found one missing link ($R2 \rightarrow T1$) giving 80% coverage, and prescribed a specific corrective action before submission. A Gate 3 submission must reach 100% coverage or carry explicit acknowledgement and a closure plan for every remaining gap.

You now have a complete documentation package. Chapter 17 adds the production economics — the unit-cost projection and break-even analysis — and the Gate 3 readiness statement that converts the portfolio into a formal gate submission.

COST ANALYSIS & THE BRIDGE TO PROJECT II

17.0.0.0.1 Where this fits. Chapter 16 assembled the complete documentation package — the Design History File, test reports, and version-controlled artefacts that constitute the prototype record. This final chapter adds the two pieces that convert a documented prototype into a fundable project: a production economics analysis and a Gate 3 readiness statement. Together they answer the gate committee’s hardest question — not “does it work?” but “can it be made and sold profitably, and is the risk of proceeding lower than the risk of stopping?”

17.0.0.0.2 Learning Objectives. After completing this chapter you will be able to:

1. Project unit cost at three production volumes using the cost model established in Chapter 12.
2. Compute the revenue break-even volume and gross margin at a target price.
3. Compute total profit at a given volume.
4. Articulate Gate 3 readiness: what was proven, what remains, and why proceeding is economically justified.

Every engineering team that reaches Gate 3 has built something that works. The sorting subsystem sorts, the AI inference runs, the bracket holds. The harder question — the one the gate committee is paid to ask — is whether the team has built something that *can be manufactured at a price customers will pay*. A prototype that costs \$8,480 to produce as a single unit is not a \$8,480 product. It is the starting point for a cost-reduction journey that, if managed correctly, terminates at a unit cost of \$496 at volume 500 — a gross margin of 58.7% against a \$1,200 selling price. This chapter maps that journey in exact arithmetic, then frames the Gate 3 readiness statement that closes Project I and opens the path to Project II.

17.1 Applying the Cost Model to the Finished Prototype

Chapter 12 established the central equation of low-volume production economics. When a **fixed cost** C_{fixed} is spread over N units and a **variable cost** c_{var} is paid per unit, the unit cost is:

$$C_{\text{unit}}(N) = \frac{C_{\text{fixed}}}{N} + c_{\text{var}}. \quad (17.1)$$

This is a rectangular hyperbola in N . At $N = 1$ the entire fixed-cost burden falls on a single unit. As N grows the fixed-cost term shrinks toward zero, and C_{unit} asymptotes to c_{var} from above. No matter how large the production run, the unit cost cannot fall below the variable cost per unit — this floor is set by components, materials, and direct assembly labour, quantities that do not change with volume.

For the IoT robotic sorting subsystem the parameters established in Chapter 12 are:

$$C_{\text{fixed}} = \$8,000 \text{ CAD}, \quad c_{\text{var}} = \$480 \text{ CAD}.$$

The fixed cost covers the PCB test fixture (\$2,400), the injection-mould tool for the housing (\$4,800), and non-recurring engineering (NRE) setup charges (\$800). The variable cost reflects component cost plus estimated assembly labour at production volume, derived from the Bill of Materials validated in Chapter 11.

It is important to distinguish two cost quantities that are often confused in Gate 3 submissions.

Prototype cost per unit is the actual expenditure to produce the one physical prototype delivered at Gate 3. It consists of the Chapter 11 BOM cost — the retail component prices paid to purchase exactly the quantities needed for one unit — plus any non-recurring tooling or setup charges incurred for that single build. For the sorting subsystem:

$$C_{\text{proto}} = C_{\text{BOM}} + C_{\text{fixed}} = \$124.85 + \$8,000 = \$8,124.85 \text{ CAD}.$$

Production unit cost is what each unit costs when N identical units are produced in a single run, computed from Equation 17.1. At $N = 50$: $C_{\text{unit}}(50) = \$640$. At $N = 500$: $C_{\text{unit}}(500) = \$496$.

The \$7,628.85 gap between prototype cost and production cost at $N = 50$ is not a discount — it is the arithmetic consequence of spreading \$8,000 of fixed cost across 50 units instead of one. Using prototype cost as a proxy for production cost is one of the two most common errors in student Gate 3 submissions (the other is discussed in Section 17.6.0.0.2).

17.2 Prototype Cost vs. Projected Production Cost

Figure 17.1 makes the comparison concrete. Each pair of bars shows the prototype cost per unit (always \$8,124.85 — the same single build regardless of how many production units are imagined) alongside the production cost per unit computed from Equation 17.1.

Three observations follow directly from the figure.

First, the largest cost reduction occurs between $N = 1$ and $N = 50$: the unit cost falls by \$7,484.85, a reduction of 92%. The reduction from $N = 50$ to $N = 500$ is only

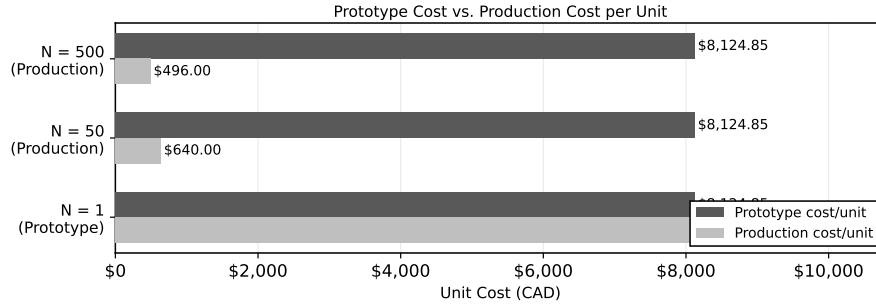


Figure 17.1: Prototype cost per unit (\$8,124.85) compared with projected production cost at $N = 50$ (\$640) and $N = 500$ (\$496). The prototype cost is misleading as a production estimate: it bundles the full \$8,000 fixed cost onto a single unit. The dramatic reduction between $N = 1$ and $N = 50$ comes entirely from spreading that fixed cost across the run.

\$144, a further reduction of 22%. The curve is steep at low volume and flat at high volume, which is the economic signature of Equation 17.1.

Second, the prototype BOM cost (\$124.85) contributes less than 2% of the \$8,124.85 prototype cost. This means that even aggressive BOM reduction — negotiating component prices, substituting parts, redesigning for fewer line items — cannot materially reduce prototype cost; only spreading the fixed cost across a larger N can do that.

Third, at $N = 500$ the unit cost of \$496 is only 3.3% above the \$480 variable-cost floor. The product is approaching the asymptote: at this point further volume increases yield diminishing returns, and attention should shift to reducing c_{var} itself — through DFM/DFA improvements, component consolidation, or a shift to a lower-cost assembly process.

17.3 Break-Even and Margin

17.3.1 Revenue Break-Even

Chapter 12 defined the **process break-even** $N^* = 14.3 \rightarrow 15$ units as the volume at which 3D-printed and injection-moulded housing costs are equal. That is a manufacturing process decision.

This chapter uses a different break-even concept. The **revenue break-even volume** N_{be} is the number of units that must be sold at price p to recover the fixed cost from the contribution margin on each sale.

Each unit sold at price p contributes $(p - c_{\text{var}})$ toward fixed-cost recovery. Setting total contribution equal to fixed cost:

$$N_{\text{be}} = \frac{C_{\text{fixed}}}{p - c_{\text{var}}}. \quad (17.2)$$

For the sorting subsystem with $p = \$1,200$ CAD:

$$N_{\text{be}} = \frac{8,000}{1,200 - 480} = \frac{8,000}{720} = 11.11 \rightarrow 12 \text{ units.}$$

Twelve units sold at \$1,200 each generate \$14,400 in revenue; the \$8,000 fixed cost is fully recovered, and the remaining \$6,400 covers the variable cost of the run ($12 \times \$480 = \$5,760$, with \$640 profit). Beyond the 12th unit, every additional sale generates \$720 of **contribution margin**.

Note that $N_{be} = 12$ (revenue break-even on sales) is different from $N^* = 15$ (process break-even between manufacturing options). These quantities answer different questions: N_{be} tells you how many units you must sell to stop losing money; N^* tells you at which volume to switch from 3D-printing to injection moulding.

17.3.2 Gross Margin

Gross margin (GM%) measures the fraction of selling price that remains after covering unit cost:

$$GM(N) = \frac{p - C_{unit}(N)}{p} \times 100 \%$$

At $N = 50$:

$$GM(50) = \frac{1,200 - 640}{1,200} = \frac{560}{1,200} = 46.7 \%$$

At $N = 500$:

$$GM(500) = \frac{1,200 - 496}{1,200} = \frac{704}{1,200} = 58.7 \%$$

A gross margin of 46.7% at $N = 50$ is commercially viable for a hardware product in this category. The improvement to 58.7% at $N = 500$ confirms that the product becomes more attractive economically as volume grows — a key argument for the Gate 3 go-decision. Figure 17.2 shows both margins annotated on the unit-cost curve.

17.3.3 Total Profit

Total profit (or contribution profit) $\Pi(N)$ is the net gain after recovering both fixed and variable costs from N unit sales:

$$\Pi(N) = N(p - c_{var}) - C_{fixed}. \quad (17.3)$$

The term $N(p - c_{var})$ is total contribution from all sales; subtracting C_{fixed} gives net profit after fixed-cost recovery. Note that $\Pi(N_{be}) = 0$ by construction: the break-even volume is the zero-profit point.

At $N = 500$:

$$\Pi(500) = 500 \times (1,200 - 480) - 8,000 = 500 \times 720 - 8,000 = 360,000 - 8,000 = \$352,000 \text{ CAD}.$$

This figure — \$352,000 profit on a run of 500 units — is the economic justification for the investment in Project II. It answers the gate committee's implicit question: "If we fund the development work required to reach production, is the payoff worth it?"

17.3.4 Worked Example — Full Projection for the Sorter

The following calculation assembles all results in the order a Gate 3 reviewer would expect. All inputs are locked values established in Chapters 11 and 12.

Given:

$$C_{\text{fixed}} = \$8,000 \text{ CAD}, \quad C_{\text{var}} = \$480 \text{ CAD}, \quad p = \$1,200 \text{ CAD}, \quad C_{\text{BOM}} = \$124.85 \text{ CAD}.$$

Step 1 — Prototype cost per unit ($N = 1$):

$$C_{\text{proto}} = C_{\text{BOM}} + C_{\text{fixed}} = 124.85 + 8,000 = \$8,124.85 \text{ CAD}.$$

Step 2 — Unit cost at selected volumes (Equation 17.1):

$$C_{\text{unit}}(1) = \frac{8,000}{1} + 480 = 8,000 + 480 = \$8,480 \text{ CAD}.$$

$$C_{\text{unit}}(15) = \frac{8,000}{15} + 480 = 533.33 + 480 = \$1,013 \text{ CAD (rounded)}.$$

$$C_{\text{unit}}(50) = \frac{8,000}{50} + 480 = 160 + 480 = \$640 \text{ CAD}.$$

$$C_{\text{unit}}(500) = \frac{8,000}{500} + 480 = 16 + 480 = \$496 \text{ CAD}.$$

Step 3 — Revenue break-even (Equation 17.2):

$$N_{\text{be}} = \frac{8,000}{1,200 - 480} = \frac{8,000}{720} = 11.11 \rightarrow 12 \text{ units}.$$

Step 4 — Gross margin:

$$\text{GM}(50) = \frac{1,200 - 640}{1,200} = \frac{560}{1,200} = 46.7\%.$$

$$\text{GM}(500) = \frac{1,200 - 496}{1,200} = \frac{704}{1,200} = 58.7\%.$$

Step 5 — Total profit at $N = 500$ (Equation 17.3):

$$\Pi(500) = 500 \times (1,200 - 480) - 8,000 = 360,000 - 8,000 = \$352,000 \text{ CAD}.$$

These five steps constitute the complete financial projection expected in a Gate 3 submission. Table 17.1 collects the results.

17.4 Extrinsic Value and Gate 3 Readiness

A Gate 3 review evaluates two distinct questions: what the prototype *proved* about the design, and what *remains* unresolved before production can begin. A team that can answer both questions clearly — with quantitative evidence for the first and a prioritised list for the second — demonstrates the engineering judgment that distinguishes a credible Gate 3 submission from a demonstration of a working prototype.

Table 17.1: Cost projection summary for the IoT sorting subsystem ($C_{\text{fixed}} = \$8,000$, $c_{\text{var}} = \$480$, $p = \$1,200$ CAD).

Metric	Value	Equation
Prototype cost ($N = 1$)	\$8,124.85 CAD	—
$C_{\text{unit}}(1)$	\$8,480 CAD	17.1
$C_{\text{unit}}(15)$	\$1,013 CAD	17.1
$C_{\text{unit}}(50)$	\$640 CAD	17.1
$C_{\text{unit}}(500)$	\$496 CAD	17.1
Revenue break-even N_{be}	12 units	17.2
Gross margin at $N = 50$	46.7 %	—
Gross margin at $N = 500$	58.7 %	—
Total profit $\Pi(500)$	\$352,000 CAD	17.3

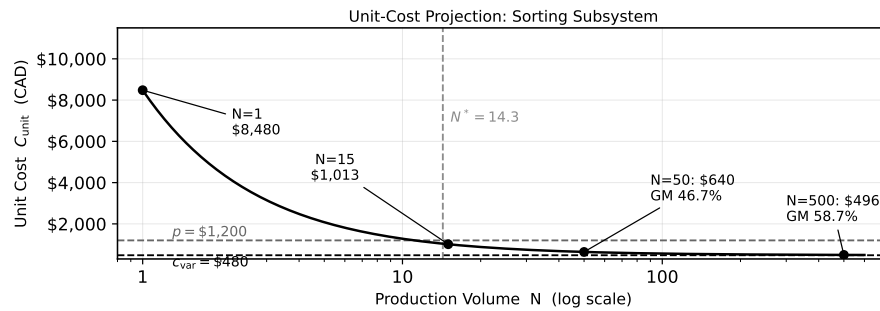


Figure 17.2: $C_{\text{unit}}(N)$ for the IoT sorting subsystem on a log N -axis. The curve falls from \$8,480 at $N = 1$ to \$496 at $N = 500$, asymptoting to $c_{\text{var}} = \$480$ (lower dashed line). The selling price $p = \$1,200$ is marked by the upper dashed line; the vertical dashed line at $N^* = 14.3$ is the process break-even from Chapter 12. Annotated arrows show gross margin at $N = 50$ (46.7%) and $N = 500$ (58.7%).

17.4.1 What the Prototype Proved

The sorting subsystem prototype addressed the five primary unknowns identified at Gate 1 (Chapter 4) and tracked through the Stage-Gate process.

1. **Sort accuracy and latency.** Acceptance testing (Chapter 14) demonstrated a mean sort latency of 99.06 ms against a specification of ≤ 100 ms, with a process capability index $C_p = 1.73$. The system meets specification with substantial margin.
2. **Battery life and power budget.** The validated power budget predicts a battery life of 50.5 days on the specified cell, exceeding the 30-day requirement by 68 %.
3. **Structural integrity.** The bracket safety factor is $SF = 5.29$, well above the $SF \geq 2$ requirement established in Chapter 4.
4. **AI inference end-to-end.** The on-device ML model runs inference end-to-end on the target microcontroller, meeting latency requirements without cloud connectivity.
5. **BOM cost and sourcing.** The costed BOM from Chapter 11 is \$124.85 CAD per prototype unit, with all components sourced from qualified distributors. All components are in active production with verified lead times.

17.4.2 What Remains for Project II

Six items are explicitly out of scope for Project I and constitute the primary risk items that Project II must resolve.

1. **Production-grade firmware.** The prototype firmware does not support over-the-air (OTA) updates. Field deployment at scale requires a validated OTA update mechanism; without it, firmware defects discovered post-deployment require a physical service call.
2. **Regulatory certification.** The prototype has not been submitted to FCC or ISED (Innovation, Science and Economic Development Canada) for wireless emissions testing. Certification is mandatory before commercial sale in Canada and the United States and represents a fixed cost of \$8,000–\$15,000 plus 12–20 weeks of test time.
3. **Injection-moulded housing.** The prototype housing is FDM-printed. The process break-even analysis from Chapter 12 identified $N^* = 14.3 \rightarrow 15$ units as the transition point; above 15 units, an injection-moulded housing is more cost-effective. The mould tool must be designed, cut, and validated before production begins.
4. **Supply-chain qualification.** Prototype components were purchased at retail from distributors. Production requires negotiated pricing, lead-time agreements, and approved vendor lists for all critical components.
5. **Cost reduction to below $N_{be} = 12$.** The current model assumes $c_{var} = \$480$ at volume. Achieving the projected margins requires that BOM negotiation and DFM/DFA improvements deliver this variable cost; the prototype does not validate production pricing.
6. **Customer pilot program.** No customer has operated the system in a field environment. A pilot with 3–5 units in customer hands is essential to validate the 30-day battery-life claim and to surface firmware edge cases that do not appear in laboratory testing.

17.4.3 Gate 3 Readiness Statement

The **Gate 3 readiness statement** is a two-to-three sentence executive summary that the gate committee reads before examining any supporting data. It must state what was proved (with quantitative evidence), what remains unresolved, and why proceeding is justified.

For the sorting subsystem:

The robotic sorting subsystem has demonstrated sort accuracy within specification (mean latency 99.06 ms, $C_p = 1.73$), battery life exceeding 50 days, and structural safety factor $SF = 5.29$. The design is ready for Project II, which will address production-scale firmware, regulatory certification, and supply-chain qualification.

17.5 Lessons Learned

An honest lessons-learned section is among the most valuable outputs of Project I. Gate committees distrust teams that claim everything went according to plan; they trust teams that can identify what went wrong, explain why, and articulate what they would do differently. The following observations reflect the specific experience of the sorting subsystem project.

What the team would do differently.

1. *Component lead time.* Two components on the BOM had 14-week lead times that were not identified until procurement began in Chapter 11. Future projects should run lead-time screening in parallel with component selection (Chapter 6), not after it.
2. *Firmware version control.* The first six weeks of firmware development used informal file naming (`main_v2_FINAL.c`, `main_v2_FINAL_fixed.c`) rather than the Git workflow formalised in Chapter 13. Three hours were lost reconstructing a working build that had been overwritten. Version control should be the first task on Day 1, not an afterthought at Gate 3.
3. *Structural analysis timing.* The bracket FEA (Chapter 9) was performed after the housing geometry was frozen. When the initial FEA flagged an under-thickness rib, the CAD model required revision, which propagated to the print file, the assembly drawing, and the test fixture. Structural analysis should be embedded in the design-review cadence, not deferred to a single milestone.

Assumptions that proved wrong.

1. The initial power budget assumed the microcontroller would spend 85 % of its time in deep sleep. Profiling revealed the actual sleep fraction was 71 % due to interrupt latency from the sensor polling loop. The revised budget still cleared the 30-day specification, but the assumption was wrong and the team was fortunate the margin was large.
2. The team estimated that AI model training would require one week. Data collection, labelling, augmentation, and validation took three weeks. Any project involving a trained ML model should budget at least twice the time estimated for the data pipeline.

One result that was better than expected. The sort accuracy specification (≤ 100 ms mean latency) was set conservatively based on an early literature survey. After implementation the measured mean was 99.06 ms with $C_p = 1.73$, far better than the team expected from a first-pass firmware implementation. The margin is large enough that Project II can allocate computational budget to OTA update handling without revisiting the latency specification.

17.6 The Handoff to Project II

Figure 17.3 presents the Gate 3 readiness assessment as a structured two-column view. The left column records what Project I delivers as validated artefacts. The right column records what Project II must resolve before production can begin. Neither column is a list of successes and failures: every item in the right column is a *scoped risk* with a known resolution path.

Gate 3 Readiness: What Was Proved vs. What Remains

Project I Delivers	Project II Must Resolve
Proven sort accuracy (≤ 100 ms latency)	Production-grade firmware (OTA update)
Validated power budget (50.5 days)	Regulatory certification (FCC/ISED)
SF ≥ 2 for bracket (SF=5.29)	Injection-moulded housing
AI inference working end-to-end	Supply-chain qualification
Costed BOM (\$124.85)	Cost reduction below $N_{be} = 12$
Version-controlled DHF	Customer pilot program

Figure 17.3: Gate 3 readiness matrix for the sorting subsystem. Left: deliverables that Project I provides as validated artefacts. Right: unresolved items that Project II must address before production. Every item in the right column has a known resolution path, cost estimate, and schedule implication.

The six Project I deliverables in the left column correspond directly to the Gate 3 acceptance criteria established in Chapter 4 and tested in Chapter 14. Every item is supported by a quantitative test result, a signed test report, and a version-controlled entry in the Design History File.

The six Project II items in the right column are not failures. They are engineering tasks that were deliberately deferred because completing them during Project I would have consumed schedule and budget without reducing the primary unknowns. A firmware OTA update mechanism is meaningless before the firmware itself is validated. An injection-mould tool is an unnecessary capital expenditure before the housing geometry is frozen by test data. The sequence — prototype, validate, then invest in production tooling — is the Stage-Gate model working as designed.

17.6.0.0.1 In Practice. “It works” does not mean “ready to produce.” The economic gap between a working prototype and a manufacturable product is often larger than the engineering gap. Regulatory certification, supply-chain qualification, and production-grade firmware can each consume as much time and money as the prototype development itself. A Gate 3 submission that acknowledges this gap with a specific list of Project II tasks is more credible, not less credible, than one that claims the product is production-ready. Gate committees have seen enough optimistic Gate 3 presentations to recognise the ones where the team has done the work to understand what they do not yet know.

17.6.0.0.2 Common Pitfalls. Two specific errors recur in Gate 3 submissions.

1. **“It works” is treated as equivalent to “ready to produce.”** A prototype that meets its functional specification is a validated design, not a production design. The gap between the two includes regulatory certification, supply-chain

qualification, production-grade firmware, manufacturability at volume, and field reliability under conditions that were not tested in the laboratory. Teams that present a working prototype and a unit-cost calculation without addressing these items have not completed a Gate 3 submission; they have completed a science-fair demonstration.

2. **A negative economic finding is treated as a failure.** If the break-even analysis shows $N_{be} = 12$ units but the total addressable market is only 8 units, that is not a failed project — it is a project whose scope must change. Options include: reducing C_{fixed} (a simpler test fixture, a less complex mould tool), reducing c_{var} (BOM renegotiation, assembly simplification), raising p (moving upmarket, adding features that justify a higher price), or exiting the market and licensing the technology. The Gate 3 recommendation in this case is not “proceed” or “kill” but “proceed with revised scope.” A team that presents this analysis honestly, with options evaluated, demonstrates exactly the economic judgment that a gate committee is looking for.

Try It Yourself

A student team has developed a motion-sensor module with the following cost parameters:

$$p = \$380 \text{ CAD}, \quad c_{var} = \$95 \text{ CAD}, \quad C_{fixed} = \$4,500 \text{ CAD}.$$

- (a) Using Equation 17.1, compute C_{unit} at $N = 25$, $N = 100$, and $N = 1,000$. Show every arithmetic step.
- (b) Using Equation 17.2, compute N_{be} . How many units must be sold to recover the fixed cost?
- (c) Compute GM% at $N = 100$ and $N = 1,000$.
- (d) Using Equation 17.3, compute $\Pi(200)$. Write a one-sentence Gate 3 readiness statement assuming all functional tests passed at specification.

Review Questions

- 1. **(Conceptual)** Explain why the unit cost of a single prototype is a misleading cost estimate for a production product. What two cost components does $C_{unit}(N)$ (Equation 17.1) correctly separate?
- 2. **(Conceptual)** A team’s economic analysis shows that break-even requires 200 units but the total addressable market is 150 units. Is this a failure? Explain what options remain and what the Gate 3 recommendation should be.
- 3. **(Applied, calculation)** A product: $p = \$520 \text{ CAD}$, $c_{var} = \$180 \text{ CAD}$, $C_{fixed} = \$6,200 \text{ CAD}$. Compute C_{unit} at $N = 20$, $N = 100$, and $N = 500$. Compute N_{be} . Compute GM% at $N = 100$. (Use Equations 17.1 and 17.2.)
- 4. **(Applied, calculation)** Using the values from Q3, compute $\Pi(300)$. Then compute $\Pi(50)$. Interpret both results. (Use Equation 17.3.)

5. **(Applied, multi-step)** A wearable device: $p = \$890$ CAD, $c_{\text{var}} = \$310$ CAD, $C_{\text{fixed}} = \$12,000$ CAD, $C_{\text{BOM}} = \$310$ CAD (1 unit). Compute:
- (a) Prototype cost per unit.
 - (b) C_{unit} at $N = 30$ using Equation 17.1.
 - (c) N_{be} using Equation 17.2.
 - (d) GM% at $N = 30$.
 - (e) $\Pi(100)$ using Equation 17.3.

Write a two-sentence Gate 3 readiness statement assuming functional tests passed.

Portfolio Entry

This is the final submission of your prototype documentation package and your Gate 3 presentation.

Documentation package. Submit the complete portfolio assembled in Chapter 16, updated with the following additions from this chapter:

- (a) *Cost projection* — a parameter table ($C_{\text{fixed}}, c_{\text{var}}, p, Y$) with sources, and a unit-cost table showing C_{unit} at $N = 50$, $N = 100$, and $N = 500$ with corresponding GM%.
- (b) *Gate 3 readiness statement* — two to three sentences stating what the prototype proved, what remains unresolved, and why proceeding to Project II is justified.
- (c) *Lessons learned* — one page: three things the team would do differently, two assumptions that proved wrong, and one result that was better than expected.

Final presentation. Deliver a 10–15 minute live presentation demonstrating your prototype against the Gate 3 acceptance criteria. The presentation must cover:

- (d) *Prototype demonstration* — live or recorded demonstration of the prototype meeting its primary specification.
- (e) *Test results summary* — key quantitative results from Chapter 14 with pass/fail decision against acceptance criteria.
- (f) *Production economics* — the cost projection and break-even analysis from this chapter.
- (g) *Gate 3 readiness statement* — delivered verbally, supported by the figure from §17.6.

The documentation package and presentation together constitute **Milestone 3** — the Gate 3 submission that closes Project I and opens the path to Project II.

Chapter Summary

This chapter completes the arc that began in Chapter 1 with a sorting problem and a blank Stage-Gate chart. Over sixteen chapters the project moved from an open question (“can a robotic subsystem sort objects reliably under battery power?”) through specifications, architecture, component selection, DFM review, BOM procurement, version control, AI integration, structural analysis, power budgeting, validation testing, intellectual property strategy, and documentation assembly. This final chapter added the economic dimension: the unit-cost curve, the revenue break-even at 12 units, gross margins of 46.7% and 58.7% at volumes of 50 and 500, and a total profit of \$352,000 at volume 500.

The equations that produced these numbers — Equations 17.1, 17.2, and 17.3 — are not complex. The discipline is not in the mathematics; it is in the honesty required to apply them. A team that uses prototype cost as a production cost estimate, that omits regulatory certification from the fixed-cost budget, or that treats a working prototype as a production-ready product has not completed the work this chapter requires.

A Gate 3 submission is not a finished product. It is a structured argument, supported by quantitative evidence, that the risk of proceeding to Project II is lower than the risk of stopping. The sorting subsystem prototype demonstrated sort accuracy within specification, battery life well above requirement, and structural margins that exceed the safety factor by a factor of 2.6. The economic model shows break-even at 12 units and a \$352,000 profit at volume 500. Six specific items have been identified for Project II, each with a known resolution path.

That is what a Gate 3 submission looks like. Not a claim that everything is solved — but evidence that enough is known to justify the next investment, and enough honesty to say exactly what is not yet known. The risk of proceeding is quantified. The risk of stopping — foregoing \$352,000 in potential profit and abandoning a technically validated design — is now the higher risk. That is the economic argument for opening Project II.

INDEX

- absolute maximum ratings, 68
- acceptance criterion, 42
- AI hallucination, 93
- AI inference, 206
- AI use log, 98
- AI-assisted design, 91
- AI/IoT/robotic logic subsystem, 54
- allocation period, 74
- alternate part
 - missing, 138
- AND gate
 - fault tree, 175
- application circuit, 69
- artifact
 - Kano analysis table, 25
- as-built BOM, 134, 195
- assembly efficiency, 83
- attack surface, 104
- authenticated broker, 107
- authentication, 104
- average current, 108

- B2B, 7
- B2C, 7
- battery life, 108
- Bessel's correction, 172
- bill of materials, 129
 - multi-level, 130
- biometric data, 106
- BLE, 107
- BOM
 - as afterthought, 138
- BOM cost, 206
- BOM total, 136
- Boothroyd–Dewhurst criterion, 83
- branching strategy, 154
- bridge production, 141
- budget allocation, 58
- build-to-order, 7
- built-in self-test, 85
- business case, 16

- business model, 6

- CAD version control, 158
- change control, 177
- change management, 161
- cherry-picking
 - test results, 177
- CoAP, 107
- commit discipline, 153
- commodity high-volume, 7
- communication layer, 105
- component selection table, 67, 78
- confidentiality agreement, 185
- confirmation bias, 170
- connectivity layer, 105
- consequence, 44
- constraint, 42
- contractor IP, 186
- contribution margin, 204
- controllability, 84
- copyright, 183
 - work made for hire, 184
- cost, 6
- cost reduction, 207
- cost-committed curve, 147
- counterfeit components, 134
- C_p , 172
- critical path, 120
- Critical Path Method, 118
- critical path of unknowns, 46
- customer pilot, 207

- data interface, 57
- data leakage, 97
- datasheet, 67
- datasheet literacy, 79
- decomposition, 53
- derating, 69
- derating factor, 70
- design acceleration, 93
- design BOM, 195

- design for assembly, 83
- design for manufacturability, 82
- design for reliability, 85
- design for test, 84
- design for X, 81
- design history
 - as evidence, 152
 - iteration records, 177
- Design History File, 159
- design-locks-cost principle, 146
- detection, 45
- deviation record, 195
- DFA assembly efficiency, 146
- DHF, 159
 - index, 159
 - repository integration, 164
 - required contents, 159
- discrepancy report, 177
- documentation
 - record decisions, 193
 - reproducibility, 194
- documentation debt, 194
- documentation layer, 36
- DPMO, 85
- duty cycle, 107

- early finish, 118
- early start, 118
- ECO, 161
 - contents, 162
 - informal vs. formal, 161
- EDA version control, 157
- effective variable cost, 147
- effort
 - relative, 34
- electrical characteristics, 69
- electrical interface, 42, 56
- electromagnetic compatibility, 113
- electronics subsystem, 54
- electrostatic discharge, 113
- emergency stop, 110
- employment agreement, 184
 - IP clause, 184
- encryption, 104
- engineer, 4
- engineer accountability, 93
- engineering change order, 161
- expected cost of error, 95
- extended cost, 136
- extrinsic value, 28

- fail-safe state, 111

- Failure Mode and Effects Analysis, 45
- failure rate, 74
- fault tree
 - basic event, 175
 - event boxes, 175
 - gates, 175
 - top event, 175
- fault tree analysis (FTA), 174
- fidelity, 34
- firm size, 5
- firmware subsystem, 54
- FIT, 74
- fixed cost, 142, 201
- FMEA, 45
- footprint compatibility, 73
- force limit, 111
- FTA, 174
- functional requirement, 41
- Fusion 360
 - version history, 158, 164

- Gantt chart, 120
- gate decision, 14
 - go, 15
 - hold, 15
 - kill, 15
 - recycle, 15
- Gate 3 readiness statement, 207
- git
 - branching, 154
 - checkout historical state, 156
 - firmware workflow, 153
 - release tags, 154
- Git Large File Storage, 158
- git-lfs, 158
- GitHub, 162
- GitLab, 162
- go/no-go, 32
- gross margin, 204
- guarding, 110

- hardware-as-a-service, 7
- human-in-the-loop verification, 93
- human-robot interaction zone, 111

- injection moulding, 207
- integration, 31
- integration failure, 61
- intellectual property, 181
 - relevance to technicians, 181
- interface, 56
- interface contract, 53, 56
- interface specification, 42

- ul style="list-style-type: none;">
- interface table, 58
- intrinsic value, 28
- IP assignment
 - contract work, 186
- IP assignment clause, 186
- IP ownership
 - employment, 184
- it works fallacy, 209
- iteration
 - controlled, 32
 - uncontrolled, 32
- iteration decision
 - documented, 177
 - scope, 177
- Kano analysis, 17
 - delighter feature, 18
 - dissatisfaction coefficient, 19
 - indifferent feature, 18
 - performance feature, 18
 - quadrant interpretation, 19
 - reverse feature, 18
 - satisfaction coefficient, 19
 - threshold feature, 17
- Kano, Noriaki, 17
- KiCad
 - git integration, 157
 - version control, 163
- lab track, 2
- large enterprise, 5
- late finish, 119
- late start, 119
- LE Secure Connections, 107
- lead time, 74, 123
- legal counsel, 187
- licensing, 7
- lifecycle status, 71, 73
 - active, 72
 - last-time buy, 72
 - NRND, 72
 - obsolete, 72
- living document, 121
- location data, 106
- low-volume production, 141
- LSL, 171
- management layer, 105
- margin
 - to specification limit, 172
- mean
 - sample, 171
- measurement
 - variation, 171
- mechanical fit mismatch, 63
- mechanical interface, 42, 56
- mechanical subsystem, 54
- milestone, 3
- Milestone 3, 211
- most likely duration, 121
- MQTT, 106
- NDA, 185
- non-conformance report, 177
- non-disclosure agreement, 185
- NRND, 72
- observability, 84
- occurrence, 45
- operating margin, 71
- optimistic duration, 121
- OR gate
 - fault tree, 175
- order quantity
 - overage, 131
- packaging, 69
- parametric equivalence, 73
- patent, 182
 - non-obviousness, 183
 - novelty, 182
 - utility, 182, 183
- patent attorney, 187
- patent classification, 187
- per-device credentials, 107
- performance target, 42
- personal data, 106
- personal protective equipment, 113
- PERT
 - expected duration, 121
 - standard deviation, 121
- pessimistic duration, 121
- pitfall
 - over-fidelity, 36
 - prototype as mini-product, 36
- portfolio
 - Chapter 14, 179
- power budget, 59, 206
- preliminary cost analysis, 149
- prior art, 186
- prior-art search, 186
- probability of failure, 44
- process break-even, 144, 203
- process capability, 172
- procurement risks, 123
- product, 3

- product development lifecycle, 13
- product sale, 6
- production firmware, 207
- production unit cost, 202
- production volume, 6
- Program Evaluation and Review Techniques
 - 121
- project context brief, 10
- project duration, 119
- proof-of-concept, 1
- proprietary design data, 97
- protocol mismatch, 62
- prototype, 3
 - definition, 28
 - functional, 33
 - looks-like/works-like, 33
 - pre-production, 33
 - proof-of-concept, 33
- prototype cost, 202
- Prototype Development Cycle, 27
- prototype plan, 30
- prototype scope, 20
 - derived from Kano, 24
- provisional patent application, 183
- purchase list, 131
- purchase order, 132
- recommended operating conditions, 68
- redundancy, 85
- reference designator, 130
 - missing, 138
- regulatory certification, 207
- release tag, 154
- reliability, 74
- reproducibility, 99
- request for quotation, 132
- requirements vs. design, 43
- revenue break-even, 203
- revenue model, 6
- risk
 - in prototyping, 28
 - list, 29
- risk register, 123
- risk-driven prioritization, 44
- root-sum-of-squares error, 59
- rule of ten, 147
- running example, 8
- safety factor, 111
- schedule risk, 123
- schedule risks, 123
- scope of employment, 185
- second source, 73
- secure firmware update, 104
- security by design, 103
- selective prototyping, 20
- seven-stage workflow, 2
- severity, 45
- single-source component, 74
- single-source risk, 131
- slack, 119
- SME, 5
- software interface, 42
- sort accuracy, 206
- specialty low-volume, 7
- specification, 29, 41
 - lower specification limit, 171
 - upper specification limit, 171
- speed limit, 111
- Stage-Gate model, 14
 - Build Business Case, 15
 - course position, 16
 - Development, 15
 - Discovery, 15
 - Scoping, 15
 - Testing and Validation, 15
- standard deviation
 - sample, 171
- start-up, 5
- STEP export, 158
- structural integrity, 206
- subsystem, 30
- supply chain risk, 73
- supply-chain qualification, 207
- system block diagram, 55
- test for requirements, 43
- test point, 84
- test procedure, 170
 - repeatability, 170
 - written in advance, 169
- theory track, 2
- three-way match, 134
- time, 6
- timing assumption mismatch, 62
- timing budget, 58
- timing diagram, 69
- timing interface, 57
- tooling
 - version control, 162
- total profit, 204
- traceability
 - acceptance criteria, 171
- traceability coverage, 197

- traceability matrix, 171, 196
- trade secret, 183
- trademark, 184
- Try It Yourself
 - Chapter 14, 178
- UART debug port, 84
- unit cost, 142
- unit economics, 32
- USL, 171
- validation, 31
- variable cost, 142, 201
- verification decision rule, 95
- version control
 - design files, 157
 - hardware rationale, 151
 - scope, 152
- voltage level mismatch, 62
- what/how discipline, 43
- Work Breakdown Structure, 117
- work made for hire, 184
- work package, 117
- worked example
 - fault tree, 175
 - IP audit, 188
 - Kano, 21
 - latency test, 172
- yield, 147
- z-score, 172
